

कार्यपालक अभियन्ता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, सहरसा

पत्रांक 1778315/

सहरसा, दिनांक 14-11-2023/

प्रेषक:-

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, सहरसा।

सेवा में,

नोडल पदाधिकारी,
3054 (M.R) कोषांग,
बिहार, पटना।

विषय:- शीर्ष 3054 नई अनुरक्षण नीति-2018 अंतर्गत Initial Rectification and Surface renewal. कराये गये कार्य हेतु अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक कहना है कि विहित प्रपत्र में संलग्न विवरणी के अनुसार शीर्ष Mr 3054 New Maintenance Policy-2018. अन्तर्गत Bakhri Mahendra Sahu House To Uttar Rami Mehta House Middle School Bakhri Lakshmi Mehta House पथ का Initial Rectification and Surface renewal. कराये गये कार्य हेतु राशि Rs.88.95174/- (रूपये अठासी लाख पनचानवें हजार एक सौ चौहतर) मात्र राशि की आवश्यकता है।

अतः कार्यहित में अनुरोध है कि उक्त अधियाचित राशि Rs.88.95174/- (रूपये अठासी लाख पनचानवें हजार एक सौ चौहतर) उपलब्ध कराने की कृपा की जाय ताकि कराये जा रहे कार्यो का विपत्र भुगतान किया जा सके।

- अनु०:- (1) अधियाचना प्रपत्र
(2) IRI Value Report
(3) Map
(4) प्रमाण-पत्र।

14/11/23

विश्वासभाजन

14-11-2023

कार्यपालक अभियन्ता
ग्रा०का०वि०, कार्य प्रमण्डल,
सहरसा

Name of Division:- RWD Works Division Saharsa

Rural Works Department
MR NEW MAINTENANCE POLICY-2018, ALLOTMENT REQUISITION

Sl. No	Year	Name of Road	Name of Contractor (In English)	Project Id	Administrative Sanction		Agreement Amount (In Lacs)		Value of Bt (in million)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Allotment Received (in Lacs)	Total Expenditure as per MIS (in Lacs)	Value of Measurement (in Lacs)	Current Demand (in Lacs)	Remarks
					Length (In Km)	Amount (In Lacs)	Main Work	Maintenance								
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17
60	2022-23	Dakini Mahendra Sahu House To Utiar Rami Menha House Middle School Dakini Lakshmi Menha House	Arvind Kumar	20904313028	2.250	124.33800	88.95174	28.42520	2778	25	5%	0.00000	0.00000	88.95174	88.95174	Complete

74/11/23
D.A.O
RWD Works Division
Saharsa

Executive Engineer
RWD Works Division
Saharsa

74/11/23
11-20

**OFFICE OF THE EXECUTIVE ENGINEER
RWD WORKS DIVISION SAHARSA.**


**Name of Scheme:- Bakhri Mahendra Sahu House To Uttar Rami Mehta House Middle School
Bakhri Lakshmi Mehta House, PACKAGE No- RM/SA/SAH/22/0008, Project ID- 20904313028.**

**Certified that all item wise 100%
Measurement has been taken by me**


14/11/2023

Junior Engineer
RWD Work section Saurbazar
Works Division Saharsa

**Certified that all item wise 50%
Measurement has been cheked by me**


17/11/23

Assistant Engineer
RWD Work Section Saurbazar
Works Division Saharsa

**Certified that all item wise 10%
Measurement has been cheked by me**


14-11-2023

Executive Engineer
Rural work Department
Works Division Saharsa

Name of Road -

Name of Contractor Atvind Kumar

Batch Name -IRM/SV/SAH/22/0008

Date	Time	Section		Length	Bumps		Speed	OR	IRI	CATEGOR Y	Latitude	Longitude	Event
		No.	In km		In mm	Rate							
14-11-2023	02:54:13	92	0.100	180	10.1	2000	2478	G	25.832278	ROAD		86.641117	Normal
14-11-2023	02:54:34	92	0.100	180	10.1	2000	2478	G	25.832198			86.640313	Normal
14-11-2023	02:55:00	92	0.100	270	10.1	2700	3167	G	25.831873			86.639639	Normal
14-11-2023	02:55:14	92	0.100	180	10.1	2000	2478	G	25.831807			86.639549	Normal
14-11-2023	02:55:25	92	0.100	200	10.1	2000	2478	G	25.831799			86.639519	Normal
14-11-2023	02:56:00	92	0.100	180	10.1	2000	2478	G	25.831586			86.639200	Normal
14-11-2023	02:56:34	92	0.100	270	10.1	2700	3167	G	25.831534			86.638694	Normal
14-11-2023	02:57:09	92	0.100	180	10.1	2000	2478	G	25.831570			86.637416	Normal
14-11-2023	02:57:21	92	0.100	270	10.1	2700	3167	G	25.831190			86.635930	Normal
14-11-2023	02:58:02	92	0.100	180	10.1	2000	2478	G	25.830197			86.635022	Normal
14-11-2023	02:58:37	92	0.100	270	10.1	2700	3167	G	25.829465			86.634960	Normal
14-11-2023	02:59:08	92	0.100	200	10.1	2000	2478	G	25.828479			86.635151	Normal
14-11-2023	02:59:45	92	0.100	180	10.1	2000	2478	G	25.827821			86.635347	Normal
14-11-2023	03:00:04	92	0.100	180	10.1	2000	2478	G	25.827614			86.635361	Normal
14-11-2023	03:00:29	92	0.100	270	10.1	2700	3167	G	25.825450			86.635222	Normal
14-11-2023	03:01:07	92	0.100	180	10.1	2000	2478	G	25.825359			86.635306	Normal
14-11-2023	03:01:48	92	0.100	270	10.1	2700	3167	G	25.824880			86.635329	Normal
14-11-2023	03:01:57	92	0.100	180	10.1	2000	2478	G	25.824588			86.635480	Normal
14-11-2023	03:02:15	92	0.100	200	10.1	2000	2478	G	25.822084			86.634781	Normal
14-11-2023	03:02:38	92	0.100	180	10.1	2000	2478	G	25.821924			86.634595	Normal
14-11-2023	03:02:51	92	0.100	270	10.1	2700	3167	G	25.821611			86.634272	Normal
14-11-2023	03:03:05	92	0.100	180	10.1	2000	2478	G	25.820152			86.633870	Normal
14-11-2023	03:03:25	92	0.050	270	10.1	2700	3167	G	25.820253			86.634171	Normal
						Total	62506.0		2778.04	Average			

$$Y = 0 \cdot X^2 + 0.924 \cdot X + 510.7$$

$$X =$$

$$Y = 2577$$

(R) RURAL ROAD

Good Average Poor

<4000 4001-5000 >5001

14/11/23

14/11/23

14-11-2023

Name of Customer :	Arvind Kumar
Name of Work/ Road :	Bakhni Mahendra Sahu House
Lab Job number	
Date :	11/14/2023
Section No.	92


Test Date :	11/14/2023	Road Name :	Bakhni Lakshmi Mehta House
Machine No :	403	Road Type :	(A) ASPHALTIC
Start S No :		Side :	
Start E No :		Interval	
Weather :		UIV Range :	1478 To 4000 1000 mm/km
Start Location :		Dist Range :	0 To 2.4 0.1 * 1000 m
End Location :		Equation :	test

Print

Generate Report and Graph

Redraw Graph

Map View

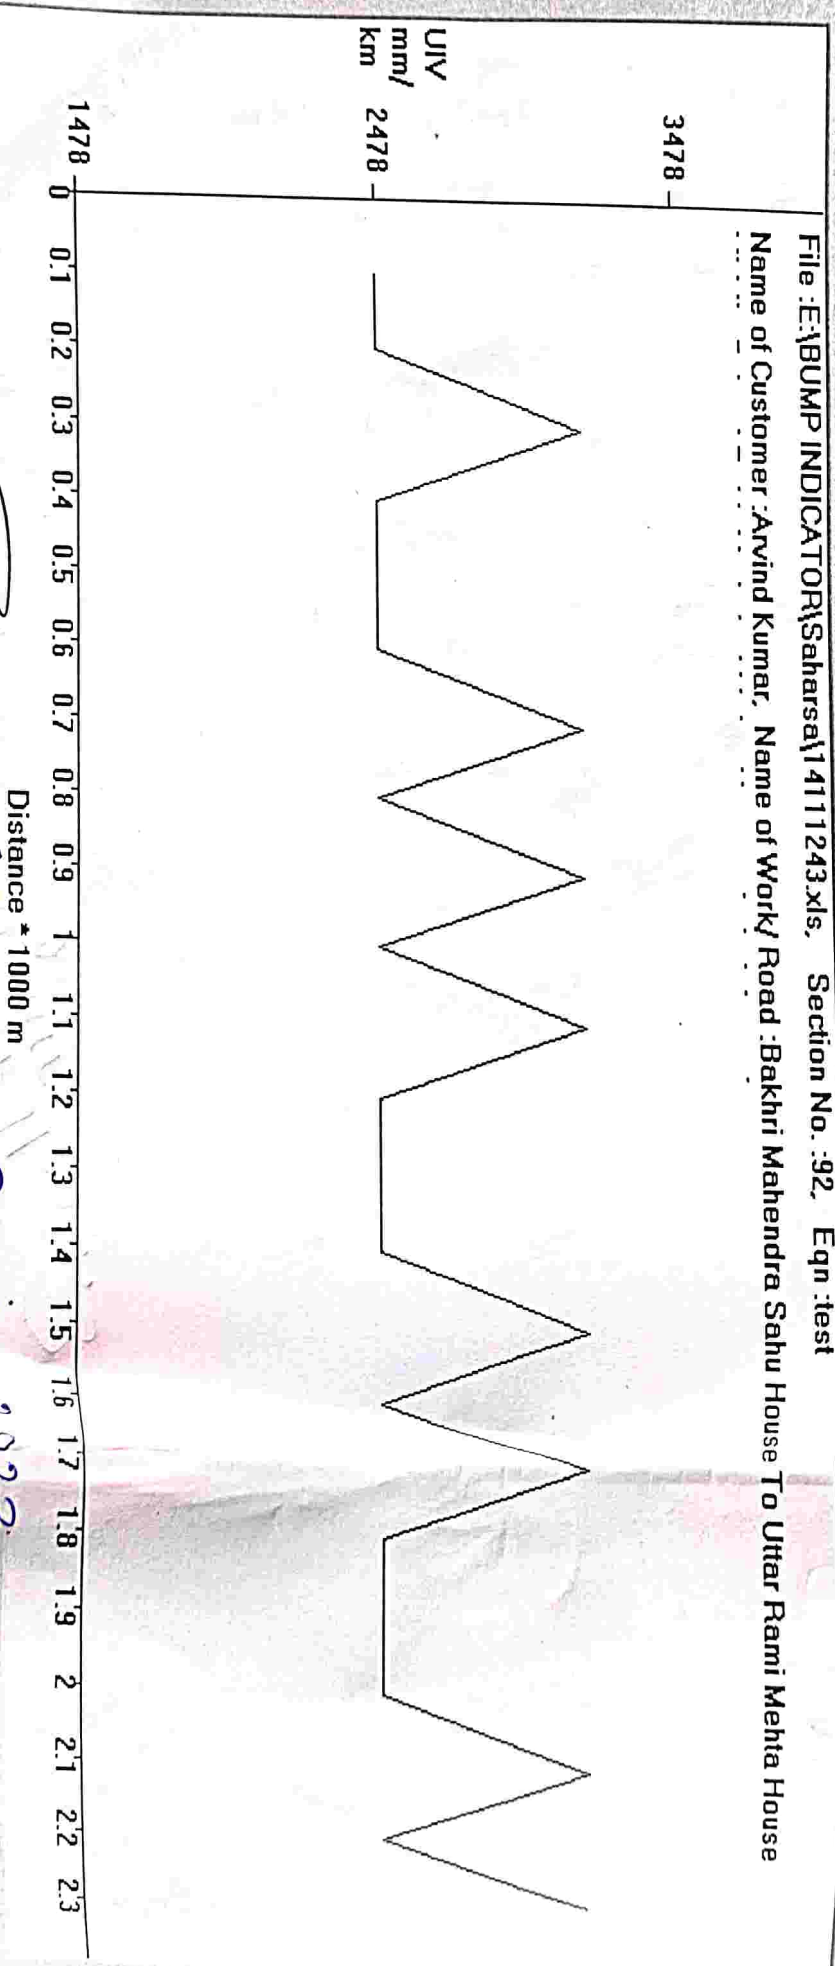

Arvind Kumar
14/11/2023

14/11/23

14-11-2023
