

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 2362 (अनु०)

/नरकटियागंज, दिनांक 7/12/2024

प्रेषक,

ई० मनीष कुमार,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुस्क्षण नीति-2018” (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुस्क्षण नीति-2018” योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुस्क्षण
नीति-2018” योजनान्तर्गत पथ:-

1. REO ROAD INARWA – BASANTPUR
2. L038-T04 Podmole to Basantpur (VR38)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र
में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



ई० मनीष कुमार
कार्यपालक अभियन्ता,
ग्रा०का०वि०, का०प्र०, नरकटियागंज

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Alloted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/24/0003	REO ROAD INARWA - BASANTPUR	31808902087	6115 04.12.2023	1.300	61.48400	36.52100	10.54745	06/24-25 23.08.2024	22.05.2025		2926	SDBC-25mm	5%	0.00000	0.00000	28.83264	Surface complete
2	RM/WE/NAR/24/0003	L038-T04 Podmole to Basantpur (VR38)	N318089002104	6115 04.12.2023	1.774	77.97000	44.93189	14.50715	06/24-25 23.08.2024	22.05.2025		2890	SDBC-25mm	5%	0.00000	0.00000	42.99089	Surface complete

Suman
05/12/24
TS

Suman
5/12/24
AE


Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- L038-T04 Podmole to Basantpur (VR38)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- RAJESH KUMAR


Length of Road :- 1.774 KM

Project ID :- N318089002104


Package No. :- RM/WE/NAR/24/0003

Name of Block :- Mainatanr

Certified that all item wise 100% measurement has been taken by me


JE 05/12/2024 TS

Certified that all item wise 50% measurement has been verified by me


AE 5/12/24

Certified that all item wise 10% measurement has been verified by me


EE

Name of Road - L038-T04 Podmole to Basantpur (VR38) (Sec-10)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
5/ 12/ 24	12: 58: 9	10	0.1	300	23.4	3000	2982	G	27.13108	84.58047	Normal
5/ 12/ 24	12: 59: 6	10	0.1	270	26.4	2700	2715	G	27.13190	84.58083	Normal
5/ 12/ 24	12: 59: 16	10	0.1	300	28.3	3000	3001	G	27.13240	84.58165	Normal
5/ 12/ 24	12: 59: 41	10	0.1	270	26.6	2700	2708	G	27.13275	84.58257	Normal
5/ 12/ 24	13: 0: 7	10	0.1	310	26.8	3100	3080	G	27.13356	84.58297	Normal
5/ 12/ 24	13: 0: 17	10	0.1	280	26.3	2800	2813	G	27.13400	84.58381	Normal
5/ 12/ 24	13: 0: 47	10	0.1	270	26.3	2700	2679	G	27.13459	84.58455	Normal
5/ 12/ 24	13: 1: 0	10	0.1	270	33.5	2700	2666	G	27.13524	84.58525	Normal
5/ 12/ 24	13: 1: 11	10	0.1	280	33.5	2800	2775	G	27.13584	84.58599	Normal
5/ 12/ 24	13: 1: 27	10	0.1	300	24.6	3000	3024	G	27.13660	84.58660	Normal
5/ 12/ 24	13: 1: 37	10	0.1	270	33.5	2700	2746	G	27.13726	84.58724	Normal
5/ 12/ 24	13: 1: 57	10	0.1	310	33.5	3100	3141	G	27.13781	84.58801	Normal
5/ 12/ 24	13: 2: 11	10	0.1	320	26.7	3200	3151	G	27.13832	84.58886	Normal
5/ 12/ 24	13: 2: 32	10	0.1	250	26.7	2500	2527	G	27.13882	84.58972	Normal
5/ 12/ 24	13: 2: 57	10	0.1	320	26.7	3200	3169	G	27.13944	84.59047	Normal
5/ 12/ 24	13: 2: 57	10	0.1	290	26.7	2900	2895	G	27.14017	84.59106	Normal
5/ 12/ 24	13: 3: 9	10	0.1	300	26.7	3000	2998	G	27.14096	84.59152	Normal
5/ 12/ 24	13: 3: 26	10	0.074	300	33.5	3000	2955	G	27.14154	84.59193	Normal
Average IRI Value=							2890				

Suman
05/12/24
TS

Suman
5/12/24
AE

[Signature]
Executive Engineer
Rural Works Department
Works Division Narkatiaganj

Name of Customer : Rajesh Kumar
Name of Work/ Road : L038-T04 Podmole to Basantpur
Lab Job number :
Date : 5/12/2024
Section No. : 10

Date	5/12/2024	Section	L038-T04 Podmole to Basantpur
Station	472	Road Type	(R) RURAL ROAD
Start E. No.		Side	
Start E. No.		Interval	
Weather		UV Range	1527 To 4000 1000 mm/km
Start Location	0.000	Dist Range	0 To 1.9 0.1 * 1000 m
End Location	1.774	Equation	$Y = 0 * X^2 + 0.829 * X + 458.6$

Print

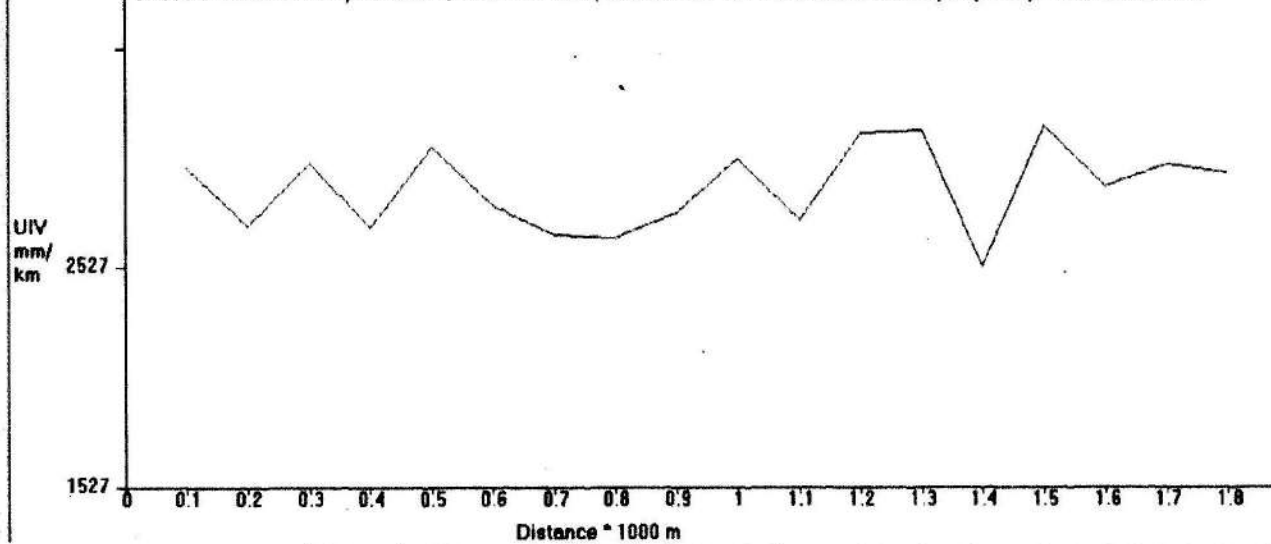
Generate Report and Graph

Redraw Graph

Map View

File : G:\245012782.Xls. Section No. : 10. Eqn : $Y = 0 * X^2 + 0.829 * X + 458.6$

Name of Customer : Rajesh Kumar, Name of Work/ Road : L038-T04 Podmole to Basantpur (VR38), Lab Job number



Suman
05/12/2024
TS

Suman
5/12/24
AE

Executive Engineer
Rural Works Department
Works Division Narkatiaganj
