

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 2394 (अनु.)

/नरकटियागंज, दिनांक. 16/12/2024

प्रेषक,

ई0 मनीष कुमार,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति-2018" (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) "नई अनुरक्षण नीति-2018" योजनान्तर्गत पथ के निर्माण में
संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) "नई अनुरक्षण
नीति-2018" योजनान्तर्गत पथ:-

1. T03 to Senuria via Sindhwalia (VR47)
2. T03 to Purbi (VR46)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र
में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0:-यथोक्त।

विश्वासभाजन

16/12/24

ई0 मनीष कुमार

कार्यपालक अभियन्ता,


ग्रा0का0वि0. का0प्र0. नरकटियागंज

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatlaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/Km)	Thickness of Bitumen Layer In mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (In Lakh)	Up-to-date Expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
				Length (In Km)	Amount (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)										
RM/WENAR/2 4/0005	T03 to Senuria via Sindhwalia (VR47)	31808902169	6115 04.12.2023	1.770	97.96000	73.80932	16.96830	02/24-25 03.09.2024	02.06.2025		2969	SDBC-25mm	5%	0.00000	0.00000	73.56352	Surface complete
RM/WENAR/2 4/0005	T03 to Purbli (VR46)	31808902168	6115 04.12.2023	0.940	49.70600	36.53680	9.41445	02/24-25 03.09.2024	02.06.2025		3034	SDBC-25mm	5%	0.00000	0.00000	36.46770	Surface complete

1 day 12/12/24


 Executive Engineer
 Rural Works Department
 Work(s) Division Narkatlaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- T03 to Purbi (VR46)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- Khurshid Alam

Length of Road :- 0.940 KM

Project ID :- 31808902168

Package No. :- RM/WE/NAR/24/0005

Name of Block :- Sikta

Certified that all item wise 100% measurement has been taken by me


JE

Certified that all item wise 50% measurement has been verified by me


AE

Certified that all item wise 10% measurement has been verified by me


EE

Name of Road - T03 to Purbi (VR46) (Sec-12)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
6/12/24	12:39:5	12	0.1	300	23.3	3000	2952	G	26.996936	84.759182	Normal
6/12/24	12:40:13	12	0.1	290	23.4	2900	2894	G	26.997347	84.758313	Normal
6/12/24	12:40:48	12	0.1	300	23.4	3000	2968	G	26.997519	84.757358	Normal
6/12/24	12:41:0	12	0.1	340	33.5	3400	3368	G	26.997854	84.756425	Normal
6/12/24	12:41:0	12	0.1	300	23.4	3000	3033	G	26.998131	84.755470	Normal
6/12/24	12:41:23	12	0.1	300	23.4	3000	3021	G	26.998427	84.754515	Normal
6/12/24	12:41:23	12	0.1	290	23.4	2900	2929	G	26.998733	84.753539	Normal
6/12/24	12:42:0	12	0.1	300	13.3	3000	3008	G	26.998991	84.752595	Normal
6/12/24	12:42:0	12	0.1	310	23.4	3100	3138	G	26.998991	84.751586	Normal
6/12/24	12:42:34	12	0.04	300	23.4	3000	3033	G	26.998972	84.751189	Normal
Average IRI Value=							3034				

6/12/2024
J.C.

Pat
06/12/24

M 16/12/24


Name of Customer : Khurshid Alam
 Name of Work/ Road : T03 to Purbi (VR46)
 Lab Job number :
 Date : 6/12/2024
 Section No : 12

Test Date : 6/12/2024 Road Name : T03 to Purbi (VR46)
 Machine No : 472 Road Type : (R) RURAL ROAD
 Start S No : Side : Interval
 Start E No :
 Weather : UIV Range : 1074 To 4000 1000 mm/km
 Start Location : 0.000 Dist Range : 0 To 1.01 * 1000 m
 End Location : 0.940 Equation : $Y = 0 * X^2 + 0.829 * X + 458.6$

Print Generate Report and Graph

Redraw Graph

Map View

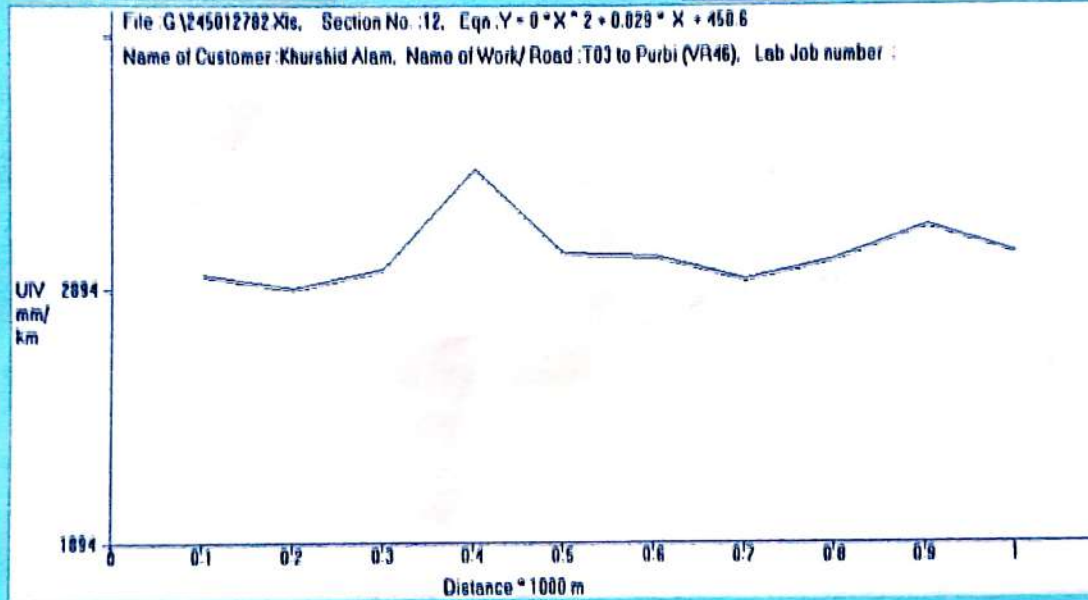

Man
6/12/2024
J.C.

Pratik
06/12/24
