

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 2431 (अनु०)

/नरकटियागंज, दिनांक 21/12/2024

प्रेषक,

ई० मनीष कुमार,
कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
“नई अनुरक्षण नीति-2018” (3054-MR),
ग्रामीण कार्य विभाग, बिहार पटना।

विषय :- शीर्ष MR(3054) “नई अनुरक्षण नीति-2018” योजनान्तर्गत पथ के निर्माण में
संवैदक के विपत्र भुगतान हेतु राशि की अधियाचना के सम्बन्ध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) “नई अनुरक्षण
नीति-2018” योजनान्तर्गत पथ:-

1. PWD Road – Bargo
2. Pipra Chauk to Langra (VR70)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र
में भर कर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन

21/12/24


ई० मनीष कुमार

कार्यपालक अभियन्ता,
ग्रा०का०वि०, का०प्र०, नरकटियागंज

Office Of The Executive Engineer
Rural Works Department, Works Division, Narkatiaganj

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2020 (Initial Rectification and Surface Renewal)

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval(AA) Letter No. & Date	Administrative		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer in mm	Value of Bitumen content in Percentage	Previous Total Allotted Amount (in Lakh)	Up-to-date Expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (in Km)	Amount (in Lakh)	Initial Rectification with Surface Renewal (in Lakh)	5 Year Routine Maintenance (in Lakh)										
1	RM/WE/NAR/24/0004	PWD Road - Bargo	31808802109	<u>6115</u> 04.12.2023	1.820	103.52000	80.07338	16.23500	<u>162425</u> 23.10.2024	22.07.2024		3153	SDBC-25mm	5%	0.00000	0.00000	80.05047	Surface complete
2	RM/WE/NAR/24/0004	Pipra Chauk to Langra (VR70)	31808902213	<u>6115</u> 04.12.2023	1.870	117.78000	91.10020	18.05500	<u>162425</u> 23.10.2024	22.07.2024		3234	SDBC-25mm	105%	0.00000	0.00000	91.01924	Surface complete


Executive Engineer
Rural Works Department
Work(s) Division Narkatiaganj

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- Pipra Chauk to Langra (VR70)

Name of Scheme :- MR 3054 New Maintenance Policy 2018

Name of Contractor :- YOGENDRA SAH

Length of Road :- 1.870 KM

Project ID :- 31808902213

Package No. :- RM/WE/NAR/24/0004

Name of Block :- Narkatiaganj

Certified that all item wise 100% measurement has been taken by me

R. S. S.
20/12/24

JE

Certified that all item wise 50% measurement has been verified by me

m. s. s.
20/12/24

AE

Certified that all item wise 10% measurement has been verified by me

Q. S. S.
21/12/24


EE

Name of Road - Pipra Chauk to Langra (VR70) (Sec-14)

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD			
20/12/24	11:39:5	14	0.1	310	27.7	3100	3145	G	27.137363	84.417674	Normal
20/12/24	11:40:13	14	0.1	320	27.7	3200	3248	G	27.138163	84.418144	Normal
20/12/24	11:40:48	14	0.1	320	34.5	3200	3205	G	27.139054	84.418186	Normal
20/12/24	11:41:0	14	0.1	340	27.7	3400	3420	G	27.139955	84.418190	Normal
20/12/24	11:41:0	14	0.1	310	34.5	3100	3096	G	27.140836	84.418338	Normal
20/12/24	11:41:23	14	0.1	310	24.5	3100	3107	G	27.141724	84.418402	Normal
20/12/24	11:41:23	14	0.1	300	25.5	3000	3003	G	27.142207	84.417553	Normal
20/12/24	11:42:0	14	0.1	280	25.5	2800	2807	G	27.142413	84.416570	Normal
20/12/24	11:42:0	14	0.1	310	25.5	3100	3107	G	27.142565	84.415576	Normal
20/12/24	11:42:34	14	0.1	310	25.5	3100	3137	G	27.142723	84.414552	Normal
20/12/24	11:43:0	14	0.1	310	25.5	3100	3116	G	27.142966	84.413490	Normal
20/12/24	11:43:9	14	0.1	330	25.5	3300	3298	G	27.143452	84.412762	Normal
20/12/24	11:44:0	14	0.1	350	25.5	3500	3503	G	27.144121	84.412174	Normal
20/12/24	11:44:0	14	0.1	350	25.5	3500	3489	G	27.144576	84.411283	Normal
20/12/24	11:44:19	14	0.1	320	25.5	3200	3238	G	27.145390	84.411036	Normal
20/12/24	11:44:54	14	0.1	350	25.5	3500	3545	G	27.146173	84.410391	Normal
20/12/24	11:45:0	14	0.1	320	26.7	3200	3217	G	27.146787	84.409701	Normal
20/12/24	11:45:29	14	0.1	330	26.7	3300	3319	G	27.147557	84.409170	Normal
20/12/24	11:45:29	14	0.07	340	26.7	3400	3443	G	27.147712	84.409063	Normal
Average IRI Value=							3234				

R.D. 20/12/24
J.E.

20/12/24
A.E.


 Executive Engineer
 Rural Works Department
 Works Division Narkatiaganj

Name of Customer : YOGENDRA SAH
Name of Work/ Road : Pipra Chauk to Langra (VR70)
Lab Job number :
Date : 20/12/2024
Section No. : 14

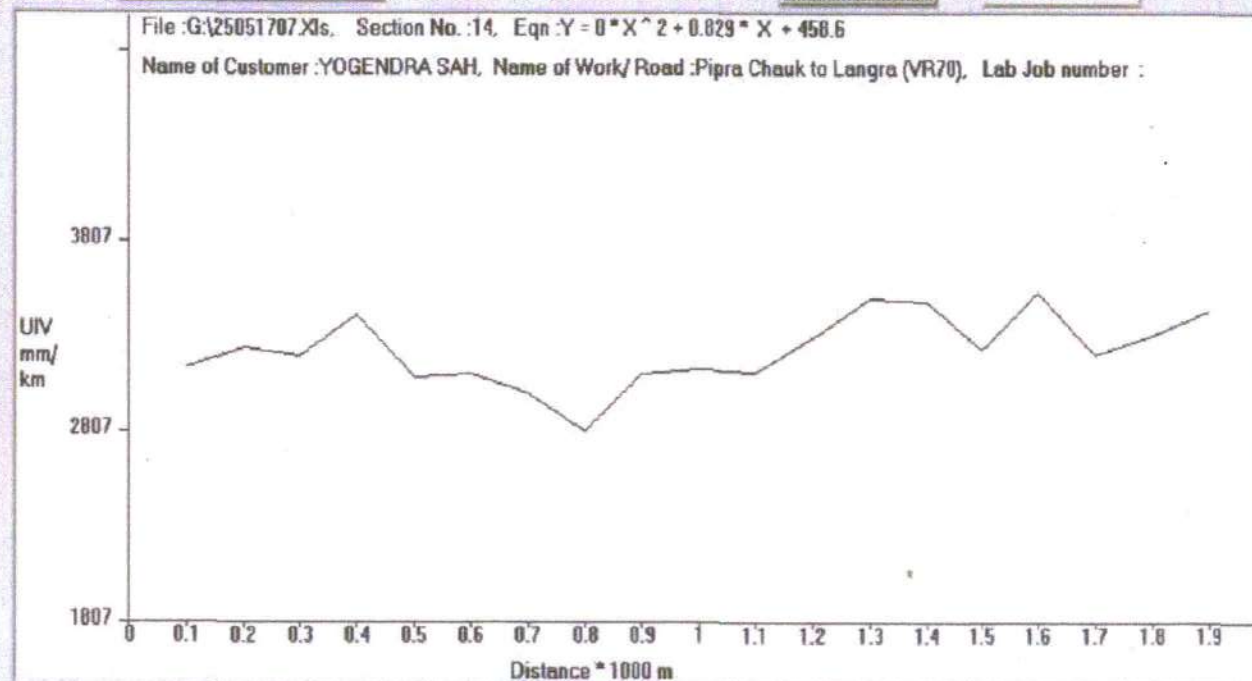
Test Date : 20/12/2024 Road Name : Pipra Chauk to Langra (VR70)
Machine No : 472 Road Type : (R) RURAL ROAD
Start S No : Side :
Start E No : Interval
Weather : UIV Range : 1807 To 5000 1000 mm/km
Start Location : 0.000 Dist Range : 0 To 2 0.1 * 1000 m
End Location : 1.870 Equation : $Y = 0 * X^2 + 0.829 * X + 458.6$

Print

Generate Report and Graph

Redraw Graph

Map View



R.D. 20/12/24

20/12/24

AG

21/12/24
Executive Engineer
Rural Works Department
Works Division, Bokatiadani
