

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद

पत्रांक ५५९३५०

प्रेषक,

कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद

सेवा में,

नोडल पदाधिकारी (MR-3054),
ग्रामीण कार्य विभाग,
बिहार, पटना।

औरंगाबाद / दिनांक २१/२/२४

विषय : गैर योजना मुख्य शीर्ष 3054 (नई अनुरक्षण नीति) सड़क अनुरक्षण ईकाई मद के लिए आवंटन निर्गत करने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि गैर योजना मुख्य शीर्ष 3054 (नई अनुरक्षण नीति) योजनान्तर्गत मांग पत्र विहित प्रपत्र में तैयार कर आपके आवश्यक कार्रवाई हेतु समर्पित किया जाता है।

अतः अनुरोध है कि संवेदक का भुगतान हेतु आवंटन निर्गत करने की कृपा की जाय।

अनु० - यथोक्त

विश्वासभाजन

२०/२/२४
कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद
२०/२/२४

Requisition Format for scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy - 2018 (Initial Rectification and Surface Renewal)

Name of Works Division : Rural Works Department, Works Division, Aurangabad


Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)	Agreement Amount (In Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/Km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Allocated Amount (in Lakh)	Up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
1	RM/AU/AU R/23/0004	L023-T04 TO NEURA DERI (TRACK23)	10602802147	24-Feb-23	2.7	129.54	33/MBD/2 023-24	11-May-24		2950.154	25	5%	65.87492	65.87492	28.23212	SURFACE COMPLETE
2	RM/AU/AU R/23/0006	L081-T04 AURANGABAD RAFIGANJ ROAD TO DHANDHAWA (TRACK81)	10602802281	24-Feb-23	6.61	330.644	32/MBD/2 023-24	11-May-24		3166.81	25	5%	155.68442	155.68442	66.72190	SURFACE COMPLETE
3	RM/AU/AU R/23/0008	L096-T04 POIWA MORE TO SEOGANJ RAFIGANJ BHAYYA POIWA (TRACK96)	10602802317	31-Mar-23	14.085	828.573	36/MBD/20 23-24	04-Jun-24		2678.61	25	5%	399.56058	399.56058	171.24026	SURFACE COMPLETE
Total													621.11992	621.11992	266.19428	

- Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed except SDBC Work.
- Up-to-date Physical Progress has been uploaded in MIS.

Sr. Divisional Account Officer,
Rural Works Department,
Works Division Aurangabad

Executive Engineer,
Rural Works Department,
Works Division, Aurangabad

File :C:\Users\BRARDA132\Desktop\NEW BUMP Report\RINA SINGH\03121502-1.xlsx Section No.:4. Egn test
 Name of Customer :RINA SINGH, Name of Work/ Road :L023-T04 TO NEURA DERI (TRACK23), Lab Job number

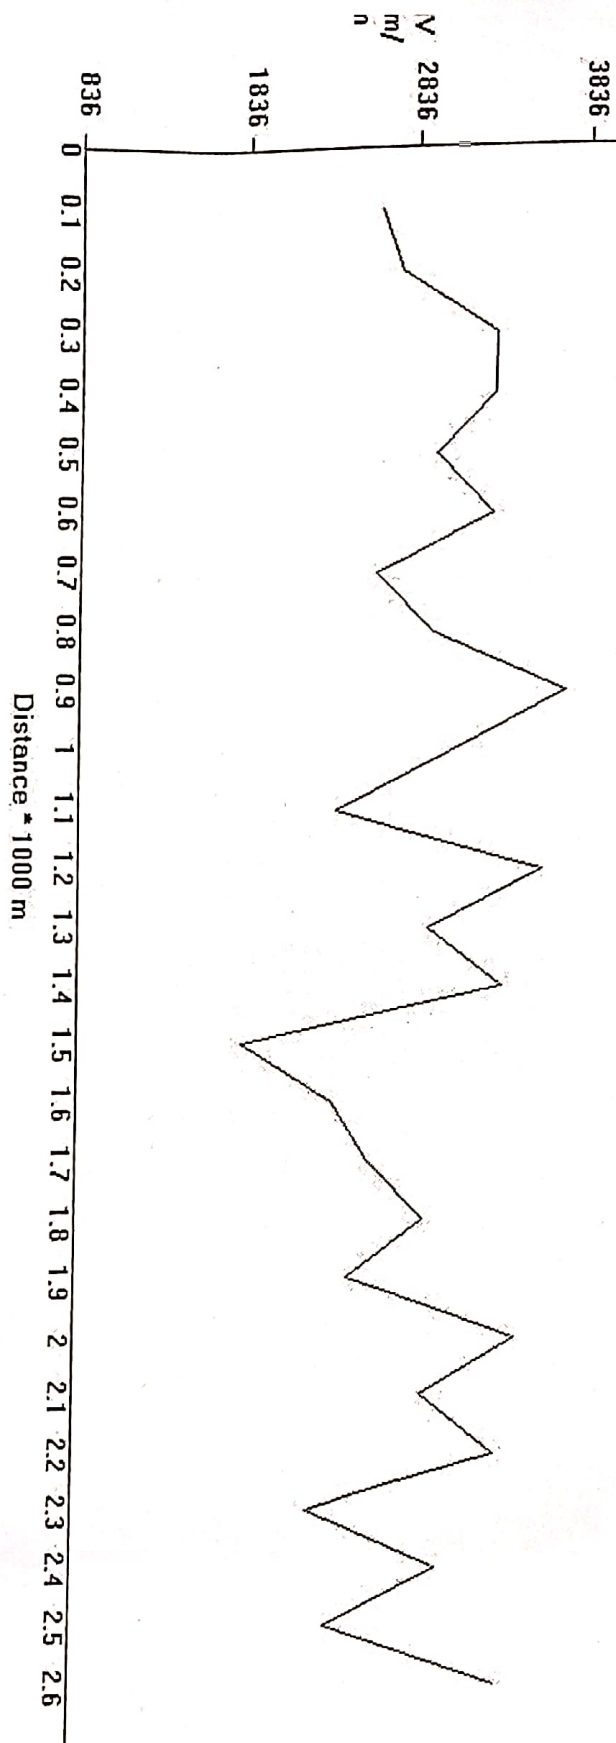

[Signature]
 09/12/23
 J.E.

[Signature]
 09/12/23
 A.E.

[Signature]
 Executive Engineer
 R.W.D. (W) Division
 Aurangabad

NAME OF ROAD - 1023-T04 TO NEURA DERI (TRACK23)

CONTRACTOR NAME- RINA SINGH

CONTRACTOR NAME- RINA SINGH														
SL.NO.	Date	Time	Section	No.	Length	Bumps	Speed	OR	UIV	TEGORY	IRI	Latitude	longitude	Event
					in km	in mm	Rate	mm/km		ROAD				
1	9/12/23	14:40:02		4	0.1	220	20.2	2200	2631 G					
2	9/12/23	14:40:28		4	0.1	230	20.2	2300	2745 G		3.58	24.674202	84.30034	Normal
3	9/12/23	14:41:18		4	0.1	280	20.2	2800	3313 G		3.72	24.67482	84.29965	Normal
4	9/12/23	14:42:0		4	0.1	280	20.2	2800	3313 G		4.4	24.674527	84.30003	Normal
5	9/12/23	14:43:0		4	0.1	250	20.2	2500	2972 G		4.4	24.674015	84.30082	Speed Breaker
6	9/12/23	14:43:4		4	0.1	280	20.2	2800	3313 G		3.99	24.673355	84.30131	Speed Breaker
7	9/12/23	14:44:0		4	0.1	220	20.2	2200	2631 G		6.11	24.672535	84.30128	Normal
8	9/12/23	14:44:15		4	0.1	250	20.2	2500	2972 G		5.33	24.671593	84.30128	Normal
9	9/12/23	14:44:15		4	0.1	320	10.1	3200	3767 G		4.93	24.670743	84.30165	Normal
10	9/12/23	14:44:50		4	0.1	260	20.2	2600	3086 G		4.13	24.66979	84.30327	Normal
11	9/12/23	14:45:0		4	0.1	310	20.2	3100	3654 G		4.8	24.668565	84.30456	Normal
12	9/12/23	14:45:25		4	0.1	290	20.2	2900	3426 G		4.53	24.666177	84.30552	Normal
13	9/12/23	14:45:25		4	0.1	200	20.2	2000	2404 G		3.3	24.66482	84.30574	Normal
14	9/12/23	14:45:25		4	0.1	220	20.2	2200	2631 G		3.3	24.663845	84.30549	Normal
15	9/12/23	14:46:1		4	0.1	250	20.2	2500	2972 G		3.58	24.66184	84.30564	Normal
16	9/12/23	14:46:1		4	0.1	290	20.2	2900	3426 G		3.99	24.667198	84.30508	Normal
17	9/12/23	14:46:36		4	0.1	150	20.2	1500	1836 G		2.6	24.666177	84.30552	Normal
18	9/12/23	14:47:11		4	0.1	200	20.2	2000	2404 G		2.6	24.66482	84.30574	Normal
19	9/12/23	14:47:11		4	0.1	220	20.2	2200	2631 G		3.3	24.663845	84.30549	Normal
20	9/12/23	14:47:11		4	0.1	250	20.2	2500	2972 G		3.58	24.66184	84.30564	Normal
21	9/12/23	14:48:0		4	0.1	210	20.2	2100	2518 G		3.99	24.660927	84.30547	Normal
22	9/12/23	14:48:22		4	0.1	300	20.2	3000	3540 G		3.44	24.65993	84.30542	Normal
23	9/12/23	14:48:22		4	0.1	250	20.2	2500	2972 G		4.66	24.65962	84.30626	Normal
24	9/12/23	14:48:22		4	0.1	290	20.2	2900	3426 G		3.99	24.659507	84.30714	Normal
25	9/12/23	14:49:0		4	0.1	190	20.2	1900	2290 G		4.53	24.657938	84.30737	Normal
26	9/12/23	14:51:22		4	0.1	260	20.2	2600	3086 G		3.16	24.658898	84.30756	Normal
27	9/12/23	14:51:22		4	0.1	200	20.2	2000	2404 G		4.13	24.657337	84.30668	Curve
28	9/12/23	14:52:0		4	0.1	290	20.2	2900	3426 G		3.3	24.657452	84.30687	Normal
Average												2950.154		

Cam 9/12/23
J.E.

09/12/23
A-E.

Executive Engineer
R.W.D. (M) Division
Aurangabad
