

कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज

Mobile No- 8986915814

Email ID- eerwdwd2bettiah@gmail.com

पत्रांक- 885

/ नरकटियागंज, दिनांक- 30/05/2025

प्रेषक,

कार्यपालक अभियन्ता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, नरकटियागंज।

सेवा में,

नोडल पदाधिकारी,
नई अनुसंधान नीति-2018 (MR-3054)
ग्रामीण कार्य विभाग, बिहार पटना।

विषय:- MR(3054) New Maintenance Policy 2018 योजना अन्तर्गत पथ के निर्माण में संवेदक के विपत्र भुगतान हेतु राशि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में सूचित करना है कि शीर्ष MR(3054) New Maintenance Policy 2018 अन्तर्गत पथ:-

1. L043-T04 to Maheshpur (VR43)

का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भरकर की जाती है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु०:-यथोक्त।

विश्वासभाजन



कार्यपालक अभियन्ता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नरकटियागंज

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl. No.	Package No.	Name of Road	Project IS as per MIS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks.
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenance (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/WE/NAR/24/0005	L043-T04 to Maheshpur (VR43)	31808902157	<u>6115</u> <u>04.12.2023</u>	2.230	119.240	89.96733	20.45620	<u>03/24-25</u> <u>03/09/2024</u>	02-06-2025	-	2872	SDBC-25MM	5%	0.00000	89.88882		Surface Complete

Executive Engineer
Rural Works Department
Works Division Narkatiaganj

Name of Road:-1.043-T104 to Maheshpur (VR43), Length-2.230 KM

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	ATFGOR ROAD	Latitude	Longitude	Event
29-05-2025	10:31:08	85	0.1	380	20.2	3800	3285	G	27.7072	84.674562	Normal
29-05-2025	10:32:00	85	0.1	370	20.1	3700	3743	G	27.7927	84.674595	Normal
29-05-2025	10:32:18	85	0.1	340	20.2	3400	3457	G	27.8537	84.67508	Normal
29-05-2025	10:32:18	85	0.1	360	20.3	3600	3653	G	27.8365	84.676093	Normal
29-05-2025	10:33:00	85	0.1	300	20.1	3000	3047	G	27.8398	84.677053	Normal
29-05-2025	10:33:00	85	0.1	280	20.1	2800	2883	G	27.9162	84.677542	Normal
29-05-2025	10:33:29	85	0.1	280	21.2	2800	2883	G	27.9953	84.677978	Normal
29-05-2025	10:33:29	85	0.1	340	22.2	3400	3400	G	27.10712	84.67848	Normal
29-05-2025	10:34:04	85	0.1	320	20.2	3200	3280	G	27.11408	84.679123	Normal
29-05-2025	10:34:04	85	0.1	280	22.3	2800	2812	G	27.1207	84.67978	Normal
29-05-2025	10:34:40	85	0.1	280	23.3	2800	2812	G	27.12818	84.680302	Normal
29-05-2025	10:35:00	85	0.1	340	20.2	3400	3467	G	27.13657	84.680538	Normal
29-05-2025	10:35:15	85	0.1	320	24.3	3200	3280	G	27.14545	84.680842	Normal
29-05-2025	10:35:15	85	0.1	290	23.3	2900	2905	G	27.15363	84.681093	Normal
29-05-2025	10:35:15	85	0.1	300	24.3	3000	2999	G	27.1619	84.681447	Normal
29-05-2025	10:36:00	85	0.1	310	24.3	3100	3186	G	27.17093	84.6817	Normal
29-05-2025	10:36:00	85	0.1	370	20.2	3700	3748	G	27.17975	84.68175	Normal
29-05-2025	10:36:25	85	0.1	270	26.3	2700	2718	G	27.18863	84.681665	Normal
29-05-2025	10:36:25	85	0.1	330	23.3	3300	3373	G	27.19758	84.68172	Normal
29-05-2025	10:37:01	85	0.1	330	20.2	3300	3309	G	27.20618	84.68175	Normal
29-05-2025	10:38:00	85	0.1	270	20.3	2700	2735	G	27.21503	84.681582	Normal
29-05-2025	10:38:11	85	0.1	240	20.3	2400	2481	G	27.22297	84.68116	Normal
29-05-2025	10:38:11	85	0.1	230	20.3	2300	2336	G	27.2308	84.68069	Normal
Average IRI Value=							2872				

29/05/25

JE

29/5/25

30/5/25

Name of Customer: Khurshid Alam
 Name of Work: LO43-T04 to Maheshpur (VR43)
 Road: LO43-T04 to Maheshpur (VR43)
 Lab Job number: 29-05-2025
 Date: 29-05-2025
 Section No. 45


Print Generate Report and Graph

Test Date:	29-05-2025	Road Name:	LO43-T04 to Maheshpur (VR43)
Machine No:	402	Road Type:	(R) RURAL ROAD
Start S No:		Side:	
Start E No:		Interval:	
Weather:		UV Range:	1573 To 4000
Start Location:		Dial Range:	0 To 2.7
End Location:		Equation:	$Y = 0 \cdot X^2 + .136 \cdot X + 132.5$

Redraw Graph

Map View

File: F:\228211\47.Xls. Section No. 45. Eqn: $Y = 0 \cdot X^2 + 1.136 \cdot X + 132.5$
 Name of Customer: Khurshid Alam, Name of Work/Road: LO43-T04 to Maheshpur (VR43), Lab

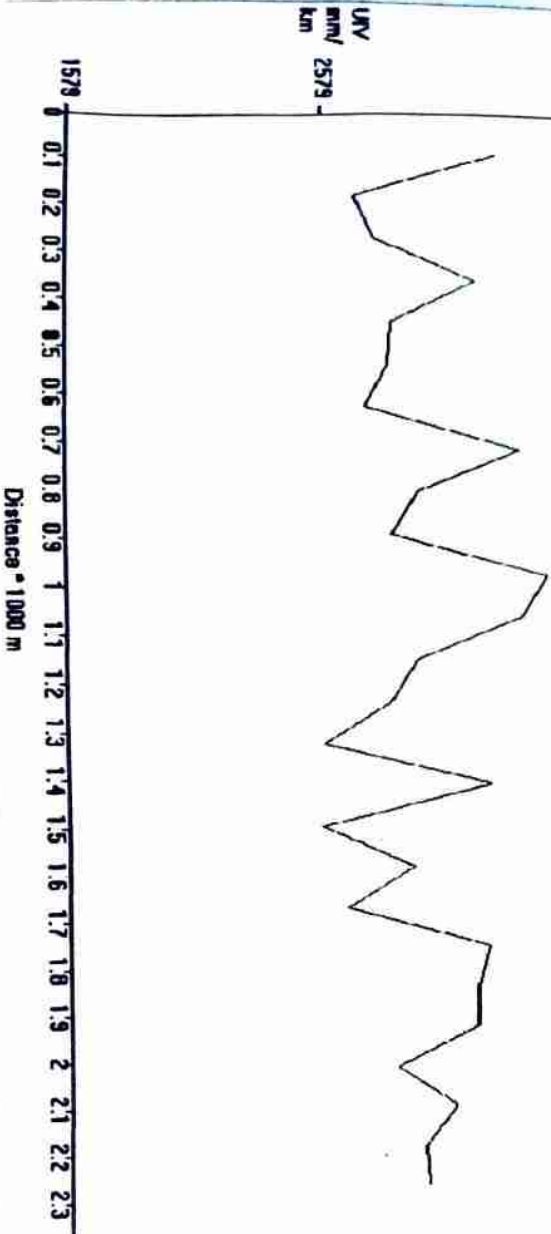

ASDH
 29/05/25
 JE

ASDH
 29/05/25
 JE

ASDH
 30/5/25

OFFICE OF THE EXECUTIVE ENGINEER,
RURAL WORKS DEPARTMENT, WORKS DIVISION, NARKATIAGANJ

Name of Road :- L.043-104 to Maheshpur (VR43)
Name of Scheme :- MR 3054 New Maintenance Policy 2018
Name of Contractor :- Khurshid Alam
Length of Road :- 2.230 KM
Project ID :- M1808902157
Package No. :- RM/WE/NAR/24/0005
Name of Block :- Sikta

Certified that all item wise 100% measurement has been taken by me


29/05/25

JE

Certified that all item wise 50% measurement has been verified by me


29/05/25
AE

Certified that all item wise 10% measurement has been verified by me


30/5/25

EE
