Steco Analyzer

Name of Customer : Chandan Kumar Singh

Name of Work/ Road : Simra Bhati to Dihara

Lab Job number : 107

Date : 24-06-2020

Section No. : 107

Test Date : 24-06-2020 | Road Name : Simra Bhati to Dihara

Machine No : 377 | Road Type : (R) RURAL ROAD

Start S No : 1230 | Side : Kutumba

Start E No : 1299 | Interval

Weather : Normal | UIV Range : 515 To 5000 1000 mm/km

Start Location : 24 68979.84 3 | Dist Range : 0 To 1.988 0.028 * 1000 m

End Location : 24 63923.84 3 | Equation : Y = 0 * X ^ 2 + 1.000 * X + 415.2

Print | Generate Report and Graph | Redraw Graph | Map View

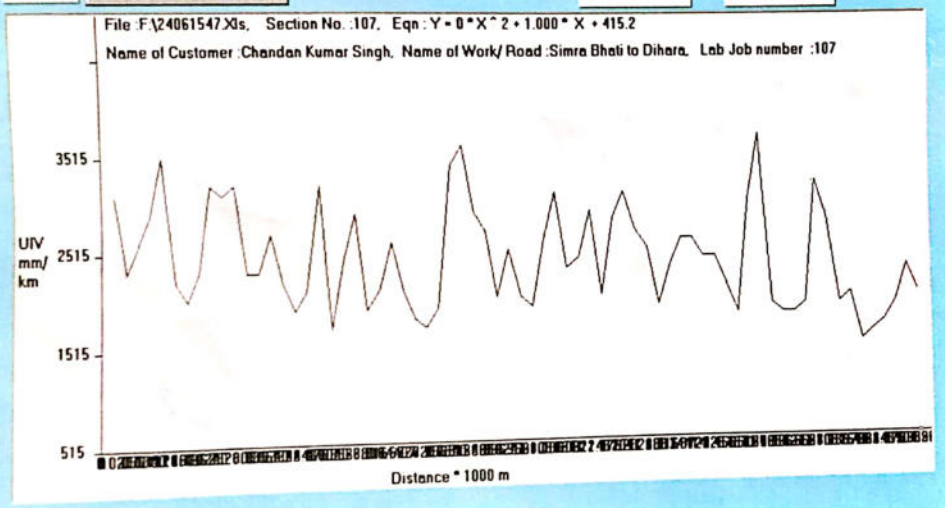

Executive Engineer
R.W.D. Works Division, Aurangabad

Scanned with CamScanner

Name of Road:- Simra Bhatul to Dihara

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/ 6/ 20	10: 58: 0	107	0.1	270	0	2700	3115	G	24.68979	84.354998	Normal
24/ 6/ 20	10: 58: 34	107	0.1	190	10.1	1900	2315	G	24.689	84.355387	Normal
24/ 6/ 20	10: 59: 8	107	0.1	220	0	2200	2615	G	24.688453	84.356077	Normal
24/ 6/ 20	11: 0: 0	107	0.1	250	0	2500	2915	G	24.68788	84.356835	Normal
24/ 6/ 20	11: 0: 19	107	0.1	310	0	3100	3515	G	24.68742	84.357693	Normal
24/ 6/ 20	11: 1: 0	107	0.1	180	0	1800	2215	G	24.686945	84.35835	Normal
24/ 6/ 20	11: 2: 0	107	0.1	160	0	1600	2015	G	24.686043	84.358282	Normal
24/ 6/ 20	11: 2: 5	107	0.1	190	10.1	1900	2315	G	24.685163	84.358113	Normal
24/ 6/ 20	11: 3: 0	107	0.1	280	10.1	2800	3215	G	24.684413	84.358602	Normal
24/ 6/ 20	11: 3: 51	107	0.1	270	0	2700	3115	G	24.683547	84.358855	Normal
24/ 6/ 20	11: 4: 26	107	0.1	280	0	2800	3215	G	24.682987	84.359612	Normal
24/ 6/ 20	11: 5: 1	107	0.1	190	0	1900	2315	G	24.682437	84.360318	Normal
24/ 6/ 20	11: 6: 0	107	0.1	190	0	1900	2315	G	24.681527	84.360403	Normal
24/ 6/ 20	11: 6: 12	107	0.1	230	0	2300	2715	G	24.681172	84.360875	Normal
24/ 6/ 20	11: 7: 22	107	0.1	180	0	1800	2215	G	24.680887	84.36182	Normal
24/ 6/ 20	11: 8: 0	107	0.1	150	0	1500	1915	G	24.67999	84.361935	Normal
24/ 6/ 20	11: 8: 33	107	0.1	170	10.1	1700	2115	G	24.679203	84.361548	Normal
24/ 6/ 20	11: 9: 8	107	0.1	280	0	2800	3215	G	24.678627	84.360823	Normal
24/ 6/ 20	11: 10: 0	107	0.1	130	0	1300	1715	G	24.678723	84.35983	Normal
24/ 6/ 20	11: 10: 19	107	0.1	200	10.1	2000	2415	G	24.678047	84.359343	Normal
24/ 6/ 20	11: 11: 29	107	0.1	250	0	2500	2915	G	24.67734	84.35882	Normal
24/ 6/ 20	11: 12: 5	107	0.1	150	0	1500	1915	G	24.676463	84.358585	Normal
24/ 6/ 20	11: 12: 40	107	0.1	170	0	1700	2115	G	24.675557	84.358535	Normal
24/ 6/ 20	11: 13: 15	107	0.1	220	0	2200	2615	G	24.674897	84.35914	Normal
24/ 6/ 20	11: 14: 0	107	0.1	170	10.1	1700	2115	G	24.67448	84.36	Normal
24/ 6/ 20	11: 14: 26	107	0.1	140	0	1400	1815	G	24.673662	84.360302	Normal
24/ 6/ 20	11: 15: 1	107	0.1	130	0	1300	1715	G	24.672768	84.360185	Normal
24/ 6/ 20	11: 15: 36	107	0.1	150	0	1500	1915	G	24.671855	84.36008	Normal
24/ 6/ 20	11: 16: 12	107	0.1	300	0	3000	3415	G	24.670978	84.359948	Normal
24/ 6/ 20	11: 17: 0	107	0.1	320	0	3200	3615	G	24.670102	84.359965	Normal
24/ 6/ 20	11: 18: 0	107	0.1	250	0	2500	2915	G	24.669205	84.359882	Normal
24/ 6/ 20	11: 18: 33	107	0.1	230	0	2300	2715	G	24.66831	84.359713	Normal
24/ 6/ 20	11: 19: 8	107	0.1	160	0	1600	2015	G	24.667642	84.359157	Normal
24/ 6/ 20	11: 20: 0	107	0.1	210	0	2100	2515	G	24.667397	84.358182	Normal
24/ 6/ 20	11: 20: 18	107	0.1	160	0	1600	2015	G	24.667115	84.35739	Normal
24/ 6/ 20	11: 21: 29	107	0.1	150	0	1500	1915	G	24.666198	84.357238	Normal
24/ 6/ 20	11: 22: 4	107	0.1	220	0	2200	2615	G	24.66536	84.357373	Normal
24/ 6/ 20	11: 22: 40	107	0.1	270	0	2700	3115	G	24.665115	84.358332	Normal
24/ 6/ 20	11: 23: 15	107	0.1	190	0	1900	2315	G	24.664832	84.359258	Normal
24/ 6/ 20	11: 24: 0	107	0.1	200	0	2000	2415	G	24.664062	84.359325	Normal
24/ 6/ 20	11: 24: 25	107	0.1	250	0	2500	2915	G	24.663163	84.35914	Normal
24/ 6/ 20	11: 25: 1	107	0.1	160	0	1600	2015	G	24.662252	84.358988	Normal
24/ 6/ 20	11: 26: 11	107	0.1	240	0	2400	2815	G	24.661722	84.358972	Normal
24/ 6/ 20	11: 27: 0	107	0.1	270	0	2700	3115	G	24.661805	84.357978	Normal
24/ 6/ 20	11: 27: 22	107	0.1	230	0	2300	2715	G	24.661462	84.357305	Normal
24/ 6/ 20	11: 28: 0	107	0.1	210	0	2100	2515	G	24.66059	84.35702	Normal
24/ 6/ 20	11: 29: 8	107	0.1	150	0	1500	1915	G	24.659712	84.35677	Normal
24/ 6/ 20	11: 29: 43	107	0.1	190	10.1	1900	2315	G	24.658822	84.356548	Normal
24/ 6/ 20	11: 30: 18	107	0.1	220	0	2200	2615	G	24.657945	84.356295	Normal
24/ 6/ 20	11: 31: 0	107	0.1	220	0	2200	2615	G	24.657065	84.356027	Normal
24/ 6/ 20	11: 31: 29	107	0.1	200	10.1	2000	2415	G	24.656188	84.355773	Normal
24/ 6/ 20	11: 32: 4	107	0.1	200	0	2000	2415	G	24.655305	84.355522	Normal
24/ 6/ 20	11: 32: 39	107	0.1	170	0	1700	2115	G	24.654408	84.355318	Normal
24/ 6/ 20	11: 33: 15	107	0.1	140	10.1	1400	1815	G	24.653537	84.3551	Normal
24/ 6/ 20	11: 34: 0	107	0.1	260	10.1	2600	3015	G	24.65264	84.354882	Normal
24/ 6/ 20	11: 35: 1	107	0.1	330	0	3300	3715	G	24.651765	84.354662	Normal
24/ 6/ 20	11: 35: 36	107	0.1	150	0	1500	1915	G	24.65087	84.354528	Normal
24/ 6/ 20	11: 36: 11	107	0.1	140	0	1400	1815	G	24.649988	84.354393	Normal
24/ 6/ 20	11: 37: 0	107	0.1	140	10.1	1400	1815	G	24.649082	84.354208	Normal
24/ 6/ 20	11: 37: 22	107	0.1	150	10.1	1500	1915	G	24.64818	84.354023	Normal
24/ 6/ 20	11: 38: 0	107	0.1	280	10.1	2800	3215	G	24.647288	84.353855	Normal
24/ 6/ 20	11: 38: 0	107	0.1	240	10.1	2400	2815	G	24.64641	84.353703	Normal
24/ 6/ 20	11: 38: 32	107	0.1	150	10.1	1500	1915	G	24.645508	84.353568	Normal
24/ 6/ 20	11: 39: 7	107	0.1	160	10.1	1600	2015	G	24.644615	84.3534	Normal
24/ 6/ 20	11: 39: 43	107	0.1	110	10.1	1100	1515	G	24.6437	84.353248	Normal
24/ 6/ 20	11: 40: 18	107	0.1	120	10.1	1200	1615	G	24.642793	84.35308	Normal
24/ 6/ 20	11: 40: 53	107	0.1	130	10.1	1300	1715	G	24.641915	84.352895	Normal
24/ 6/ 20	11: 41: 0	107	0.1	150	10.1	1500	1915	G	24.641027	84.35271	Normal
24/ 6/ 20	11: 41: 29	107	0.1	190	10.1	1900	2315	G	24.640122	84.352542	Normal
24/ 6/ 20	11: 42: 4	107	0.1	160	10.1	1600	2015	G	24.639228	84.35239	Normal
Total Length			7.000								

Y = 0 * X ^ 2 + 1.000 * X + 415.2
X = 1900
Y = 2315

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

Sunilkumar
26/6/2020
J.E.

26/6/20
Executive Engineer
R.W.D. Works Division, Aurangabad

Scanned with CamScanner

OM SAI CONSULTANTS

(AN ISO 9001:2015 & ISO/IEC 17025: 2017 CERTIFIED NABL ACCREDITED LAB)
Address: - Bank of India Colony, Near Jai Shree Gas Godown, South D/SS,
P.O.-B.V. College Raja Bazaar, Patna-800014, Contact No. +919472909287
Email- omsaiconsultantspatna@gmail.com
Doc. No.: OSC/7.8/F-01

TEST REPORT

Issue To:
M/S CHANDAN KUMAR SINGH
ANANDIBAG, DEO, P.O. + P.S.- DEO,
DIST. - AURANGABAD- 824202, BIHAR.

Report No.: OSC/BR/150620/01
Date of Receiving: 12/06/2020
Testing Period: 12/06/2020 TO 15/06/2020
Date of Reporting: 15/06/2020

Project Name: CONSTRUCTION OF ROAD FROM SIMRA BHATTHI TO AMBA DEO ROAD, (3054).

Sample Description: Semi Dense Bituminous Concrete (S.D.B.C.)

Sample Condition: Good (Packed in Bag).

BITUMEN CONTENT TEST

S. No.	Test Parameter	Test Method	Result	Requirements MORTH Specification Table- 500- 15	Conformity
1.	Binder Content (%)	IRC SP-11	5.09	5.0 Min	Yes

.....End of Report.....

26.6.20
Executive Engineer
R.W.D. Works Division, Aurangabad

Sunilkumar
26/6/2020
J. R.

OM SAI CONSULTANTS

Checked By

Authorized Signatory

1. The result listed refers only to the tested samples and applicable parameters endorsement of product is neither inferred nor implied.
2. Total liability of our Lab. is limited to the invoiced amount.
3. Samples will be destroyed after 90 days from the date of issue of test report.
4. This report is not be reproduced wholly or in part and cannot be used as an evidence in the court of law and should not be used in any advertising media without our special permission in writing.

NABL ACCREDITED LABORATORY

Scanned with CamScanner

कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, औरंगाबाद।

Email ID:-eerwdaurangabad1@gmail.com

पत्रांक 2610 अनु औरंगाबाद / दिनांक 26.6.2020

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद।

सेवा में,

नोडल पदाधिकारी **(MR 3054)**
ग्रामीण कार्य विभाग
पटना, बिहार

विषय :– नई अनुरक्षण नीति–2018MR (3054)योजना के अंतर्गत पथ में कराये गये कार्य के विरूद्ध आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपरोक्त विषय के संबंध में सूचित करना है कि नई अनुरक्षण नीति–2018 MR (3054)योजना के अंतर्गत पथ में कराये गये कार्य के लिए संवेदक को भुगतान करने हेतु अधियाचना विहित प्रपत्र में भरकर आवश्यक कार्यवाही हेतु समर्पित की जाती है।

अनु :– यथोक्त।

विश्वासभाजन
26.6.20
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, औरंगाबाद
26.06

Scanned with CamScanner

OFFICE OF EXECUTIVE ENGINEER, RURAL WORKS DEPARTMENT, WORKS DIVISION, Aurangabad

Reqisition Format for Scheme Head- MR(3054) under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- Aurnagabad

Sl no.	Package No MR-N/ 2019-20 Aurangabad/	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No & Date	Administrative Approval (AA)		Agreement Amount (In Lakh)		Agreement No& Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/ km)	SDBC		Previous Total Alloted Amount (In Lakh)	up-to-date expenditure as per MIS (In Lakh)	Requisition against work done (In Lakh)	Remarks
					Length (In km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintenance (In Lakh)					Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage				
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	10	Tengra - Rahua	10602802090	Letter No. 3140 Date 22.07.2019	4.37	114.270	102.84000	37.30000	84MBD/2019-20 Date 25.02.2020	24.11.2020	–	2315	25	5.121	0.00000	0.00000	102.84000	Ongoing
2	10	GULJAR PIGHA To PIPRA	NEA2200064	Letter No. 3140 Date 22.07.2019	1.300	39.21000	35.56000	11.10000	84MBD/2019-20 Date 25.02.2020	24.11.2020	–	3315	25	5.11	0.00000	0.00000	35.56000	Ongoing
3	3	Punpun Jamhor Road To Dhramsala Via Jivan Bigha,Taliahara	10602803028	Letter No. 3140 Date 22.07.2019	2.350	84.98036	76.48232	22.584	90MBD/2019-20 Date 22.02.2020	21.11.2020	–	3715	25	5.09	0.00000	0.00000	76.48232	Ongoing
4	22	Simra Bathi to Amba Deo Road	10602901062	Letter No. 3140 Date 22.07.2019	7.000	159.30914	143.37823	65.780	77MBD/2019-20 Date 20.02.2020	19.11.2020	–	2315	25	5.09	0.00000	0.00000	143.37823	Ongoing
		Total															358.26055	

26.6.20

Executive Engineer
Rural Works Department
Works Division, Aurnagabad

Scanned with CamScanner
