कार्यपालक अभियंता का कार्यालय

ग्रामीण कार्य विभाग,कार्य प्रमंडल,झाझा (जमुई)।

मोवाइल न०- 8986915861 ईमेल- rwdjhajha0@gmail.com

पत्रांक- 1307 / झाझा दिनांक- 29.06.2020

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल झाझा।

सेवा में,

नोडल पदाधिकारी,
"नई अनुरक्षण नीति 2018" (3054-MR)
ग्रामीण कार्य विभाग,बिहार, पटना।

विषय :-3054(MR)/ नई अनुरक्षण नीति 2018 के अंतर्गत कराये गए निम्न कार्यों के विरुद्ध में आवंटन उपलब्ध कराने के सम्बन्ध में।

महाशय,

उपरोक्त विषय के सम्बन्ध में सूचित करना है कि 3054(MR) / "नई अनुरक्षण नीति 2018" के अंतर्गत **(1)** Fatehpur More- Rankura, **(2)** Dhamna- Jhajha Path Near Harhanja-Chhapa **(3)** Jagitila More-Jogitila **(4)** Harhanja-sidhesari एवं **(5)** Pargaha More To Bhikha Road का Surface कार्य पूर्ण हो चुका है। इस कार्य के भुगतान हेतु आवंटन की अधियाचना विहित प्रपत्र में भर कर की जाती है।

अतः सादर अनुरोध है कि शीघ्र आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0-यथोक्त।

विश्वासभाजन

29/6/2020

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल,झाझा।

पता:-पिपराडीह, शहीद सुनील चौक के नजदीक नवाव रोड, झाझा,जिला-जमुई,पिन कोड-811308

Scanned with CamScanner

RWD Works Division, Jhajha (Dist :- Jamui)

Requisition Format for Scheme Head- MR (3054) Under Bihar Rural Road " New Manitenance Policy 2018" (Initial Rectification and Surface Renewal)

Name of Division:- Jhajha

S.N	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (A.A) Letter No. & Date	Administrative Approval (A.A)		Agreement Amount (in Lakh)		Agreement No. & Date	Date of Comletion as per Agreement	Actual Date of Completion	Value of IRI in MM/KM	Thickness of Bitumen Layer (in MM)	Value of Bitumen Content (in %)	Previous Total Alloted Amount (in Lakh)	Up-to -date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks
					Length (K.M)	Amount (in Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Yaar Routine Maintenance										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N/19-20 JHAJHA/17	Fatehpur More-Ranikura	20804102051	3030 & 16.07.2019	1.166	36.088	20.15227	10.2202	02/MBD/MR-N/2020-21 & 15.05.2020	14.02.2021	26.06.2020	3098	25	5.20	0	0	20.15227	Surface Completed
2	MR-N/19-20 JHAJHA/17	Dhamna- Jhajha Path Near Harhanja-Chhapa	NEA22000742	3030 & 16.07.2019	2.00	61.768	34.50624	17.50013	02/MBD/MR-N/2020-21 & 15.05.2020	14.02.2021	25.06.2020	2897	25	5.00	0	0	34.50624	Surface Completed
3	MR-N/19-20 JHAJHA/17	Jagitila More-Jogitila	20804102058	3030 & 16.07.2019	1.054	35.448	20.33030	9.44968	02/MBD/MR-N/2020-21 & 15.05.2020	14.02.2021	27.06.2020	3244	25	5.04	0	0	20.33030	Surface Completed
4	MR-N/19-20 JHAJHA/18	Harhanja-sidhesari	20804102055	3030 & 16.07.2019	1.244	38.812	21.44434	11.25153	05/MBD/MR-N/2020-21 & 18.05.2020	17.02.2021	24.06.2020	3062	25	5.14	0	0	21.44434	Surface Completed
5	MR-N/19-20 JHAJHA/18	Pargaha More To Bhikha Road	20804101064	3030 & 16.07.2019	1.700	53.877	30.54199	14.75923	05/MBD/MR-N/2020-21 & 18.05.2020	17.02.2021	25.06.2020	3132	25	5.04	0	0	30.54199	Surface Completed

29/6/2020

Executive Engineer
RWD Works Division, Jhajha

Scanned with CamScanner

Name of Road:- Fatehpur More- Ranikura , Length (1.170 KM)												
Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
28/ 6/ 20	12: 35: 0	6	0.1	220	10.1	2200	2214	G	3.07	24.80689	86.36436	Normal
28/ 6/ 20	12: 35: 0	6	0.1	340	30.3	3400	3439	G	4.54	24.80641	86.36508	Normal
28/ 6/ 20	12: 36: 0	6	0.1	250	30.3	2500	2520	G	3.44	24.80603	86.36606	Normal
28/ 6/ 20	12: 36: 0	6	0.1	250	30.3	2500	2520	G	3.44	24.80578	86.3669	Normal
28/ 6/ 20	12: 36: 0	6	0.1	260	30.3	2600	2622	G	3.57	24.80526	86.36776	Speed Breaker
28/ 6/ 20	12: 37: 0	6	0.1	390	10.1	3900	3950	G	5.14	24.80506	86.36854	Normal
28/ 6/ 20	12: 37: 0	6	0.1	330	30.3	3300	3337	G	4.42	24.80587	86.36874	Normal
28/ 6/ 20	12: 37: 0	6	0.1	250	30.3	2500	2520	G	3.44	24.80668	86.36924	Normal
28/ 6/ 20	12: 38: 0	6	0.1	380	30.3	3800	3848	G	5.02	24.80749	86.36976	Normal
28/ 6/ 20	12: 38: 0	6	0.1	380	30.3	3800	3848	G	5.02	24.80791	86.36901	Normal
28/ 6/ 20	12: 38: 0	6	0.1	330	30.3	3300	3337	G	4.42	24.80874	86.36909	Normal
28/ 6/ 20	12: 39: 0	6	0.089	300	10.1	3000	3031	G	4.06	24.80738	86.3697	Normal

Y = 0 * X ^ 2 + 1.021 * X - 31.77
X = 0
Y = -32

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

29/6/2020

Executive Engineer
Rural Works Department
Works Division, Jhalda

Scanned with CamScanner

Steco Analyzer

Name of Customer :	Rajeev Kumar	Test Date :	6 /28/2020
Name of Work/ Road :	Fatehpur More- Ranikura	Machine No :	385
Lab Job number		Start S No :	
Date :	6 /28/2020	Start E No :	
Section No.	6	Weather :	
		Start Location :	0
		End Location :	1.166

Road Name : Fatehpur More- Ranikura
Road Type : (R) RURAL ROAD
Side :
Interval
UIV Range : 1214 To 5000 1000 mm/km
Dist Range : 0 To 1.3 0.1 * 1000 m
Equation : Y = 0 * X ^ 2 + 1.021 * X - 31.77

Print | Generate Report and Graph | Redraw Graph | Map View

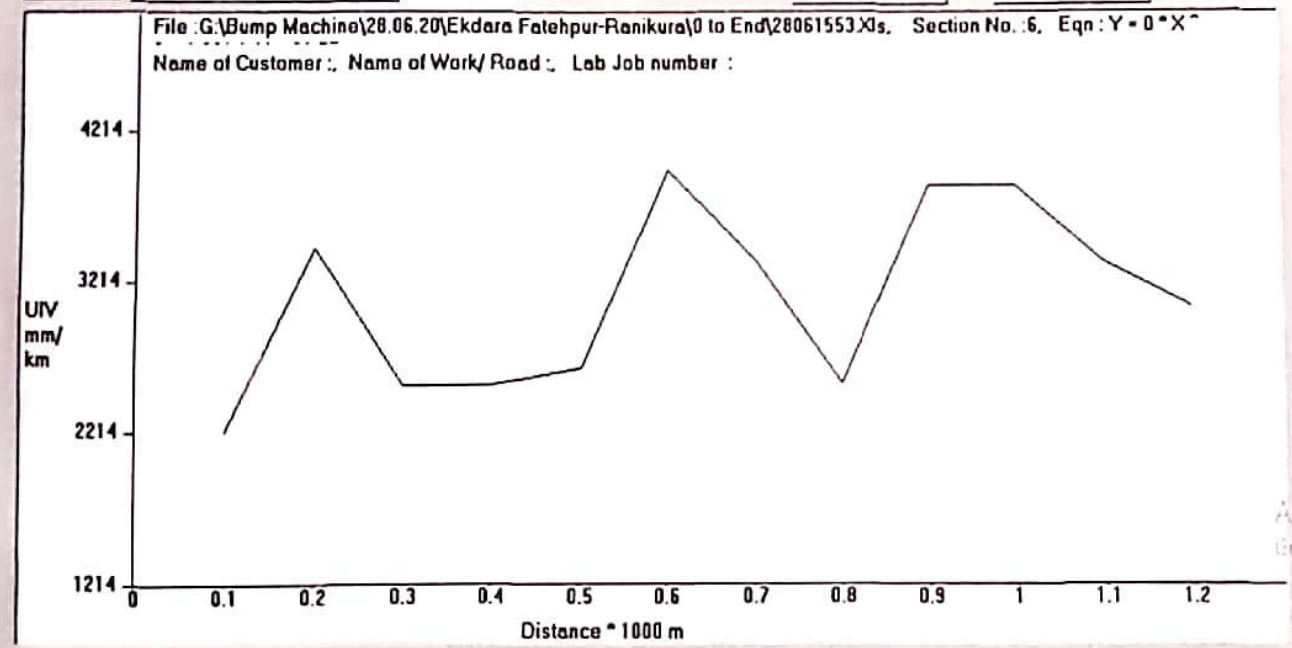

29/6/2020

Executive Engineer
Rural Works Department
Works Division. Jhalha

Scanned with CamScanner
