कार्यपालक अभियन्ता का कार्यालय

ग्रामीण कार्य विभाग, कार्य प्रमंडल, नरकटियागंज (प0 चम्पारण)
मोबाईल नं0–8986915814ईमेल
आई0डी0–eerwdwd2bettiah@gmail.com

पत्रांक...1232.../ नरकटियागंज दिनांक...8/6/21...../

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज

सेवामें,

अपर मुख्य कार्यपालक पदाधिकारी–सह–सचिव
नोडल पदाधिकारी (3054)
ग्रामीण कार्य विभाग, बिहार पटना।

विषयः– **MR(3054) New Maintenance Policy 2018 योजना अन्तर्गत निर्माण कार्य की राशि के संबंध में।**

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि MR(3054) New Maintenance Policy 201 योजना अन्तर्गत भुगतान हेतु अधियाचना विहित प्रपत्र में तैयार कर आवश्यक अग्रेतर कार्रवाई हे समर्पित किया जाता है। अधियाचना प्रपत्र के साथ उपयोगिता प्रमाण पत्र भी संलग्न है।

अतः निवेदन है कि अधियाचित राशि विमुक्त करने की कृपा की जाय ताकि कराये गये का का भुगतान किया जा सके।

अनु0– यथोक्त।

विश्वासभाजन

8/6/21

(राजीव रंजनसुधांशू)
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, नरकटियागंज

08/06/2

FORM GFR 19-A

(See Government of India's Decision (1) Below Rule - 150)

STATE - BIHAR

Form of Utilisation Certificate upto 22-05-2021

MR NEW MAINTENANCE POLICY

Sl. No.	Name of scheme	Sanction No. and Date	Amount received (in Rs. Lacs)	Particulars
1	MR NEW MAINETANCE POLICY	Secretary cum Empowerd officer BRRDA, letter No. UPTO DATE PL OFFICE LEVEL 1	5900.82374	Certified that out of Rs. 3096.09617 lacs of grants -in- aid sanctioned during the year 2021-22 in favour of EE - RWD (WD) NARKATIAGANJ, a sum of Rs5636.15368 lacs has been utilized for the purpose of MR NEW MAINTENANCE POLICY Schemes as given in the margin for which it was Sanctioned and that the **balance of Rs 264.67006 Lac remaining unutilised** at the end of the period under.
	Total		5900.82374	

2 Certified that I have satisfied myself that the conditions on which the grants - in - aid was sanctioned have been

Kinds of checks exercised:-

i Works have been supervised by Executive Enguneer / Superitending engineer .
ii Periodical inspection has been conducted by Executive Engineer / Superutending Engineer.
iii Construction materials have tested.
iv Measurements have been recorded in the MBs and test check conducted by the Assistant
v All other codal formalities have been observed .

3 Physical progress achieved:-

i Construction of Raod Works.
ii Construction of C.D. Works.

8/6/21

DAO
Rural Works Department
Works Division, Narkatiaganj

08/06/21

8/6/21

Executive Engineer
Rural Works Department
Works Division, Narkatiaganj

08/06/21

Requisition Format for Scheme Head - MR(3054) under Bihar Rural Road Maintenance Policy- 2018 (Initial Rectification and surface Renewal)

Name of Division :- Narkatiaganj

Name of Circle :- Bettiah

Sl. No.	Package No.	Name of Road	Project IS as per MIS	Administrative Sanction Letter No & Date.	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (in lakh)	up-to-date expenditure as per MIS (in Lakh)	Requisition against work done (in Lakh)	Remarks.
					Length (in km)	Amount of (in Lakh)	Initial Rectification with surface Renewal (in Lakh)	5 Years Routine Maintenace (in Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MR-N19-20 Narkatiaganj/ 06	Matihani to Gamhariya	31808802100	3350/01.08.2019	1.95	78.057	53.439	17.95532	89/2020-21 Date- 25.06.2020	24.06.2021	07.06.2021	2421.8	25 mm	5%	0.00	0.00	53.439	
2	MR-N19-20 Narkatiaganj/ 06	Done Canal to Sithi	31808802080	3350/01.08.2019	2.44	102.0034	71.728	22.22107	89/2020-21 Date- 25.06.2020	24.06.2021	07.06.2021	2524.4	25 mm	5%	0.00	0.00	71.728	
		Total			4.39	180.0604	125.167	40.17639							0.00	0.00	125.167	

1 Signed Hard Copy and Soft Copy (in excel) of Recorded IRI is enclosed.

2 Up-to-date Physical Progress has been uploaded in MIS.

8/6/21

Executive Engineer
Rural Works Department
Works Division Narkatiaganj

8/6/21

Road Name-Matihani se Gamhariya

Date	Time	Section	Length	Bumps	Speed	OR		CATEGORY	IRI	Latitude	Longitude	Event
		No.	in km	in mm	Rate	mm/km	UIV	ROAD				
7/ 6/ 21	14: 10: 31	8	0.1	280	0	2800	2868	G	3.86	27.2682	84.4586	Normal
7/ 6/ 21	14: 10: 31	8	0.1	290	20.2	2900	2972	G	3.99	27.26871	84.45761	Normal
7/ 6/ 21	14: 11: 0	8	0.1	360	20.2	3600	3705	G	4.86	27.26958	84.45657	Normal
7/ 6/ 21	14: 11: 7	8	0.1	280	20.2	2800	2868	G	3.86	27.27045	84.45566	Normal
7/ 6/ 21	14: 11: 7	8	0.1	210	30.3	2100	2135	G	2.97	27.27073	84.45476	Normal
7/ 6/ 21	14: 11: 7	8	0.1	180	30.3	1800	1821	G	2.58	27.27093	84.45372	Normal
7/ 6/ 21	14: 11: 42	8	0.1	180	30.3	1800	1821	G	2.58	27.27089	84.45279	Normal
7/ 6/ 21	14: 12: 0	8	0.1	160	30.3	1600	1611	G	2.31	27.27065	84.4518	Normal
7/ 6/ 21	14: 12: 0	8	0.1	250	30.3	2500	2554	G	3.49	27.27067	84.45074	Normal
7/ 6/ 21	14: 12: 17	8	0.1	200	30.3	2000	2030	G	2.84	27.27081	84.44971	Normal
7/ 6/ 21	14: 12: 17	8	0.1	220	30.3	2200	2240	G	3.1	27.27097	84.44879	Normal
7/ 6/ 21	14: 12: 17	8	0.1	200	30.3	2000	2030	G	2.84	27.27096	84.44774	Normal
7/ 6/ 21	14: 12: 52	8	0.1	260	30.3	2600	2658	G	3.61	27.27126	84.44687	Normal
7/ 6/ 21	14: 13: 0	8	0.1	360	20.2	3600	3705	G	4.86	27.27112	84.44586	Normal
7/ 6/ 21	14: 13: 27	8	0.1	200	30.3	2000	2030	G	2.84	27.27104	84.44481	Normal
7/ 6/ 21	14: 7: 8	8	0.1	170	30.3	1700	1716	G	2.44	27.27054	84.45547	Normal
7/ 6/ 21	14: 7: 44	8	0.1	170	30.3	1700	1716	G	2.44	27.26997	84.4563	Normal
7/ 6/ 21	14: 7: 44	8	0.1	270	30.3	2700	2763	G	3.74	27.26929	84.45689	Normal
7/ 6/ 21	14: 8: 0	8	0.1	240	30.3	2400	2449	G	3.36	27.26876	84.45763	Normal
7/ 6/ 21	14: 13: 27	8	0.011	40	181.8	3636	3743	G	4.9	27.27104	84.44466	Normal

$Y = 0 * X ^ 2 + 1.047 * X - 63.36$
$X = 2581$
$Y = 2638$

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

IRI Value
Average IRI-2421.8

8.6.21
OE

8.6.21
AE

8/6/21
Executive Engineer
Rural Works Department
Works Divion Narktiyaganj

08/06/2

Steco Analyzer

Name of Customer :	Surat Kumar Kushwaha
Name of Work/ Road :	Matiyani se Gamhariya
Lab Job number	8
Date :	07-06-2021
Section No.	8

Test Date :	07-06-2021	Road Name :	Matiyani se Gamhariya
Machine No :	387	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :			Interval
Weather :		UIV Range :	611 To 5000 1000 mm/km
Start Location :	Matiyani	Dist Range :	0 To 2.1 0.1 * 1000 m
End Location :	Gamhariya	Equation :	Y = 0 * X ^ 2 + 1.047 * X - 63.36

Print | Generate Report and Graph | Redraw Graph | Map View

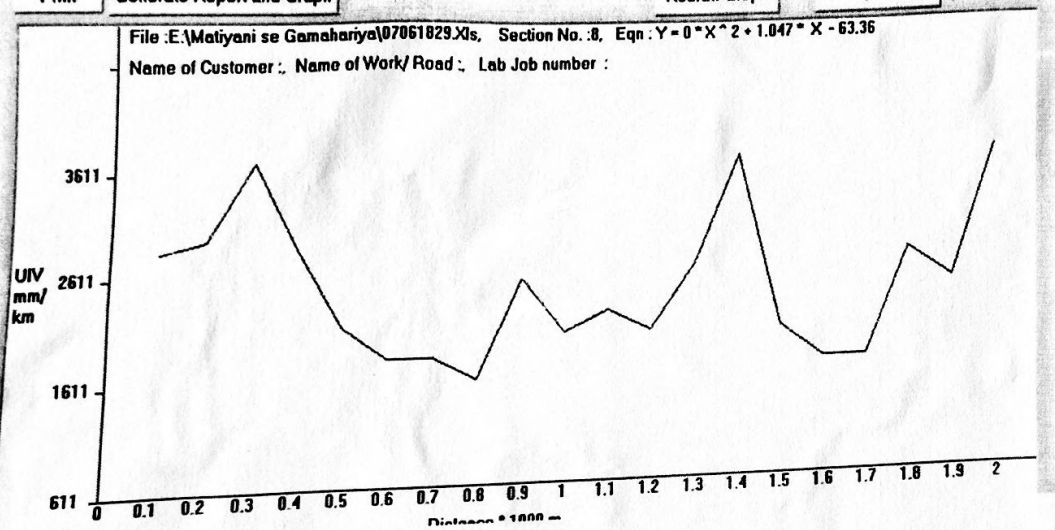

8.6.21
OB

8.6.21
AE

8/6/21
Executive Engineer
Rural Works Department
Works Divion Narktiyaganj

08/06/21
