कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग,कार्य प्रमण्डल,जमुई।

पत्रांक 872-अनु० जमुई,दिनांक 18.6.2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, जमुई ।

सेवा में,

नोडल पदाधिकारी,
3054(MR)
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषयः— शीर्ष MR New Maintenance Policy 2018 योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण का आवंटन उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि शीर्ष MR New Maintenance Policy 2018 योजना अन्तर्गत 5(पाँच) वर्षीय अनुरक्षण के पथों का पथवार मांगी जाने वाली आंवटन की सूची पत्र के साथ भवदीय के अवलोकनार्थ एवं आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

सूचनार्थ सादर समर्पित।

अनु0— यथोक्त

विश्वासभाजन

18/6/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल,जमुई।

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name :- RWD(WD), Jamui
Block Name:- Sikandara

1	Name of the Road	Navi Nagar to sahpur via Hathiya Road.
2	Batch No.	RM/JA/JAM/19/0002
3	Project ID	20804101016
4	Total Lenth of Road (in KM)	3.25
5	Length of Road to Meet Required Service Level [Completed length](in Km) [1]	3.25
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] **(in Lakh)**	26.19255
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule **(in Lakh)** [2]	1.30963

Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weighted Value for Payment Reduction (%)[4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANMENTS	0	10%	0.00
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00
V	VEGATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (IN Lakh) [5]				**0.00000**
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				**1.30963**

Date of inspection by E/I or his agent
Prepare by Contractor's self Control unit

Name and Designation of person inspecting road

Date 18/06/22

(Signature)

18/6/22

Signature of person inspecting road

Certify by E/I [signature] Date:-
Executive Engineer
Rural Works Department
Works Division, Jamui

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name Of Woks Division:- Jamui

1 Year (3rd Quarter)

Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:Navi Nagar to Sahpur via Hathiya road
(Package No.-RM/JA/JAM/19/0002)
Length of Road :-3.250Km
Inspector :- J.E RWD Sub Division :Sikandra

To:-
Executive Engineer
RWD, Works Division Jamui

Date:- 17.6.2022

Position :- J.E

	standard Of Work Item	Work	Unit OF Required in each Kilometere										
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	Comments
OM100	Sealed payment												
OM101	Pothole Patching	m^2	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m3	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patchibg Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Agreegate (SurfacebRavelling)	m^2	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m^2	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m^2	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m^2	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m^2	N.A	N.A	N.A	N.A							
107	Concreate pavement	m^3	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M^3	NIL	NIL	NIL	NIL							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage Including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M^3	Nil	Nil	Nil	Nil							Not Required
	Other activities(Whilw washing)	M^2	Nil	Nil	Nil	Nil							Not Required

	Standard Of Work Item	Work	Unit Of Required in each Kilometers										
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	Comments
DW400	Vegetation												
	Grass Control												
DW401	(a) Roadside General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear view Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
DW402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M^2	Nil	Nil	Nil	Nil							Not Required
DW500	Safety Signage and Road		Nil										Not Required
DW501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
DW502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
DW503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
DW504	Road Marking	M^2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

14/6/22

Executive Engineer,R.W.D. Works Division,Jamui

Work-Navi Nagar to sahpur via Hathiya Road.

Name of Contractor-Jitendra Kumar Singh

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
14/6/22	9:27:6	93	0.1	370	0	3700	3405	G	24.98759	85.90678	Normal
14/6/22	9:27:6	93	0.1	360	30.3	3600	3322	G	24.98735	85.90771	Normal
14/6/22	9:28:6	93	0.1	340	30.3	3400	3156	G	24.98704	85.90872	Normal
14/6/22	9:28:6	93	0.1	300	10.1	3000	2825	G	24.98663	85.909545	Normal
14/6/22	9:29:0	93	0.1	390	10.1	3900	3570	G	24.9864	85.910453	Normal
14/6/22	9:29:17	93	0.1	370	10.1	3700	3405	G	24.98644	85.91148	Normal
14/6/22	9:29:17	93	0.1	390	20.2	3900	3570	G	24.98673	85.912423	Normal
14/6/22	9:29:52	93	0.1	340	30.3	3400	3156	G	24.98673	85.91342	Normal
14/6/22	9:30:0	93	0.1	370	30.3	3700	3405	G	24.98689	85.91446	Normal
14/6/22	9:30:0	93	0.1	360	30.3	3600	3322	G	24.98699	85.91547	Normal
14/6/22	9:30:0	93	0.1	310	30.3	3100	2908	G	24.9869	85.916463	Normal
14/6/22	9:31:0	93	0.1	380	10.1	3800	3487	G	24.98671	85.917423	Normal
14/6/22	9:31:38	93	0.1	300	10.1	3000	2825	G	24.98657	85.91843	Normal
14/6/22	9:32:13	93	0.1	390	10.1	3900	3570	G	24.98667	85.919292	Normal
14/6/22	9:32:13	93	0.1	370	10.1	3700	3405	G	24.98654	85.920302	Normal
14/6/22	9:32:48	93	0.1	300	30.3	3000	2825	G	24.98638	85.921228	Normal
14/6/22	9:33:0	93	0.1	330	30.3	3300	3073	G	24.9862	85.922305	Normal
14/6/22	9:33:0	93	0.1	280	20.2	2800	2659	G	24.9857	85.922962	Normal
14/6/22	9:33:24	93	0.1	360	30.3	3600	3322	G	24.98481	85.923163	Normal
14/6/22	9:33:24	93	0.1	380	30.3	3800	3487	G	24.98392	85.92338	Normal
14/6/22	9:33:24	93	0.1	290	30.3	2900	2742	G	24.98328	85.92276	Normal
14/6/22	9:33:24	93	0.1	330	40.4	3300	3073	G	24.98255	85.922003	Normal
14/6/22	9:34:0	93	0.1	320	20.2	3200	2991	G	24.98211	85.922288	Normal
14/6/22	9:34:0	93	0.1	360	30.3	3600	3322	G	24.98219	85.923232	Normal
14/6/22	9:34:34	93	0.1	320	40.4	3200	2991	G	24.98191	85.924258	Normal
14/6/22	9:34:34	93	0.1	340	40.4	3400	3156	G	24.98176	85.925185	Normal
14/6/22	9:34:34	93	0.1	360	40.4	3600	3322	G	24.98162	85.926262	Normal
14/6/22	9:35:0	93	0.1	300	40.4	3000	2825	G	24.98147	85.927255	Normal
14/6/22	9:35:0	93	0.1	290	50.5	2900	2742	G	24.98127	85.928147	Normal
14/6/22	9:35:9	93	0.1	340	40.4	3400	3156	G	24.98102	85.929123	Normal
14/6/22	9:35:9	93	0.1	310	40.4	3100	2908	G	24.98085	85.93012	Normal
14/6/22	9:35:9	93	0.1	380	40.4	3800	3487	G	24.98067	85.931178	Normal
	Length		3.2		Total IRI		101412				
					Average IRI		3169.13				

Y = 0 * X ^ 2 + 0.828 * X + 341.6

X = 3800

Y = 3487

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

18/6/22

Executive Engineer
Rural Work Department
Works Division-Jamui

Analyzer

Name of Customer :	Jitendra Kumar Singh
Name of Work/ Road :	Navi Nagar to sahpur via Hathi
Lab Job number	
Date :	14-06-2022
Section No.	93

Test Date :	14-06-2022	Road Name :	Navi Nagar to sahpur via Hathi
Machine No :	399	Road Type :	(R) RURAL ROAD
Start S No :	0.000	Side :	
Start E No :	3.200		Interval
Weather :		UIV Range :	1659 To 5000 1000 mm/km
Start Location :		Dist Range :	0 To 3.3 0.1 *1000 m
End Location :		Equation :	Y = 0*X^2 + 0.828* X + 341.6

Print | Generate Report and Graph | Redraw Graph | Map View

File :D:\RITM\mr policy offline Reqution\Ashok\jitendra\Hathiya to Navinagar\14120936.Xls, Section No. :93, Eqn :
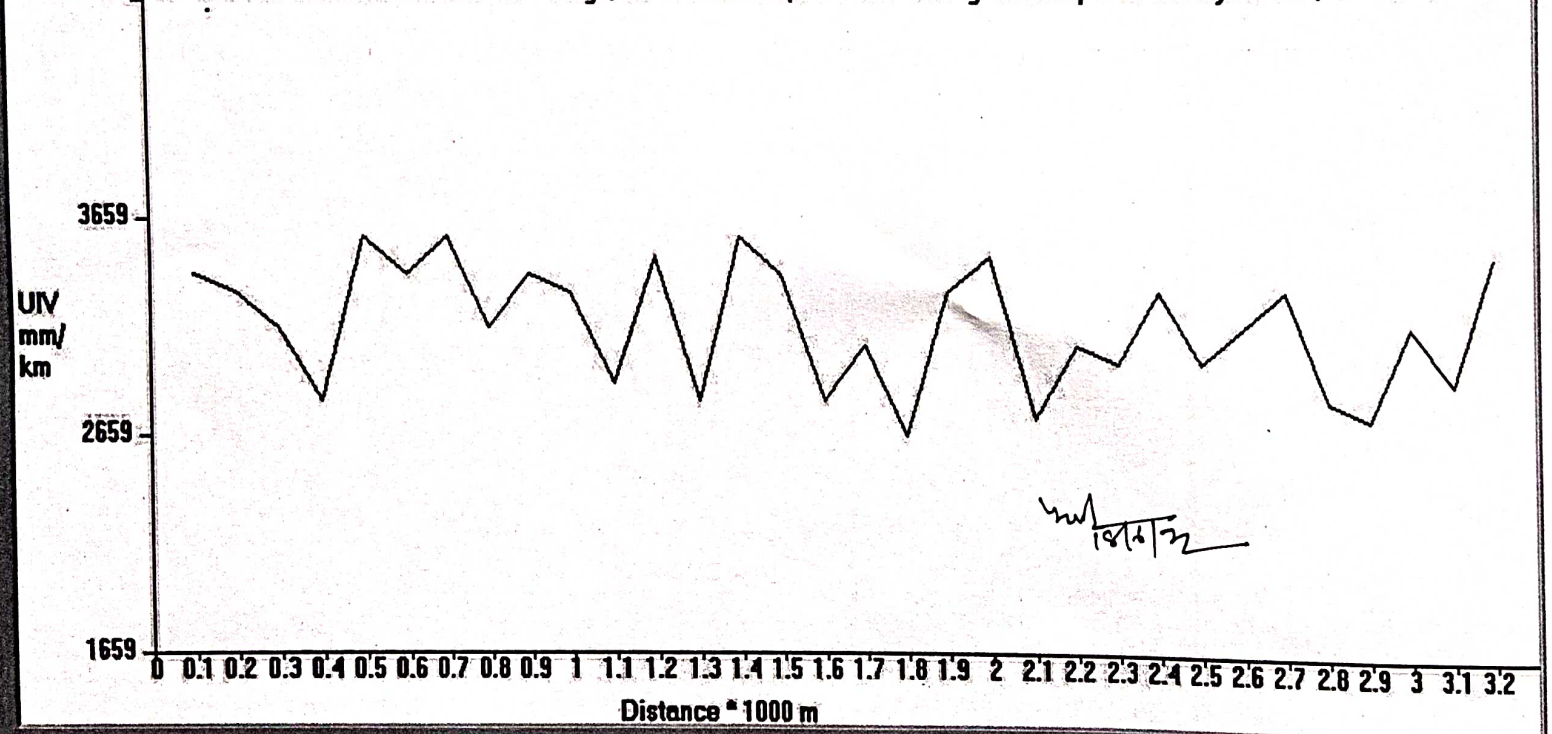
Name of Customer :Jitendra Kumar Singh, Name of Work/ Road :Navi Nagar to sahpur via Hathiya Road., Lab Job
