कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

पत्रांक :– 1007/अ/मुज0, दिनांक :– 27/6/2022

प्रेषकः– कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम।

सेवा में,
अपर मुख्य कार्यपालक पदाधिकारी
–सह–सचिव,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषयः– शीर्ष नई अनुरक्षण नीति–2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022–23 में व्यय हेतु आवंटन की मांग।

महाशय,

उपर्युक्त विषयक शीर्ष नई अनुरक्षण नीति–2018 (MR) अनुरक्षण अन्तर्गत वित्तीय वर्ष 2022–23 में व्यय हेतु आवंटन संलग्न विवरणी के अनुसार रु0 **82.00108** (बेरासी लाख एक सौ आठ) रुपये मात्र का आवंटन उपलब्ध कराने की कृपा की जाये, ताकि किये गये कार्य का भुगतान किया जा सके।

अनुलग्नक– 1. विहित प्रपत्र में अधियाचना।

विश्वासभाजन

27/6/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
मुजफ्फरपुर पश्चिम

Scanned with CamScanner

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Muzaffarpur West

Details					AA Details		Agreement								Actual Maintenance Expenditure								Current Maintenance Demand								
Name of Roads	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh)	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintanance Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance	Total	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
1	Pradhanmantri Road to Santosh Singh ke Ghar tak Path nirman Karya	RMMRUMRUZ/190018	31907401093	26/08/2020	30.582	12.090	27.44000	0.36565	1.24678	3.64896	1.56347	3.85582	10.88068	1.500	0.000	0.000	0.000	0.000	0.000	0.000	1.50	1340.000	0.54403	0.54403	0.54403	0.54403	0.54403			2.72017	
2	Improvement of Rasulpur to Mathurapur Pokhari Via House of Raju Babu and Kusheshwar Thakur	RMMRUMRUZ/190018	31907301041	04/03/2020	43.310	19.544	38.95000	1.08448	2.09768	5.55764	2.59046	6.19095	17.52121	2.196	0.000	0.000	0.000	0.000	0.000	0.000	2.20	2627.905	0.87606	0.87606	0.87606	0.87606	0.87606	0.87606	0.87606	6.13242	
3	Dhanarya - Subhanpur	RMMRUMRUZ/190018	31907202109	13/06/2020	52.780	24.940	47.34000	1.17606	2.53901	7.02360	3.17674	7.79479	21.71020	2.800	0.000	0.000	0.000	0.000	0.000	0.000	2.80	1628.000	1.08551	1.08551	1.08551	1.08551	1.08551			5.42755	
4	Kandh karja jhakra simar chemali devi asthan se NH102 singh tel dippo tak via karja transformor bhagwatpur pratmik vidyalya tak sadak nirman	RMMRUMRUZ/190018	31907301010	04/03/2020	45.866	22.237	41.23600	1.13466	2.33546	6.33539	2.87258	6.99168	19.66977	2.508	0.000	0.000	0.000	0.000	0.000	0.000	2.51	2197.000	0.98349	0.98349	0.98349	0.98349	0.98349	0.98349	0.98349	6.88442	
5	karja pul - mahammadpur urdu school path	RMMRUMRUZ/200005	NEA220002453	13/11/2020	59.316	25.664	60.11400	1.44707	2.84887	8.32662	3.60243	9.38551	25.61050	3.100	0.000	0.000	0.000	0.000	0.000	0.000	3.10	2009.000	1.28053	1.28053	1.28053	1.28053				5.12210	
6	bahilwara - karja path	RMMRUMRUZ/200005	NEA220002458	13/11/2020	155.811	69.131	158.52900	4.08302	7.79099	22.28061	9.78437	25.08155	69.02054	8.200	0.000	0.000	0.000	0.000	0.000	0.000	8.20	1996.000	3.45103	3.45103	3.45103	3.45103				13.80411	
7	PWD BARKAGAON DHALA - PANAPUR PATH	RMMRUMRUZ/200005	NEA220002476	13/11/2020	79.758	35.038	82.66400	2.10607	3.95833	11.20140	5.10104	12.59842	34.96526	4.100	0.000	0.000	0.000	0.000	0.000	0.000	4.10	2990.000	1.74826	1.74826	1.74826	1.74826				6.99305	
8	paroo shahmi tala - paroopath	RMMRUMRUZ/190027	NEA220002628	30/05/2020	22.513	8.954	20.14800	0.55689	0.85788	2.56727	1.14255	2.87173	7.99612	1.050	0.000	0.000	0.000	0.000	0.000	0.000	1.05	0638.000	0.39981	0.39981	0.39981	0.39981	0.39981	0.39981		2.39884	
9	Nimpatti - Kamalpura Main Road via gangai,Arar	RMMRUMRUZ/190027	NEA220002640	20/06/2020	84.540	37.080	76.02500	2.48733	3.68532	10.51576	4.80897	11.71947	33.21685	4.200	0.000	0.000	0.000	0.000	0.000	0.000	4.20	1315.000	1.66084	1.66084	1.66084	1.66084	1.66084			8.30421	
10	Paroo PWD Road Vishwakarma Chowk - North Koria	RMMRUMRUZ/190027	NEA220002844	13/05/2020	37.733	16.596	33.83800	1.05931	1.61416	4.75432	2.13547	5.31082	14.87208	1.930	0.000	0.000	0.000	0.000	0.000	0.000	1.93	1742.000	0.74360	0.74360	0.74360	0.74360	0.74360	0.74360		4.46162	
11	North of Majhaulia Chowk - Vahdinagar	RMMRUMRUZ/190027	NEA220002846	30/05/2020	51.790	23.640	46.52800	1.58044	2.34464	6.67726	3.06958	7.45271	21.12463	2.660	0.000	0.000	0.000	0.000	0.000	0.000	2.66	2021.000	1.05623	1.05623	1.05623	1.05623	1.05623	1.05623		6.33739	

Date of inspection by EE or his agent Prepared by
Contractor's self Control unit

EE 15/6/2022

Scanned with CamScanner

	...ods	Batch No.	Project ID	Actual Date of Completion	AA Details		Agreement								Actual Maintenance Expenditure						Length as per Bump Report	IRI As per bump Report	Current Maintenance Demand								Remarks
					Main Work Amount (in Lakh	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintanance Expenditure			0st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4th QTR Maintenance	5th QTR Maintenance	6th QTR Maintenance	7th QTR Maintenance	Total	
	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
12	Rampur Keshav - Mohmadpur Paroo	RM/MU/MUZ/190027	NEA220002647	15/06/2020	82.470	39.320	74.14600	2.49636	3.80668	11.28678	5.03564	12.60345	35.22891	4.600	0.000		0.000	0.000	0.000	0.000	4.60	1648.000	1.76145	1.76145	1.76145	1.76145	1.76145			8.80723	
13	Chochahi PWD Rd. - Chochahi	RM/MU/MUZ/190027	NEA220002651	15/06/2020	44.144	20.601	39.61200	1.35834	2.02929	5.85285	2.66152	6.52988	18.43188	2.350	0.000	0.000	0.000	0.000	0.000	0.000	2.35	1586.000	0.92159	0.92159	0.92159	0.92159	0.92159			4.60797	
	Total																													82.00108	

Executive Engineer
R.W.D. Works Division
Muzaffarpur West

Scanned with CamScanner

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division :- Muzaffarpur West

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From------- Pradhanmantri Road to Santosh Singh ke Ghar tak Path nirman Karya

To: Executive Engineer

RWD Works Division Muzaffarpur West Date:

Length of Road- 1.500 KM

Period :--------- From.....

Inspector:------ A.E RWD Sub Division, Sahebganj

Position: A.E

Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2	Nil	Nil	Nil	Nil							No. Pothole found.
OM102	Surface Depression and Rut Patching	m2	Nil	Nil	Nil	Nil							No Surface Depression and Rut Patching found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2	Nil	Nil	Nil	Nil							No Loss of Agreegate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2	Nil	Nil	Nil	Nil							No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2	Nil	Nil	Nil	Nil							No Crocodile Cracking found
OM105	Edge Repair	m2	Nil	Nil	Nil	Nil							No Edge Repair Required
OM106	Digouts	m2	N/A	N/A	N/A	N/A							
OM107	Concrete Pavement	m3	N/A	N/A	N/A	N/A							
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm	Nil	Nil	Nil	Nil							No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm	Nil	3%	2%	Nil							Defects rectified within stipulated time.
	(c) Holding Water	Lm	Nil	Nil	Nil	Nil							No Holding water found
OM202	Embankment Repair	No	Nil	Nil	Nil	Nil							No Embankment Repair Required
	Other Activite (Raincut)		3%	1%	2%								Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm	N/A	N/A	N/A	N/A							Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2	Nil	Nil	Nil	Nil							Not Required

Scanned with CamScanner

	Other activities (White Washing)	m2	Nil	Nil	Nil	Nil							Not Required
OM 400 Vegetation													
OM401	Grass Contorol												
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and shrub management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M2	Nil	Nil	Nil	Nil							Not Required
OM500	Safety Signage and Road												Not Required
OM501	Signs Maintenance	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N/A	N/A	N/A	N/A							Not Aplicable
OM503	Distance Stones	No	N/A	N/A	N/A	N/A							Not Aplicable
OM504	Road Marking	m2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

Bidder

AE 15/6/2022
Appendix

27/6/22
Executive Engineer, Rural Work Department,
Work Division, Muzaffarpur West

Scanned with CamScanner

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Pradhanmantri Road to Santosh Singh ke Ghar tak Path nirman Karya
2	Batch No.	RM/MU/MUZ/19/0018
3	Project ID	31507401003
4	Total Length of Road (in Km)	1.500
5	Length of Road to Meet Requred Service Level [Completed length] (in Km) (1)	1.500
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	10.88068
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.54403

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				**0.54403**

Date of inpection by E/1 or his agent Prepared by
Contractor's self Control unit

AE 15/6/2022

Name and Designation of person inspecting road
(Signature)

Date 15/6/2022

Signature of person inspecting road

Certify by E/1 (Signature) Date 27/6/22

Executive Engineer
Rular Work's Department
Work's Division Muzaffarpur West

Scanned with CamScanner

Name of Road - PMGSY Road to Santosh Singh Ke ghar Tak

	ime	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	UIV	IRI TEGORY ROAD		Latitude	ongitude	Event
	17: 1: 0	50	0.1	200	0	2000	1964	G	2.76	26.26777	84.95687	Normal
22	17: 1: 24	50	0.1	140	20.2	1400	1371	G	2	26.2685	84.95727	Normal
4/ 22	17: 1: 24	50	0.1	140	20.2	1400	1371	G	2	26.26915	84.95705	Normal
29/ 4/ 22	17: 2: 0	50	0.1	190	10.1	1900	1865	G	2.63	26.26938	84.95606	Normal
29/ 4/ 22	17: 2: 0	50	0.1	190	20.2	1900	1865	G	2.63	26.26954	84.95507	Normal
29/ 4/ 22	17: 2: 33	50	0.1	140	10.1	1400	1371	G	2	26.26969	84.95411	Normal
29/ 4/ 22	17: 3: 0	50	0.1	110	20.2	1100	1074	G	1.61	26.26985	84.9531	Normal
29/ 4/ 22	17: 3: 8	50	0.1	180	20.2	1800	1766	G	2.51	26.27042	84.95279	Normal
29/ 4/ 22	17: 3: 8	50	0.1	120	20.2	1200	1173	G	1.74	26.27125	84.95322	Normal
29/ 4/ 22	17: 3: 44	50	0.1	110	20.2	1100	1074	G	1.61	26.27211	84.95342	Normal
29/ 4/ 22	17: 4: 0	50	0.1	40	20.2	400	382	G	0.64	26.27258	84.95352	Normal
29/ 4/ 22	17: 4: 0	50	0.1	190	20.2	1900	1865	G	2.63	26.27287	84.9539	Normal
29/ 4/ 22	17: 5: 0	50	0.1	110	20.2	1100	1074	G	1.61	26.26985	84.95426	Normal
29/ 4/ 22	17: 5: 44	50	0.1	110	20.2	1100	1074	G	1.61	26.27211	84.95442	Normal
29/ 4/ 22	17: 6: 0	50	0.1	40	20.2	400	382	G	0.64	26.27258	84.95452	Normal
					AVG:-	1340						

Y = 0 * X ^ 2 + 0.989 * X - 13.58
X = 400
Y = 382

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

27/6/22

Executive Engineer
Rular Work's Department
Work's Division Muzaffarpur West

Scanned with CamScanner

File :G:\Rajneesh Kumar\PMGSY Road to Santosh Singh Ke ghar Tak\06100126.Xls, Section No. :50, Eqn : Y = 0 *

Name of Customer :, Name of Work/ Road :, Lab Job number :

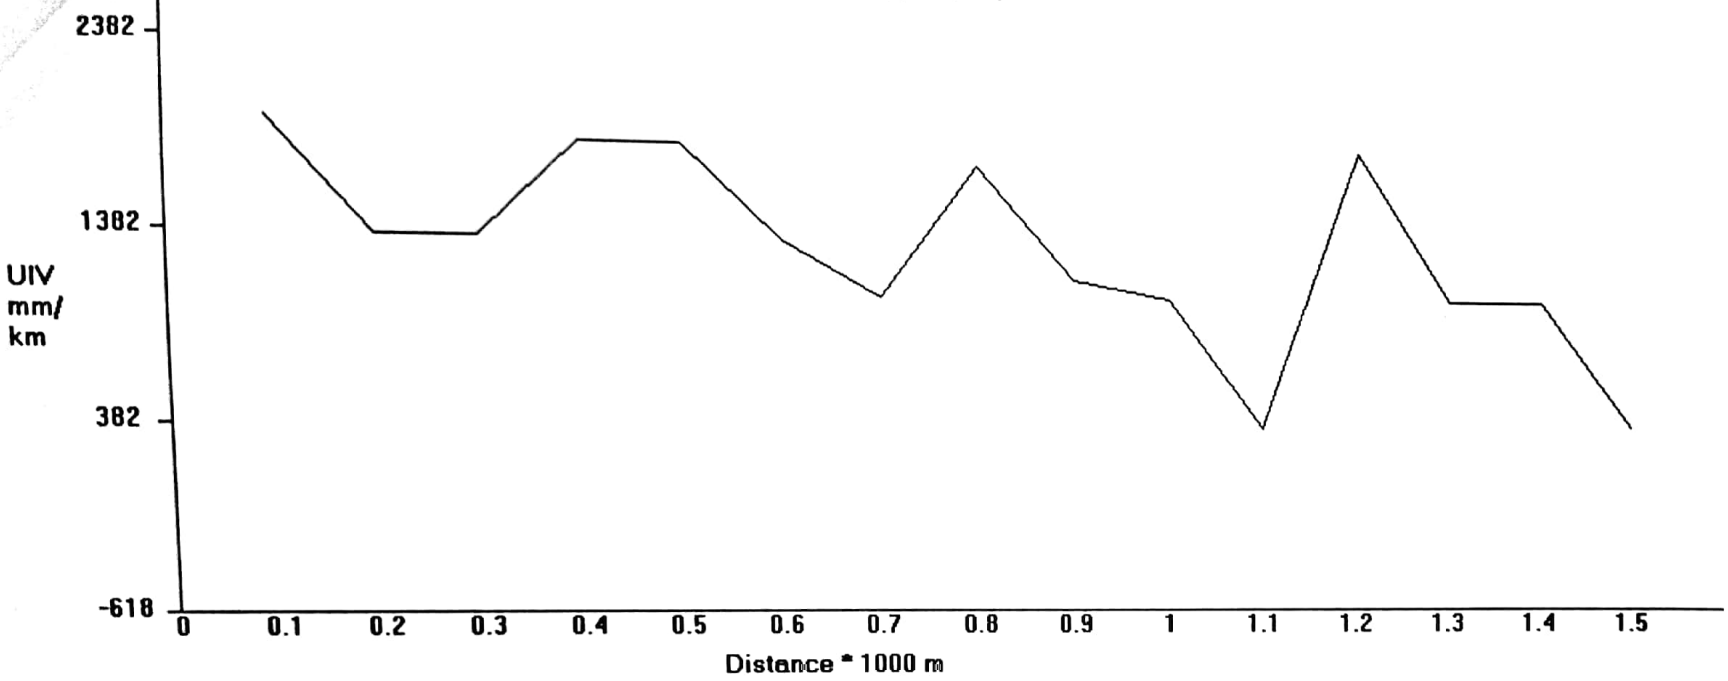

22/6/22

Executive Engineer
Rural Work's Department
Work's Division, Muzaffarpur West

Scanned with CamScanner
