कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

पत्रांक 1635 सोनपुर, दिनांक 29/9/22

प्रेषक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

सेवा में,

अपर मुख्य कार्यपालक
पदाधिकारी–सह–सचिव,
बिहार ग्रामीण पथ विकास अभिकरण
(BRRDA)
बिहार, पटना।

विषयः– **बिहार ग्रामीण पथ अनुरंक्षण निति–2018 योजनान्तर्गत अनुरंक्षण हेतु राशि की अधियाचना के संबंध में।**

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ अनुरंक्षण निति–2018 के अंतर्गत पथों का अनुरंक्षण की राशि की मांग **रुपये 5,22,531.00 (पॉच लाख बाईस हजार पॉच सौ एकतीस) मात्र** विहित प्रपत्र में अंकित कर आवश्यक कार्रवाई हेतु समर्पित किया जा रहा है।

अनुरोध है कि उपर्युक्त योजना में आवंटन उपलब्ध कराने की कृपा की जाये। कार्य का निरीक्षण किया गया कार्य संतोषप्रद है। उक्त पथ में ए0टी0आर0 लंबित नही है।

अनु0:–**Standard Formate for Roads**
Quarterly Statement

विश्वासभाजन

29/9/22

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल सोनपुर

29/9/22

FORM GER 19-A

(See Government of India's Decision (I) below Rule-150

Form of Utilization Certificate up to the month of **September-2022**

PIU:- E.E.,R.W.D. Works Division Sonepur.

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs Rs.)	Amount Received (in lac Rs.)	Particulars
1	2	3	4	5
1	**Construction of Rural Roads under New Maintenance Policy-18 (Maintenance)**		**66.42492**	Certified that out of Rs **66.42492** lakh received during the years 2020-21 to 2022-23 in favour of E.E.R.W.D. works division Sonepur a sum of Rs **5.93449** Lakh has been utilized for the purpose of **New Maintenance Policy-18 (Maintenance)** Scheme as given in the margin for which it was sanctioned and that the balance of Rs **60.49043 Lakh** remaining unutilized at the end of the period under report.

Certified that I have satisfied that the condition of which the grants-in-aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually for the purpose for which it was sanctioned.

Kind of Checks:-

i. Words have been supervised be Executive/superintending Engineer.
ii. Periodical inspection has been conducted by Executive Engineer/ superintending Engineer.
iii. Construction material has been tested.
iv. Measurements have been recorded in the MBS and test conducted by the Assistant Engineer/ Executive Engineer.
v. All other nodal formalities have been observed.

3 physical Progress achieved-

I. Construction of Road Works.
II. Construction of CD works

29.9.2022

D.A.O
R.W.D. Works Division Sonpur.

29/09/22

EXECUTIVE ENGINEER
R.W.D. Works Division Sonpur.

29/9/22

Maintenance Requisition Formate for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018

Works Division:- SONPUR

Road Details					AA Details		Agreement								Actual Maintenance Expenditure								Current Maintenance Demand					
Sl. No.	Name of Raods	Batch No.	Project ID	Actual Date of Completion	Main Work Amount (in Lakh	Maintenance Amount (in lakh)	Main Work Amount (in Lakh)	Agreement-1	Agreement-2	Agreement-3	Agreement-4	Agreement-5	Total Maintenance	Length (in KM)	1st. Year Maintenance	2nd. Year Maintenance	3rd. Year Maintenance	4th Year Maintenance	5th Year Maintenance	Total Maintananc e Expenditure	Length as per Bump Report	IRI As per bump Report	1st QTR Maintenance	2nd QTR Maintenance	3rd QTR Maintenance	4 th QTR Maintenance	Total	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25		26	30	31
1	Chapra jilantargat maker prakhand panchayat kaituka nandan gram sultanganj pradhanmantri sarak pull se dakchin noniya toli tak path nirmaan.	RM/SA/SON /19/0007	31306405003	15-01-2021	21.00200	9.55500	16.59600	0.60303	0.94688	2.28005	1.12961	2.57135	7.53092	0.900	0.000	0.000	0.000	0.000	0.000	0.000	0.900	1148	0.37655	0.37655	0.37655	0.00000	**1.12964**	
2	Maker PMGSY road to Dih Siraman	RM/SA/SON /19/0007	31306201025	15-01-2021	36.55500	18.54600	30.67100	1.36637	1.89960	4.38810	2.37263	4.70656	14.73326	1.500	0.000	0.000	0.000	0.000	0.000	0.000	1.500	2422	0.73666	0.73666	0.73666	0.00000	**2.20999**	
3	Maker - Dihi Dadanpur	RM/SA/SON /19/0007	NEA220002083	15-01-2021	32.45800	16.02100	27.18800	1.17526	1.63643	3.64105	2.04591	4.07259	12.57124	1.300	0.000	0.000	0.000	0.000	0.000	0.000	1.300	1619	0.62856	0.62856	0.62856	0.00000	**1.88569**	
	Total ----------																										**5.22531**	

29/09/22

Executive Engineer
R.W.D. Works Division
SONPUR

27/9/22

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

1	Name of the Road	Chapra jilantargat maker prakhand panchayat kaituka nandan gram sultanganj pradhanmantri sarak pull se dakchin noniya toli tak path nirmaan.
2	Batch No.	RM/SA/SON/20/0010
3	Project ID	31306405003
4	Total Length of Road (in Km)	0.900
5	Length of Road to Meet Requred Service Level [Completed length] (in Km) (1)	0.900
6	No. of Total Quarter (ie 3 Months as a unit) in 5 years	20
7	Ordinary Maintenance Cost as per Schedule (Agreement Amount for Maintenance) (in Lakh)	7.53092
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) (2)	0.37655

Compliance Criteria	Standard Job Description	Non-Compliant		Reduction Payment (6) = (3) / (1) * (2) * (4)
		Length Non Compliant (3)	Weighted Value for Payment Reduction (%) (4)	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00000
II	SHOULDERS AND EMBANMENTS	0	10%	0.00000
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0.00000
IV	SIGNAGE AND ROAD SAFETY	0	10%	0.00000
V	VEGATAION		5%	0.00000
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) [5]				0.00000
TO BE PAID FOR THE QUARTER/DEMAND (in Lakh) [6]				**0.37655**

Date of inpection by E/1 or his agent Prepared by
Contractor's self Control unit

Name and Designation of person inspecting road
(Signature)

Date

Signature of person inspecting road

26/09/2022
J.E.

26/09/22

Certify by E/I (signature) Date

29/09/22

Executive Engineer
Rural Works Department
Work Division, Sonepur

...ion Format for Scheme Head - MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

...ame of Works Division :- Sonpur | III Quater

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- Chapra jilantargat maker prakhand panchayat kaituka nandan gram sultanganj pradhanmantri sarak pull se dakchin noniya toli tak path nirmaan.
Length of Road: 0.900 KM
Periode : From.....
Inspector: A.E RWD Sub Division, Maker

To: Executive Engineer
RWD Works Division Sonpur Date:

Position: A.E

Standard Work item		Work	Units of work required in each kilometre										Comments
S No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	m2											No. Pothole found.
OM102	Surface Depression and Rut Patching	m2											No Surface Depression and Rut Patching found
OM103`	Crack Sealing	Lm											No Crack Sealing found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	m2											No Loss of Agreegate (Surface Ravelling) found
	(b) Bleeding/Flushing	m2											No Bleeding/Flushing Required
	(c) Crocodile Cracking	m2											No Crocodile Cracking found
OM105	Edge Repair	m2											No Edge Repair Required
OM106	Digouts	m2											
OM107	Concrete Pavement	m3											
	Other activities	Lm											
OM200 Shoulder													
OM201	Unsealed Shoulder	No											
	(a) Edge Drop off	Lm											No Edge Drop off Required
	(b) Roughness, Scouring or Potholes	Lm											Not required
	(c) Holding Water	Lm											No Holding water found
OM202	Embankment Repair	No											No Embankment Repair Required
	Other Activite (Raincut)												Defects rectified within stipulated time.
OM 300 Drainage including culverts major													
OM301	Surface Drains & Verge	Lm											Not Required
OM302	Culvert Cleaning	Lm											Culvert maintain within stipulated time
OM303	Culvert and Pit repair	m2											Not Required

26/09/2022 JE, Maker

28/9/22 AE

29/09/22

	er activities (White Washing)	m2												Not Required
	OM 400 Vegetation													
OM401	Grass Contorol													
	a) Roadside-General Tidy	Ha												Not Required
	b) Clear near Safety signs, kilometre posts and roadside furniture	Ha												Not Required
OM402	Tree and shrub management	No												Not Required
	Cutting trees	No												Not Required
	Cutting Shrubs	No												Not Required
	Other activities (Trimming of Grass)	M2												**Not Required**
OM500	Safety Signage and Road													Not Required
OM501	Signs Maintenance	No												Not Required
OM502	Guard Stones	Lm												Not Aplicable
OM503	Distance Stones	No												Not Aplicable
OM504	Road Marking	m2												Not Required
	Other activities													

Bidder

26/09/2022

J.E. 26/9/22

Appendix

26/9/22

Executive Engineer, Rural Work Department, Work Division, Sonpur

29/09/22

Executive Engineer
Rural Works Department
Work Division, Sonepur

Name of work :	Chapra jilantargat maker prakhand panchayat kaituka nandan gram sultanganj pradhanmantri sarak pull se dakchin noniya toli tak path nirmaan.
Name of customer :	Niraj Kumar

					(R)Rural Road										
					Good		Average			Poor					
Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
19/08/22	16:11:39	73	100	100	13.0 cm	7.2 Km/Hr	1300.0 mm/Km	1334	1.95	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:12:00	73	100	200	9.0 cm	17.3 Km/Hr	900.0 mm/Km	962	1.46	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:12:18	73	100	300	9.0 cm	19.8 Km/Hr	900.0 mm/Km	962	1.46	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:12:34	73	100	400	7.0 cm	22.2 Km/Hr	700.0 mm/Km	777	1.21	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:12:50	73	100	500	12.0 cm	22.5 Km/Hr	1200.0 mm/Km	1241	1.83	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:13:16	73	100	600	12.0 cm	13.7 Km/Hr	1200.0 mm/Km	1241	1.83	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:13:45	73	100	700	10.0 cm	12.4 Km/Hr	1000.0 mm/Km	1055	1.59	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:14:29	73	100	800	13.0 cm	8.1 Km/Hr	1300.0 mm/Km	1334	1.95	Good	25.9544192	N	85.0110559	E	Normal
19/08/22	16:14:42	73	100	900	14.0 cm	27.5 Km/Hr	1400.0 mm/Km	1426	2.07	Good	25.9544192	N	85.0110559	E	Normal

26/09/2022
J.E. Maker

28/9/22

29/09/22

Executive Engineer
Rural Works Department
Work Division, Sonepur

ner: Niraj Kumar , Machine no: 19205 , Road: Chapra jilantargat maker prakhand panchayat kaituka nandan gram sultanganj pradhanmantri sarak pull se dakchin noniya toli tak path nirmaan. , Date: 19-08-22 , Section No: 73 , Equation: Y

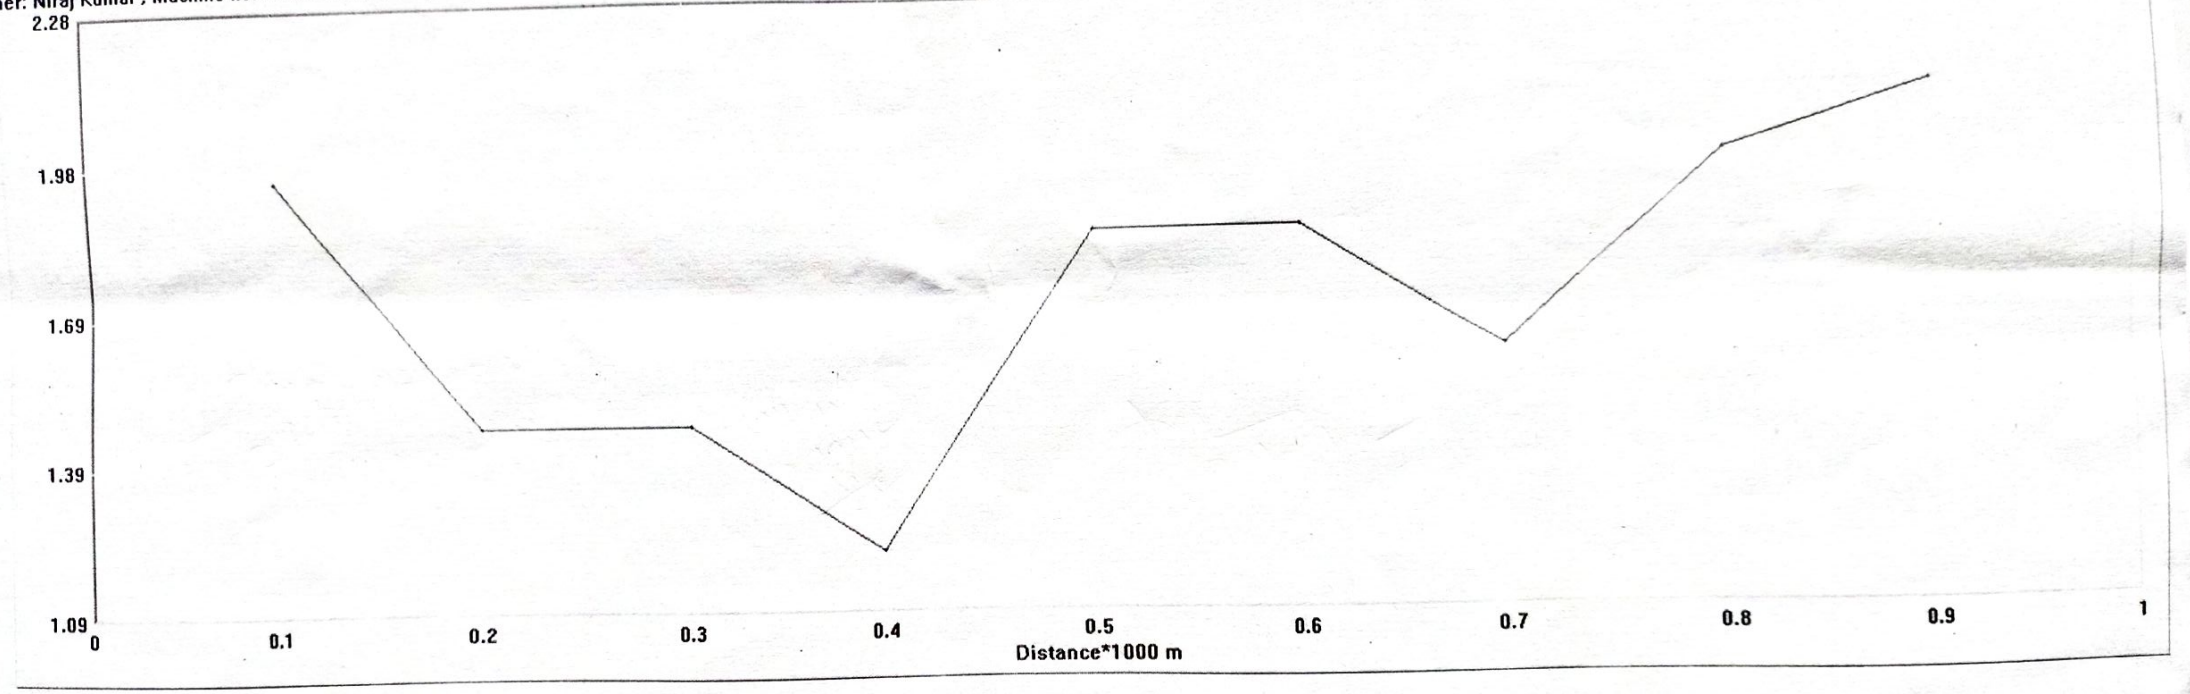

26/09/2022
J.E. Mukesh

26/9/22
AE

29/09/22
Executive Engineer
Rural Works Department
Work Division, Sonepur
