कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमंडल, गोपालगंज–2

पत्रांक 1631 गोपालगंज, दिनांक 3/9/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, गोपालगंज–2

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी,
–सह– सचिव, बिहार ग्रामीण पथ विकास एजेन्सी,
ग्रामीण कार्य विभाग, बिहार, पटना।

विषयः– **नई अनुरक्षण नीति 2018 शीर्ष 3054 अन्तर्गत पंचवर्षीय अनुरक्षण मद में आवंटन उपलब्ध कराने के संबंध में।**

महाशय,

उपर्युक्त विषयक योजनान्तर्गत कराये गये कार्य के भुगतान हेतु संलग्न मांग पत्र के अनुसार आवंटन उपलब्ध कराने की कृपा की जाए।

विश्वासभाजन

02/09/22
कार्यपालक अभियंता
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, गोपालगंज–2

अनु0– यथोक्त।

02.9.22

STANDRAD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- R.W.D. Gopalganj-2

Quarter :- 2nd (First Year – 2nd Quarter) Period :- 13.07.2021 12.10.2021

1	Name of the Road	Siwan Sarafara PWD Path to Vishambharpur Bargachhiya
2	Batch No	RM/GO/GOP/20/0006
3	Project ID	31406901011
4	Total Lenghth of Road (in Km)	5.215
5	Length of Road to Meet Requrcd Service level [Completed length] (in Km) [1]	5.215
6	No. of total Quarter (ie 3 Months as a unit) in 5 years	20
7	Ordinary Maintenance Cost as per Schedule [Agreement amount of Maintance] (in Lakh)	~~53.07045~~ 52.486675
8	Quarterly Payment :1/20 of Ordinary Maintenance Cost as per Schedule (in Likh) [2]	~~2.65352~~ 2.6243335

Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weightage Value for Payment Reduction % [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANKMENT	0	10%	0
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGITATION	0	5%	0
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	0.00
TO BE PAID FOR QUARTER/DEMAND (in Lakh)			[6]	~~2.64589~~ =2.6243335

Surath Singh
Date of inspection by E/I or his agent
Prepared by Contractor's Self Control unit

27/8/22 Rajesh 27/08/22
Name and Designation of Person inspecting road
JE, Mangliya

Date :-

Signature

Signature of Person Inspecting road

03/09/22
Executive Engineer
RWD (W) Division
Gopalganj-2
Certify by E/I (Signature) Date:

Scanned with CamScanner

Requisition Format for Scheme Head- MR (3054) Under Bihar Rural Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

Name of Works Division:- **Gopalganj-2** Quarter:- **2nd** [First Year – 2nd Quarter]

Government of Bihar
OM01
Rural works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From- **Siwan Sarafara PWD Path to Vishambharpur Bargachhiya**
(Project Id:- 31406901011, Batch No.- RM/GO/GOP/20/0006)
Length of Road:- 5.215 Km
Period:- From **13.07.2021 to 12.10.2021**
Inspector : A.E RWD Sub Division Manjha

To: **Executive Engineer**
RWD Works Division, Gopalganj-2
Position: EE
Date -

Standard Work item		Work	Units of work required in each kilometre										Comments
Sl. No.	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM100 Sealed Pavement													
OM101	Pothole Patching	M^2	Nil	Nil	Nil	Nil	Nil	Nil					No Pothole Found
OM102	Surface Depression and Rut Patching	M^3	Nil	Nil	Nil	Nil	Nil	Nil					No Surface depression & Rut Patching Found
OM103	Crack Sealing	RM	Nil	Nil	Nil	Nil	Nil	Nil					No Crack Found
OM104	Surface Treatment												
	(a) Loss of Aggregate (Surface Ravelling)	M^2	Nil	Nil	Nil	Nil	Nil	Nil					No Loss of Aggregate(surface ravelling) Found
	(b) Bleeding/Flusing	M^2	Nil	Nil	Nil	Nil	Nil	Nil					Bleeding & Flusing not found
	(c) Crocodile Cracking	M^2	Nil	Nil	Nil	Nil	Nil	Nil					Not Found
OM105	Edge Repair	M^2	Nil	Nil	Nil	Nil	Nil	Nil					Edge repair not required
OM106	Digouts Repair	M^3	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.					
OM107	Repair of Concrete Pavement	M^2	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.					
	Repair old Joint Selant	RM	Nil	Nil	Nil	Nil	Nil	Nil					old joint are in good condition
OM200 Shoulder													
OM201	Unscaled Shoulder repair												
	(a) Edge Drop off	RM	Nil	Nil	Nil	Nil	Nil	Nil					no Edge drop off Required
	(b) Roughness, Scouring or Potholes	RM	Nil	Nil	Nil	Nil	Nil	Nil					Not required
	(c) Holding Water	RM	Nil	Nil	Nil	Nil	Nil	Nil					existance not found
OM202	Embankment Repair	M^3	Nil	Nil	Nil	Nil	Nil	Nil					Not required
	Other Activite (Raincut)	M^3	Nil	Nil	Nil	Nil	Nil	Nil					Not required

Laksh Grih Contract Pvt. Ltd.

Suresh Singh

27/08/22
JE/Manjha

27/8/22
AE

02/09/22
Executive Engineer
Rural Works Department
Works Division, Gopalganj

Standard Work item		Work	Units of work required in each kilometre										Comments
Sl. No	Name	Units	1	2	3	4	5	6	7	8	9	10	
OM300 Drainage Including culverts major and minor Bridge													
OM301	Surface Drains & Verge	RM	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.					not required
OM302	Culvert Cleaning	Each	Nil	Nil	Nil	Nil	Nil	Nil					not required
OM303	Culvert and Pit repair	Each	Nil	Nil	Nil	Nil	Nil	Nil					not required
	Other activities (White Washing)	M^2	Nil	Nil	Nil	Nil	Nil	Nil					
OM400 Vegetation													
OM401	Grass Contorol												
	a) Roadside-General Tidy	Ha	Nil	Nil	Nil	Nil	Nil	Nil					not required
	b) Clear near Safety signs, kilometre posts and roadside furniture.	Ha	Nil	Nil	Nil	Nil	Nil	Nil					not required
OM402	Tree and shrub management	No	Nil	Nil	Nil	Nil	Nil	Nil					not required
	Cutting trees	No	Nil	Nil	Nil	Nil	Nil	Nil					not required
	Cutting Shrubs	No	Nil	Nil	Nil	Nil	Nil	Nil					not required
	Other activities (Trimming of (Grass)	M^2	Nil	Nil	Nil	Nil	Nil	Nil					not required
OM500 Safety Sign and Road													
OM501	Sign Maintenance	KM	Nil	Nil	Nil	Nil	Nil	Nil					not required
OM502	Guard Stones Paintings	M^2	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.					not required
OM503	Distance Stones (KM & 200 M Post)	KM	N.A.	N.A.	N.A.	N.A.	N.A.	N.A.					not required
OM504	Road Marking	M^2	Nil	Nil	Nil	Nil	Nil	Nil					not required
	Other activities												

Laksh Grih Contract Pvt. Ltd.

Surat Singh

Signature of Contractor/Authorized Repersentative

27/08/22

J.E.

27/8/22

A.E.

Executive Engineer,
Rural Works Department,
Works Division Gopalganj-2

Place:- Gopalganj

Date :-

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
27/ 8/ 22	14:05:12	88	0.1	350	10.1	3500	3514	G	26.34838	84.45642	Noaml
27/ 8/ 22	14:05:38	88	0.1	300	10.1	3000	3034	G	26.34826	84.45694	Speed Breaker
27/ 8/ 22	14:06:04	88	0.1	290	10.1	2900	2956	G	26.34842	84.45766	Normal
27/ 8/ 22	14:06:30	88	0.1	270	20.2	2700	2775	G	26.34891	84.45896	Curve
27/ 8/ 22	14:06:56	88	0.1	290	20.2	2900	2956	G	26.34891	84.45896	Normal
27/ 8/ 22	14:07:22	88	0.1	310	20.2	3100	3165	G	26.34974	84.46007	Culvert
27/ 8/ 22	14:07:48	88	0.1	360	10.1	3600	3621	G	26.35086	84.46084	Normal
27/ 8/ 22	14:08:14	88	0.1	200	0	2000	2000	G	26.35025	84.4617	Curve
27/ 8/ 22	14:08:40	88	0.1	290	10.1	2900	2948	G	26.35025	84.4617	Normal
27/ 8/ 22	14:09:06	88	0.1	320	10.1	3200	3293	G	26.34937	84.46337	Normal
27/ 8/ 22	14:09:32	88	0.1	330	10.1	330	3379	G	26.34924	84.46365	Bridge
27/ 8/ 22	14:09:58	88	0.1	280	10.1	2800	2817	G	26.34876	84.46497	Curve
27/ 8/ 22	14:10:24	88	0.1	380	10.1	3800	3817	G	26.34933	84.4653	Normal
27/ 8/ 22	14:10:50	88	0.1	290	20.2	2900	2948	G	26.34933	84.4653	Normal
27/ 8/ 22	14:11:16	88	0.1	260	20.2	2600	2603	G	26.34933	84.4653	Culvert
27/ 8/ 22	14:11:42	88	0.1	360	20.2	3600	3687	G	26.34933	84.4653	Normal
27/ 8/ 22	14:12:08	88	0.1	320	20.2	3200	3293	G	26.34933	84.4653	Normal
27/ 8/ 22	14:12:34	88	0.1	340	20.2	3400	3412	G	26.3542	84.46658	Culvert
27/ 8/ 22	14:13:00	88	0.1	300	20.2	3000	3034	G	26.3542	84.46658	Normal
27/ 8/ 22	14:13:26	88	0.1	320	20.2	3200	3214	G	26.35482	84.46773	Normal
27/ 8/ 22	14:13:52	88	0.1	230	10.1	2300	2344	G	26.35482	84.46773	Nomal
27/ 8/ 22	14:14:18	88	0.1	330	10.1	3300	3379	G	2635482	84.46773	Speed Breaker
27/ 8/ 22	14:14:44	88	0.1	290	10.1	2900	2987	G	26.35643	84.47547	Curve
27/ 8/ 22	14:15:10	88	0.1	280	10.1	2800	2862	G	26.35643	84.47547	Normal
27/ 8/ 22	14:15:36	88	0.1	290	20.2	2900	2948	G	26.35643	84.47547	Curve
27/ 8/ 22	14:16:02	88	0.1	330	20.2	3300	3293	G	26.35643	84.47598	Curve
27/ 8/ 22	14:16:28	88	0.1	260	30.3	2600	2689	G	26.35643	84.47687	Normal
27/ 8/ 22	14:16:54	88	0.1	250	20.2	2500	2517	G	26.35643	84.47874	Curve
27/ 8/ 22	14:17:20	88	0.1	260	20.2	2600	2689	G	26.35643	84.47415	Curve
27/ 8/ 22	14:17:46	88	0.1	240	30.3	2500	2574	G	26.35643	84.47498	Normol
27/ 8/ 22	14:18:12	88	0.1	220	20.2	2200	2212	G	26.35643	84.47598	Curve

Y = 0 * X ^ 2 + 0.862 * X + 448.5
X = 2800
Y =2862

(R) RURAL ROAD
Good Average Poor

27/08/22
JE, Mangliu

27/8/22

Executive Engineer
Rural Works Department
Works Division, Gopalgani

27/ 8/ 22	14:18:38	88	0.1	230	10.1	2300	2344	G	26.35643	84.47612	Curve
27/ 8/ 22	14:19:04	88	0.1	200	10.1	2000	2086	G	26.35269	84.47621	Curve
27/ 8/ 22	14:19:30	88	0.1	370	10.1	3700	3748	G	26.35226	84.47677	curve
27/ 8/ 22	14:19:56	88	0.1	310	20.2	3100	3175	G	26.35226	84.47677	Nomlal
27/ 8/ 22	14:20:22	88	0.1	350	30.3	3500	3548	G	26.35226	84.47677	Culvert
27/ 8/ 22	14:20:48	88	0.1	360	30.3	3600	3604	G	26.35226	84.47677	Culvert
27/ 8/ 22	14:21:14	88	0.1	260	20.2	2600	2689	G	26.35226	84.47677	curve
27/ 8/ 22	14:21:40	88	0.1	360	20.2	3600	3603	G	26.35226	84.47677	Normal
27/ 8/ 22	14:22:06	88	0.1	300	30.3	3000	3034	G	26.35226	84.47677	Normal
27/ 8/ 22	14:22:32	88	0.1	380	30.3	3800	3862	G	26.35226	84.47677	curve
27/ 8/ 22	14:22:58	88	0.1	280	20.2	2800	2862	G	26.35226	84.47677	curve
27/ 8/ 22	14:23:24	88	0.1	280	10.1	2800	2862	G	26.35226	84.47677	Speed Breaker
27/ 8/ 22	14:23:50	88	0.1	250	10.1	2500	2603	G	26.35226	84.47677	Normal
27/ 8/ 22	14:24:16	88	0.1	260	10.1	2600	2641	G	26.35226	84.47677	Normal
27/ 8/ 22	14:24:42	88	0.1	220	20.2	2200	2250	G	26.35226	84.47677	Normal
27/ 8/ 22	14:25:08	88	0.1	370	10.1	3700	3748	G	26.35226	84.47677	curve
27/ 8/ 22	14:25:34	88	0.1	290	20.2	2900	2956	G	26.35226	84.47677	Culvert
27/ 8/ 22	14:26:00	88	0.1	310	30.3	3100	3165	G	26.35226	84.47677	Normal
27/ 8/ 22	14:26:26	88	0.1	350	30.3	3500	3584	G	26.35226	84.47677	Culvert
27/ 8/ 22	14:26:52	88	0.1	280	20.2	2800	2862	G	26.35226	84.47677	Normal
27/ 8/ 22	14:27:18	88	0.1	280	10.1	2800	2862	G	26.35226	84.47677	Normal
AVERAGE							3020.15				

27/08/22
JE, Mayjua

27/8/22
AE.

23/8/22
Executive Engineer
Rural Works Department
Works Division, Gopalganj

File :D:\GRAPH\LAKSH GRIH\Bishambharpur Road\New folder\BISHAMBHARPUR.xlsx. Section No. :88, Eqn :test

Name of Customer :Laksh Grih Contract Pvt Ltd. Name of Work/ Road :Siwan Sarfara PWD Road Bishambharpur

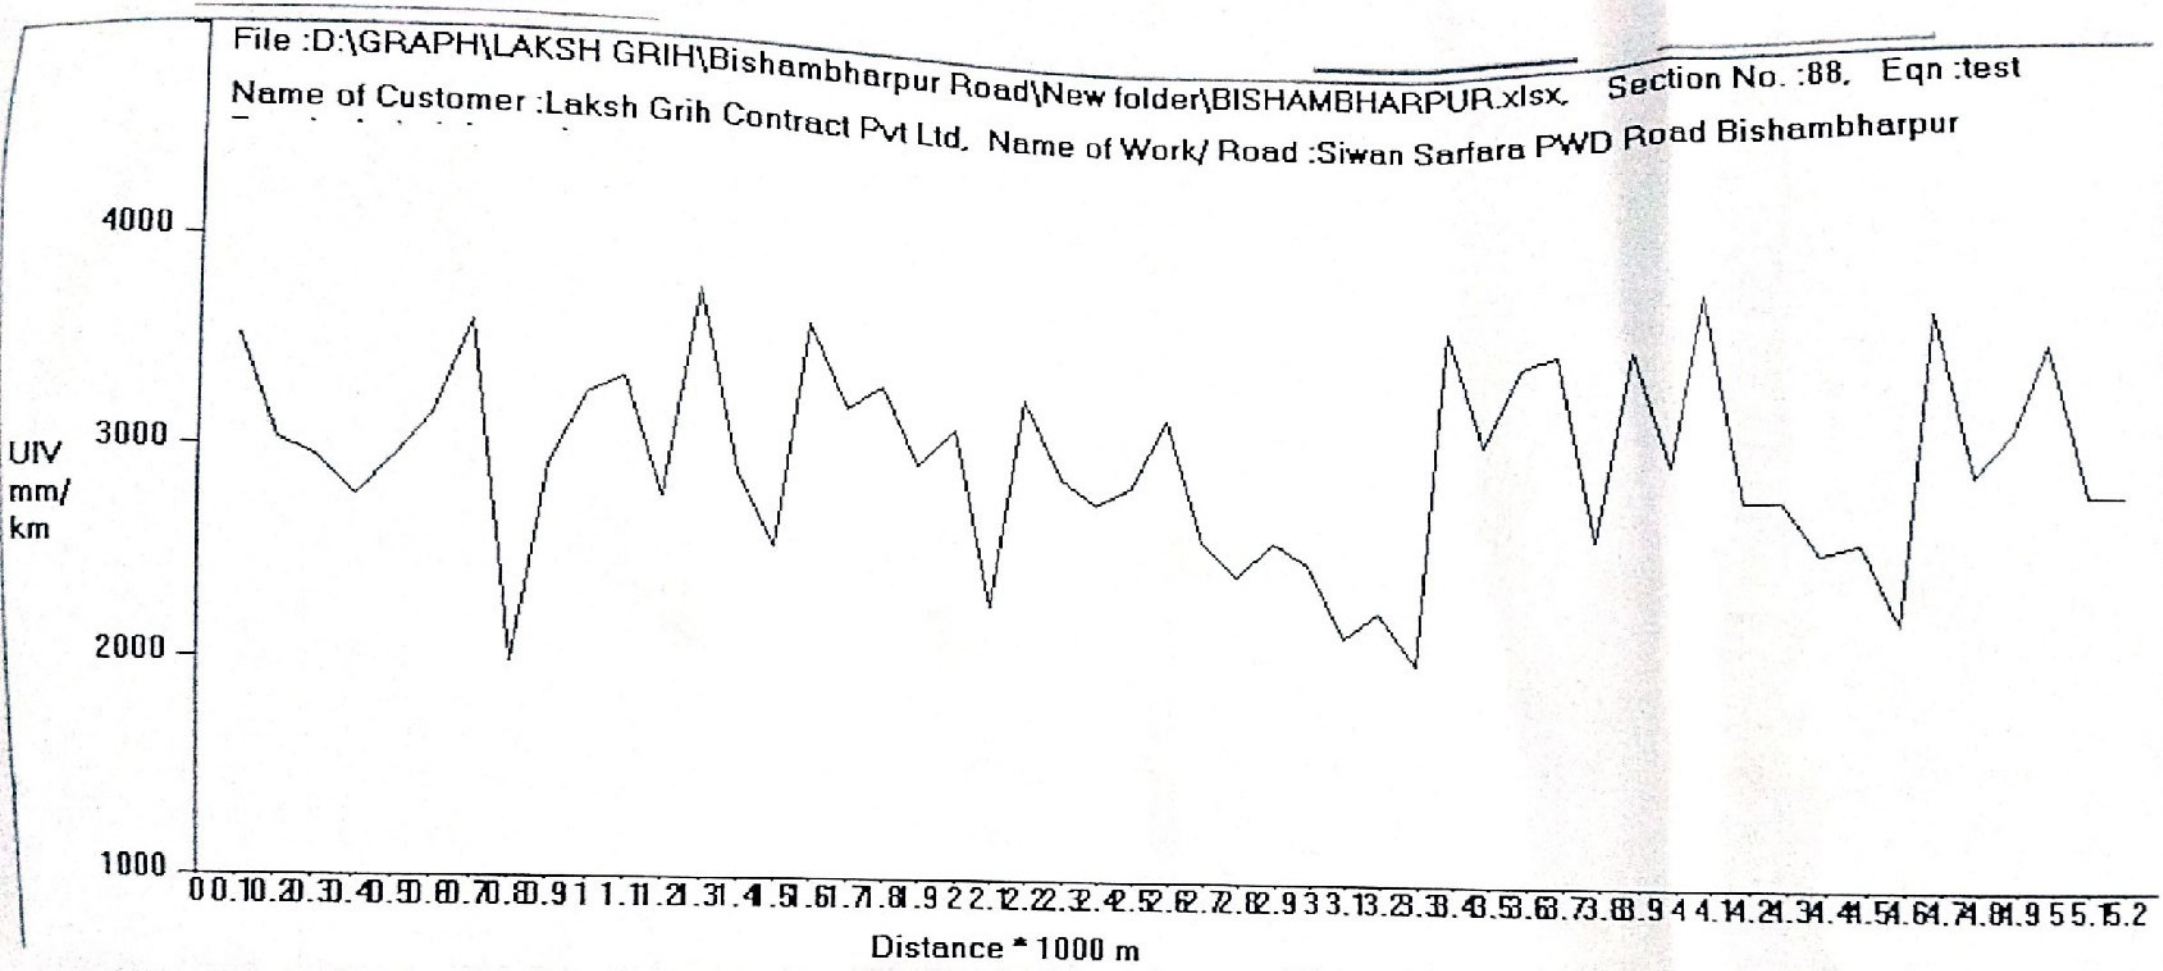

27/08/22
JE, Maighat

27/8/22
AE

03/09/22
ER
