कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, रजौली।

Mob No. 8986915851. Email I.D. – eerwdrajauli@gmail.com

पत्रांकः– 1244 (315) रजौली, दिनांकः– 01/09/2022

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, रजौली।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी–सह–सचिव,
बिहार ग्रामीण पथ विकास अभिकरण, ग्रामीण कार्य विभाग,
विश्वेश्वरैया भवन, बेली रोड, बिहार पटना।

विषयः–New Maintenance Policy-2018 योजना अंतर्गत स्वीकृत कार्यों के पंचवर्षीय रूटीन अनुरक्षण मद अंतर्गत आवंटन उपलब्ध कराने के संबंध में।

प्रसंगः– अभियंता प्रमुख, ग्रामीण कार्य विभाग,बिहार,पटना **के** पत्रांकः– मु०अ०– 4(मु०) 3054–04–229 / 2021–1135 अनु० / पटना,दिनांक–09.03.2022।

महाशय,

उपर्युक्त विषय से संबंधित विहित प्रपत्र में वांछित सूचना उपलब्ध कराते हुए अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय। ताकि संवेदक को अनुरक्षण कार्य का भुगतान किया जा सके।

अतः अनुरोध है आवंटन उपलब्ध कराने की कृपा की जाय।

अनु0– पथ विवरणी, उपयोगिता प्रमाण–पत्र एवं Formate for Road Quaterly Statement की छायाप्रति।

विश्वासभाजन

5/9/22

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल,रजौली।

FORM GFR -19A

(See Government of India's Decision (I) below Rule-150)

Name of PIU: Rural Works Department, Works Division, Rajauli

Head: New Maintenance Policy-2018 (MR-3054) (Maintenance Fund)

Form of Utilization Certificate for the month of August-2022

SL. No.	Name of Scheme	Sanctioned No. & Date	Amount (Rs.)	Particulars
1	Construction of Rural Roads under New Maintenance Policy-2018 (MR-3054) (Maintenance Fund)	-	-	Certified that out of **Rs.Nil/-** Of grants upto the year 2021-22 in favour of RWD (W) Division, Rajauli (Bihar) a sum of **Rs. Nil/** has been utilized for the purpose Schemes as given in margin for which it was given in which it was sanctioned and that the balance Rs Nil/- remaining unutilized at the end of the period under report.

2. certified that I have satisfied myself that the conditions on which the grants in aid was sanctioned have been duly fulfilled / are being fulfilled and that I have excercised the following checks to see that money was actually utilized for the purpose for which it was sanctioned.

Kind of Checks excercised:

(i) Works have veen supervised by Executive Engineer/ Superintending Engineer

(ii) Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer

(iii) Construction materials have been tested

(iv) Measurements have been recorded in MBs and test check conducted by the Assistant Engineer/ Executive Engineer

(v) All other codal formalities have been observed

3 **Physical Progress achieved**

(i) Construction of Road works

(ii) Construction of CD works

1/9/22

Executive Engineer
RWD(W) Division, Rajauli

01/09/22

Maintenance Requisition Formate for Scheme Head-MR (3054) under Bihar Rural Road Maintenance Policy - 2018 (Intial Rectification and Surface Renewal) As Per State MIS

Name of works Division- Rajauli

Road Details					A.A Deails		Agreement Details								Actual Maintenance Expenditure						Previous Maintenance Exp		Length as per Bump Report 1st year	IRI As Per bump Report	Current Demand for Maintenance Amount						Remarks
Sl No.	Road Name	Batch No.	Project ID	Actual Date of Completion	Maint work amount	Maintenance amount	Main Work Amount	Maintenance Agreement Amount 1st year	Agreement 2	Agreement 3	Agreement 4	Agreement 5	Total Maint. amount	Length	1st Year Maint. Exp.	2nd Year Maint. Exp.	3rd Year Maint. Exp.	4rth Year Maint. Exp.	5th Year Maint. Exp.	Total Maint. Exp.	1st quater	Total Malotenance EXP			1st quater	2nd quater	3rd quater	4th quater	5th quater	Total	
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	32
1	RWD road of village vijaytand to Nadaura road	RM/NA/RAJ/19/0005	10502601034	25-09-20	43.87	21.06	43.28	1.81	2.60	6.29	3.42	6.88	21.00	2.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2.00	3403.10	0.00000	0.00000	1.04803	0.00000	0.000	1.05	
Total					43.87	21.06	43.282	1.80799	2.60	6.29316	3.42	6.88	21.00491	2.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	2.00	3403.10	0.00000	0.00000	1.04803	0.00000	0.00000	1.05	

11/9/22

Executive Engineer
RWD Works Division, Rajauli

11/9/22

01/09/22

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name : Rural Works Department, Works Division, Rajauli

Qty time period :- 26-03-2021 to 25-06-2021

1	Name of Road	RWD road of village vijaytand to Nadaura road
2	Batch No.	RM/NA/RAJ/19/0008
3	Project ID	10502601034
4	Total Length of Road (in Km)	2.000
5	Length of Road to Meet Required Service Level [Completed Length] (in Km) **[1]**	2.00
6	No. of Total Quarte (ie 3 Months as a Unit) in 5 Years	20
7	Ordinary Maintenance Cost as per Schedule [Agreement Amount for Maintenance] **(in Lakh)**	21.05
8	Quarterly Payment : 1/20 of Ordinary Maintenance Cost as per Schedule **(in Lakh) [2]**	1.0525

Compliance Critera	Standard Job Description	Non- Compliance		Reduction Payment [6] = [3]/[1]*[2]*[4]
		Length Non - Compliant [3]	Weighted Value for Payment Reduction (%) [4]	
I	PAVED ROADS (CARRIAGE WAY)	0.00	60%	0.00000
II	SHOULDERS AND EMBANKEMENTS	0.03	10%	0.00158
III	CROSS DRAINAGE INCLUDING CULVERTS AND BRIDGES	0.02	15%	0.00158
IV	SIGNAGE AND ROAD SAFETY	0.00	10%	0.00000
V	VEGATION	0.05	5%	0.00131
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh) **[5]**				0.00447 lac
TO BE PAID FOR THE QUARTER / DEMAND (in Lakh) **[6]**				1.04803 lac

Date of inspection by/E/I or his agent
Prepared by Contractor's self Control Unit

Name and Designation o Executive Engineer

(Signature) Executive Engineer R.W.D. Works Div. Rajauli

Date

Signature of person inspecting road 26/04/2022

Certify by E/I [signature] Date : 26/4/22

Name of Road- RWD road of village vijaytand To Nadaura road

Name of Contractor- M/S MAA DURGA CONSTRUCTION											Batch No- RM/NA/RAJ/19/0008			
Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
3/ 8/ 22	16: 5: 0	17	0.1	360	10.1	3600	3688	G	24.88968	85.629258	Speed Breaker	Y = 0 * X ^ 2 + 0.936 * X + 278.4		
3/ 8/ 22	16: 5: 18	17	0.1	310	20.2	3100	3148	G	24.88936	85.6301	Normal	X = 6596		
3/ 8/ 22	16: 5: 54	17	0.1	320	30.3	3200	3241	G	24.88909	85.631027	Normal	Y = 6452		
3/ 8/ 22	16: 6: 0	17	0.1	340	30.3	3400	3496	G	24.8889	85.631935	Normal	(R) RURAL ROAD		
3/ 8/ 22	16: 6: 29	17	0.1	360	30.3	3600	3658	G	24.88826	85.632608	Speed Breaker	Good	Average	Poor
3/ 8/ 22	16: 7: 4	17	0.1	370	30.3	3700	3730	G	24.88767	85.633315	Speed Breaker	<4000	4001-5000	>5001
3/ 8/ 22	16: 7: 4	17	0.1	290	20.2	2900	2992	G	24.88703	85.633955	Speed Breaker			
3/ 8/ 22	16: 7: 40	17	0.1	360	30.3	3600	3648	G	24.88626	85.63441	Speed Breaker			
3/ 8/ 22	16: 7: 40	17	0.1	290	30.3	2900	2992	G	24.88555	85.634915	Normal			
3/ 8/ 22	16: 8: 0	17	0.1	290	30.3	2900	2992	G	24.88472	85.634763	Normal			
3/ 8/ 22	16: 8: 15	17	0.1	370	20.2	3700	3741	G	24.88433	85.635403	Normal			
3/ 8/ 22	16: 8: 15	17	0.1	310	20.2	3100	3180	G	24.88368	85.635773	Normal			
3/ 8/ 22	16: 8: 15	17	0.1	290	30.3	2900	2964	G	24.88278	85.635773	Normal			
3/ 8/ 22	16: 9: 0	17	0.1	310	30.3	3100	3148	G	24.88225	85.635353	Normal			

31/08/2022 J.E

03/08/22 AE

11/9/22 EC

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD						
3/ 8/ 22	16: 9: 24	17	0.1	350	30.3	3500	3535	G	24.8817	85.636127	Speed Breaker			
3/ 8/ 22	16: 10: 0	17	0.1	360	30.3	3600	3675	G	24.8814	85.636952	Speed Breaker			
3/ 8/ 22	16: 10: 0	17	0.1	350	20.2	3500	3564	G	24.88115	85.637912	Speed Breaker			
3/ 8/ 22	16: 11: 0	17	0.1	370	20.2	3700	3732	G	24.88089	85.638803	Speed Breaker			
3/ 8/ 22	16: 11: 10	17	0.1	370	20.2	3700	3786	G	24.88076	85.63973	Speed Breaker			
3/ 8/ 22	16: 12: 21	17	0.1	310	10.1	3100	3152	G	24.8807	85.640673	Speed Breaker			
		Total	**2.000**	**6680**	**495**	**66800**	**68062**							
		Average		**334**	**24.745**	**3340**	**3403.1**							

03/08/2022
JE

03/08/22
AE

7/9/22
EE

Steco Analyzer

Name of Customer :	M/S MAA DURGA CONSTRU	Test Date :	8 / 3 /2022	Road Name :	RWD road of village vijaytand				
Name of Work/ Road :	RWD road of village vijaytand T	Machine No :	408	Road Type :	(R) RURAL ROAD				
Lab Job number	17	Start S No :	0.000	Side :					
Date :	8 / 3 /2022	Start E No :	2.000					Interval	
Section No.	17	Weather :		UIV Range :	1964	To	5000	1000	mm/km
		Start Location :	RWD road of	Dist Range :	0	To	2.1	0.1	* 1000 m
		End Location :	Nadaura road	Equation :	Y = 0 * X ^ 2 + 0.936 * X + 278.4				

Print | Generate Report and Graph | Redraw Graph | Map View

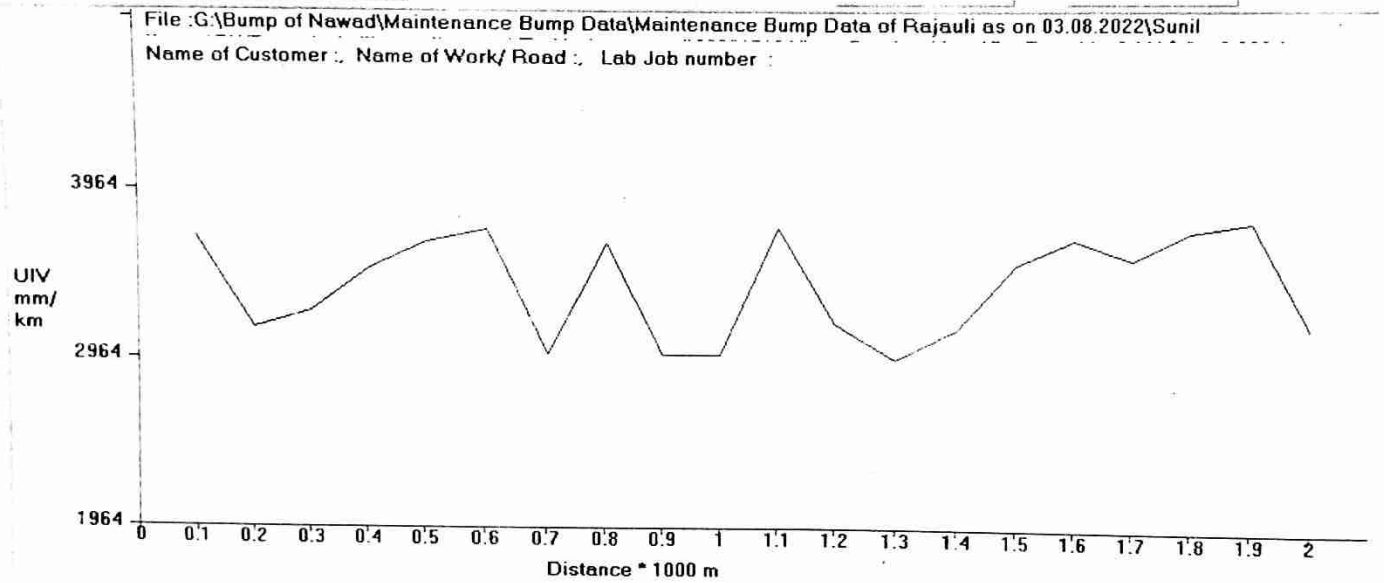

03/08/2022 J.E

03/08/22 AE

1/9/22 DC

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Rajauli

Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:-RWD road of village vijaytand to Nadaura road
Package No.- RM/NA/RAJ/19/0008

Length of Road :-2.000 K.M
Inspector :-

To:-
Executive Engineer
RWD, Works Division Rajauli

Date:- .....

Position :-

No	Standard Of Work Item Name	Work Unit	Unit OF Required in each Kilometere 1	2	3	4	5	6	7	8	9	10	Comments
OM100	**Sealed payment**												
OM101	Pothole Patching	m^2	46.875										
OM102	Surface Depression and Rut patching	m3	0.141										
OM103	Crack Sealing	Lm	2000										
OM104	Surface Treatment												
	(a) Loss of Agreegate (SurfacebRavelling)	m^2	46.875										
	(b) Bleeding / Flushing	m^2											
	© Crocodile Cracking	m^2											
105	Edge Repair	m^2											
106	Digouts	m^2	3.516										
107	Concreate pavement	m^3											
	Other activities												
OM200	**Shoulder**												
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm											
	(b) Roughness, Scouring or Potholes	Lm	562.5										
	(c) Holding water	Lm											
OM202	Embankment Repair	M^3	84.375%										
	Other activities (Rain Cuts)												
OM300	**Drainage including culverts major**												
OM301	Surface Drains & Verge	Lm											
OM302	Culvert Cleaning	No	2										
OM303	Culvert and pit Repair	M^3											
	Other activities(Whilw washing)	M^2											

No	Standard Of Work Item Name	Work Unit	Unit OF Required in each Kilometere 1	2	3	4	5	6	7	8	9	10	Comments
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha											
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha											
OM402	Tree and Shrub Management	No											
	Cutting Of Branches Of Trees	No	4.00										
	Cutting Of Shrubs From Road Way	No	2000										
	Other activities (Trimming of Grass)	M^2	4500										
OM500	**Safety Signage and Road**												
OM501	Signs Maintanence	No	2.000										
OM502	Guard Stones	Lm	15.96										
OM503	Distance Stones	No	2.000										
OM504	Road Marking	M^2											
	Other activities												

M/s Maa Durga Construsction

Bidder

Partner

Appendix

Executive Engineer
Rural works Department
Works Division, Rajauli
