कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमण्डल गोपालगंज–1

पत्रांक– 316 अनु० / गोपालगंज दिनांक 28 / 02 / 2023

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल गोपालगंज–1

सेवा में,

सचिव,
बिहार ग्रामीण पथ विकास अभिकरण,
बिहार पटना।

विषयः– राशि उपलब्ध कराने के संबंध में।

महाशय,

उपर्युक्त विषय के संबंध में कहना है कि बिहार ग्रामीण पथ नई अनुरक्षण नीति–2018 के तहत् पंचवर्षीय अनुरक्षण अवधि के अधीन पथों में कराये गये त्रैमासिक अनुरक्षण कार्य हेतु राशि की अधियाचना उपलब्ध कराये गये प्रपत्र में सभी सुचनाओं के साथ अंकित कर समर्पित किया जाता है।

अनु0–यथोक्त।

विश्वासभाजन

28/2/23

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, गोपालगंज–1

28/2/23

STANDARD FORMAT FOR ROADS QUARTERLY STATEMENT

PIU Name:- Rural Works Department, Works Division Gopalganj- I

Quarter:- 4th

Period:- 08-04-2022 to 08-07-2022

1	Name of the Road	Semra to Tulachapar
2	Batch No	RM/GO/GOP/20/0007
3	Project ID	31406902100
4	Total Length of Road (in Km)	2.43 KM
5	Length of Road to Meet Required Service level [Completed length] (in Km) [1]	2.43 KM
6	No. of total Quarter (ie 3 Months as a unit) in 5 years	20.0
7	Ordinary Maintenance Cost as per Schedule [Agreement amount of Maintenance] (in Lakh)	Rs. 24.199 Lac
8	Quarterly Payment:2/20 of Ordinary Maintenance Cost as per Schedule (in Lakh) [2]	Rs. 1.20 Lac

Compliance Criteria	Standard Job Description	Non-Compliance		Reduction Payment [6]=[3]/[1]*[2]*[4]
		Length Non-Compliant [3]	Weightage Value for Payment Reduction % [4]	
I	PAVED ROADS (CARRIAGEWAY)	0	60%	0.00
II	SHOULDERS AND EMBANKEMNT	0	10%	0
III	CROSS DRAINAGE INCULDING CULVERTS AND BRIDGES	0	15%	0
IV	SIGNAGE AND ROAD SAFETY	0	10%	0
V	VEGITATION	0	5%	0.00
TOTAL PAYMENT REDUCTION FOR THE QUARTER (in Lakh)			[5]	0.0000
TO BE PAID FOR QUARTER/DEMAND (in Lakh)			[6]	**Rs. 1.20 Lac**

Arun Kumar Rajak

Date of inspection by E/I or his agent

Prepaid by Contractor's Self Control unit

28/2/23

Name and Designation of Person Inspecting road

Date:-

28/2/23

Signature of Person Inspection road

Signature

28/2/23

Certify by E/I (Signature) Date:

Executive Engineer
R.W.D. Works Division
Gopalganj-1

28/2/23

28.2.23

Requisition Formet for Scheme Head-MR-(3054) Under Bihar Rurak Road Maintenance Policy-2018 (Initial Rectification and Surface Renewal)

RWD, Works Division Gopalganj-1

1 Year (4th Quarter)

Government Of Bihar
OM01
Rural Works Department

SUMMARY OF ORDINARY MAINTENANCE INSPECTION REPORT

Road From:- Semra to Tulachhapar
(Package No.MR-N/19-20 Gopalganj-1/14
Length of Road :-2.43 Km
Inspector :-J.E RWD Sub Division : Kuchaikote

To:-
Executive Engineer
RWD, Works Division Gopalganj-1

Date:- .....

Position :- J.E

	standard Of Work Item	Work	Unit OF Required in each Kilometere										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM100	Sealed payment												
OM101	Pothole Patching	m^2	Nil	Nil	Nil	Nil							No Pot Hole Found.
OM102	Surface Depression and Rut patching	m3	Nil	Nil	Nil	Nil							Not Surface Depression & Rut Patchibg Found
OM103	Crack Sealing	Lm	Nil	Nil	Nil	Nil							No Crack sealing Found
OM104	Surface Treatment												
	(a) Loss of Agreegate (SurfacebRavelling)	m^2	Nil	Nil	Nil	Nil							No Loss Of Aggregates (Surface Ravelling) Found
	(b) Bleeding / Flushing	m^2	Nil	Nil	Nil	Nil							No Bleeding/ Flushing Required
	© Crocodile Cracking	m^2	Nil	Nil	Nil	Nil							No Crocodile Cracking Found
105	Edge Repair	m^2	Nil	Nil	Nil	Nil							No Edge Repair Required
106	Digouts	m^2	N.A	N.A	N.A	N.A							
107	Concreate pavement	m^3	N.A	N.A	N.A	N.A							
	Other activities												
OM200	Shoulder												
OM201	Unsealed Shoulder												
	(a) Edge Drop-off	Lm	Nil	Nil	Nil	Nil							No Edge Drop-Off Required
	(b) Roughtness, Scouting or Potholes	Lm	Nil	Nil	Nil	Nil							Not Required
	(c) Holding water	Lm	Nil	Nil	Nil	Nil							No Holding Water Found
OM202	Embankment Repair	M^3	NIL	NIL	NIL	NIL							Not Required
	Other activities (Rain Cuts)		Nil	Nil	Nil	Nil							Not Required
OM300	Drainage including culverts major												
OM301	Surface Drains & Verge	Lm	N.A	N.A	N.A	N.A							Not Required
OM302	Culvert Cleaning	No	Nil	Nil	Nil	Nil							Not Required
OM303	Culvert and pit Repair	M^3	Nil	Nil	Nil	Nil							Not Required
	Other activities(Willw washing)	M^2	Nil	Nil	Nil	Nil							Not Required

28/2/23
JE

28/2/23
AE

28/2/23
Executive Engineer
R.W.D. Works Division
Gopalganj-1

	standard Of Work Item	Work	Unit OF Required In each Kilometere										Comments
No	Name	Unit	1	2	3	4	5	6	7	8	9	10	
OM400	Vegetation												
	Grass Control												
OM401	(a) Roadside- General Tidy	Ha	Nil	Nil	Nil	Nil							Not Required
	(b) Clear near Safety signs, kilometer posts and roadside furniture	Ha	Nil	Nil	Nil	Nil							Not Required
OM402	Tree and Shrub Management	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Branches Of Trees	No	Nil	Nil	Nil	Nil							Not Required
	Cutting Of Shrubs From Road Way	No	Nil	Nil	Nil	Nil							Not Required
	Other activities (Trimming of Grass)	M^2	Nil	Nil	Nil	Nil							Not Required
OM500	**Safety Signage and Road**		Nil										Not Required
OM501	Signs Maintanence	No	Nil	Nil	Nil	Nil							Not Required
OM502	Guard Stones	Lm	N.A	N.A	N.A	N.A							Not Required
OM503	Distance Stones	No	N.A	N.A	N.A	N.A							Not Required
OM504	Road Marking	M^2	Nil	Nil	Nil	Nil							Not Required
	Other activities												

28/2/23

28/2/23

28-2-23

28/2/23

Executive Engineer
R.W.D. Works Division
Gopalganj-1

28/2/23

~~Gaur bathuwa road to sonikpur~~ Semara to Tulachapra

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY	Latitude	Longitude	Event
24/ 6/ 22	13: 2: 33	35	0.1	300	0	3000	3034	G	26.534	84.22535	Normal
24/ 6/ 22	13: 3: 10	35	0.1	370	10.1	3700	3637	G	26.53493	84.22551	Normal
24/ 6/ 22	13: 3: 10	35	0.1	330	20.2	3300	3293	G	26.53583	84.22571	Normal
24/ 6/ 22	13: 3: 10	35	0.1	290	30.3	2900	2948	G	26.53672	84.22596	Normal
24/ 6/ 22	13: 3: 45	35	0.1	250	30.3	2500	2603	G	26.5376	84.22623	Normal
24/ 6/ 22	13: 4: 0	35	0.1	300	30.3	3000	3034	G	26.53852	84.22648	Normal
24/ 6/ 22	13: 4: 0	35	0.1	240	30.3	2400	2517	G	26.53939	84.227	Culvert
24/ 6/ 22	13: 4: 21	35	0.1	210	30.3	2100	2258	G	26.54033	84.227	Normal
24/ 6/ 22	13: 4: 21	35	0.1	250	30.3	2500	2603	G	26.54115	84.22746	Normal
24/ 6/ 22	13: 5: 0	35	0.1	320	10.1	3200	3206	G	26.54177	84.22805	Normal
24/ 6/ 22	13: 5: 0	35	0.1	340	10.1	3400	3379	G	26.54137	84.22892	Culvert
24/ 6/ 22	13: 5: 31	35	0.1	300	10.1	3000	3034	G	26.54106	84.22988	Normal
24/ 6/ 22	13: 6: 6	35	0.1	300	10.1	3000	3034	G	26.54076	84.23086	Curve
24/ 6/ 22	13: 6: 41	35	0.1	300	10.1	3000	3034	G	26.5402	84.23163	Speed Breaker
24/ 6/ 22	13: 7: 17	35	0.1	390	10.1	3900	3810	G	26.53953	84.23227	Normal
24/ 6/ 22	13: 7: 17	35	0.1	360	20.2	3600	3551	G	26.53925	84.23327	Normal
24/ 6/ 22	13: 7: 52	35	0.1	330	20.2	3300	3293	G	26.53979	84.23397	Normal
24/ 6/ 22	13: 8: 0	35	0.1	320	10.1	3200	3206	G	26.54069	84.23421	Speed Breaker
24/ 6/ 22	13: 8: 28	35	0.1	340	20.2	3400	3379	G	26.54156	84.23444	Normal
24/ 6/ 22	13: 9: 0	35	0.1	310	10.1	3100	3120	G	26.54241	84.23471	Speed Breaker
24/ 6/ 22	13: 9: 2	35	0.1	270	30.3	2700	2775	G	26.54323	84.23525	Normal
24/ 6/ 22	13: 9: 2	35	0.1	260	30.3	2600	2689	G	26.54385	84.23599	Normal
24/ 6/ 22	13: 9: 37	35	0.1	330	20.2	3300	3293	G	26.54449	84.23673	Normal
24/ 6/ 22	13: 10: 0	35	0.1	370	10.1	3700	3637	G	26.54505	84.23758	Normal

25/6/22
J.E.

25/6/22
AE

18/8/22

Executive Engineer
R.W.D. Works Division
Gopalganj-1

File :C:\Users\U.R Computer\Desktop\25062053.Xls. Section No. :35. Eqn : Y = 0 * X ^ 2 + 0.862 * X + 448.5

Name of Customer :Sri Sain Nirman ; Name of Work/ Road :Semara to tulachapar. Lab Job number :

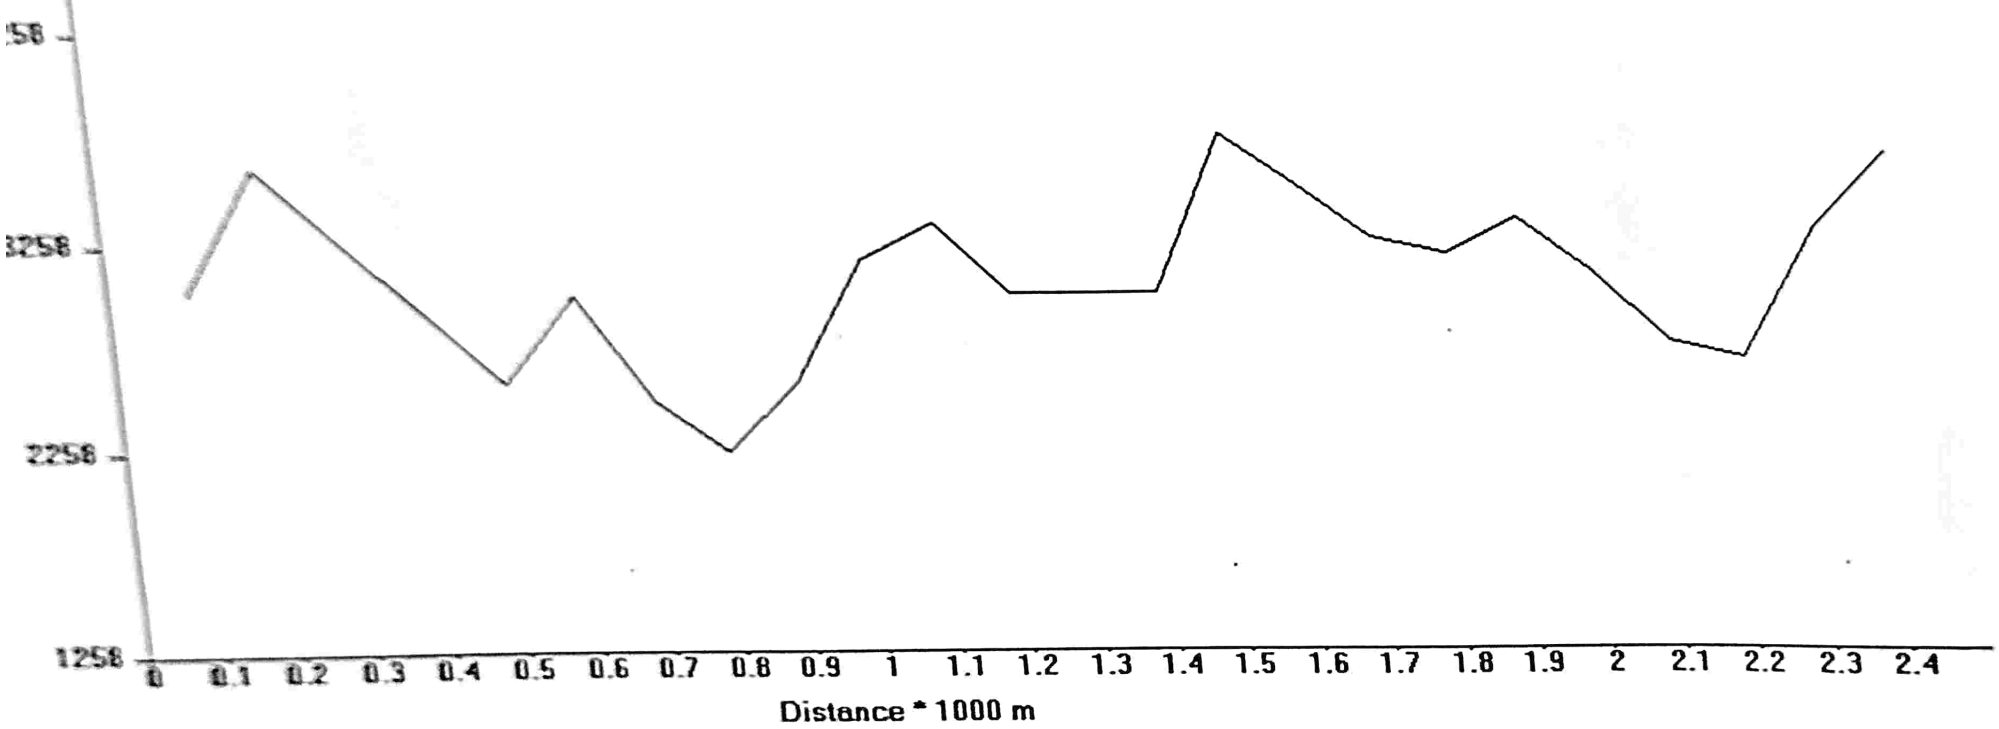

25/6/22

25/6/22 AE

18/8/22

Executive Engineer
R.W.D. Works Division
Gopalganj-1
