कार्यपालक अभियंता का कार्यालय,
ग्रामीण कार्य विभाग, कार्य प्रमंडल, झंझारपुर ।

पत्रांक 452 झंझारपुर / दिनांक 27/03/25

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, झंझारपुर ।

सेवा में,

अपर मुख्य कार्यपालक पदाधिकारी
–सह– सचिव
ग्रामीण कार्य विभाग,
पटना।

विषय : शीर्ष **3054MR** योजना अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति – 2018 के तहत स्वीकृत कार्यों के आवंटन की मांग के संबंध में।

प्रसंग : भवदीय पत्रांक मु०अ०–4 (मु०)–3054–04–251/2018–113 अनु पटना दिनांक 10.01.2020

महाशय,

उपरोक्त विषयक प्रासांगिक पत्र के आलोक में शीर्ष 3054MR योजना अंतर्गत बिहार ग्रामीण पथ अनुरक्षण नीति –2018 के तहत स्वीकृत कार्यों में कृत कार्य के भुगतान हेतु विहित प्रपत्र में अधियाचना तैयार कर आवश्यक कार्रवाई हेतु समर्पित की जा रही है।

अतः अनुरोध है कि आवंटन उपलब्ध कराने की कृपा की जाय।

अनु. – विहित प्रपत्र में अधियाचना प्रपत्र
बम्प इन्टिग्रेडर मशीन से लिया गया प्रतिवेदन

विश्वासभाजन
27/03/25
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग, कार्य प्रमंडल,
झंझारपुर

Form GFR 19- A

(See Government of India's Decision (I) below Rule - 150)

Form of Utilazation Certificate upto the month March 2025

New Maintenance Policy 2018

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (in lacs)	Amount Received (in lacs)	Particulars
1	1	07 enc/ Dt. 22.01.2025	8245.28050	Certified that Rs:-8245.28050 Lac received Till the date in favour of Executive Engineer, RWD Work Division Jhanjharpur. A sum of Rs 7684.62447 Lac has been utilized for the purpose of NEW_MR Scheme as given in the margin for which it was sanctioned and that the balance of Rs 560.65603 Lacs remaining.
		Total :	**8245.28050**	

Certifed and verified myself that the conditions on which the grands in aid was sanctioned have been duly fulfilled / are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.

Kinds of Checks exercised :-

i Works have been supervised by Executive Engineer/ Superintending Engineer.

ii Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.

iii Construction material have been tested.

iv Measurments have been recorded in the MBs and test check conducted by the Assistant Engineer/Executive Engineer.

v All other codal formalities have been observed.

Physical Progress achieved :-

i Construction of Road works.

ii Construction of CD works

27/03/25

Executive Engineer
RWD works Division
jhanjharpur

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division :Jhanjharpur

Sl. No	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Alloted Amount (I Lac)	up to date expenditure as per MIS (in Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	BM/MA/JHA/23/0008	NH-57 - SOHPUR	31909802064	6120/04.12.2023	0.55	29.25100	18.19936	4.07430	09MBD/2024-25	28.04.2025	I	3200	25mm	5.0%	0.00000	0.00000	15.55000	Surface Completed
2		Construction of Road from Mahadeo kant jha House to Ayodhi Kamat House under Chanauraganj to Nanour Chouk R.E.D. Road near bridge of Koshi Canal to beside of Choura Mahrail primary School near Yadunat	31909901002	6120/04.12.2023	1.4	107.47000	71.7297	7.95514	09MBD/2024-25	28.04.2025	I	3200	25mm	5.0%	0.00000	0.00000	64.55673	Surface Completed
3		Chanaur Goth Durga Asthan to Chanaur Muslim Tol	31909812009	6120/04.12.2023	0.22	16.04000	10.8143	0.82687	09MBD/2024-25	28.04.2025	I	2650	25mm	5.0%	0.00000	0.00000	9.50000	Surface Completed
4		NH-57 to Nonia Tol Sangram	31909812011	6120/04.12.2023	0.73	49.56400	34.26951	2.74487	09MBD/2024-25	28.04.2025	I	2800	25mm	5.0%	0.00000	0.00000	31.26000	Surface Completed
5		NH-57 Tajpur Road to Simra Mallah Tol	31909812012	6120/04.12.2023	0.915	53.493	35.17433	5.44704	09MBD/2024-25	28.04.2025	I	2800	25mm	5.0%	0.00000	0.00000	31.85000	Surface Completed

27/03/25

Executive Engineer
RWD Works Division
Jhanjharpur

Name of work	:	NH-57 Tajpur Road to Simra Mallah Tol
Name of customer	:	Praveen Kumar Mishra

(R)Rural Road		
Good	Average	Poor
< 4000	4001 - 5000	> 5000

Date	Time	Test No	Distance(m)	Total Distance(m)	BUMP(cm)	Speed(Km/Hr)	UI(mm/Km)	Corrected UI (mm/Km)	IRI	Status	Latitude	Direction	Longitude	Direction1	Remarks
21/03/25	12:35:07	26	100	100	25.0 cm	12.2 Km/Hr	2500.0 mm/Km	2720	3.69	Good	26.804315	N	86.078572	E	Normal
21/03/25	12:35:33	26	100	200	28.0 cm	13.6 Km/Hr	2800.0 mm/Km	3026	4.06	Good	26.802868	N	86.078874	E	Normal
21/03/25	12:35:55	26	100	300	24.0 cm	12.7 Km/Hr	2400.0 mm/Km	2618	3.57	Good	26.802207	N	86.079261	E	Normal
21/03/25	12:36:10	26	100	400	20.0 cm	17.1 Km/Hr	2000.0 mm/Km	2209	3.07	Good	26.803961	N	86.078698	E	Normal
21/03/25	12:36:30	26	100	500	26.0 cm	16.3 Km/Hr	2600.0 mm/Km	2822	3.81	Good	26.803998	N	86.078649	E	Normal
21/03/25	12:36:42	26	100	600	24.0 cm	15.6 Km/Hr	2400.0 mm/Km	2618	3.57	Good	26.807814	N	86.078185	E	Normal
21/03/25	12:37:20	26	100	700	28.0 cm	13.4 Km/Hr	2800.0 mm/Km	3026	4.06	Good	26.806769	N	86.078388	E	Normal
21/03/25	12:37:38	26	100	800	22.0 cm	17.6 Km/Hr	2200.0 mm/Km	2413	3.32	Good	26.810058	N	86.077664	E	Normal
21/03/25	12:37:55	26	100	900	23.0 cm	21.8 Km/Hr	2300.0 mm/Km	2516	3.44	Good	26.810327	N	86.077411	E	Normal

21-3-25
JE

ACE Scanner
PDF Scanner

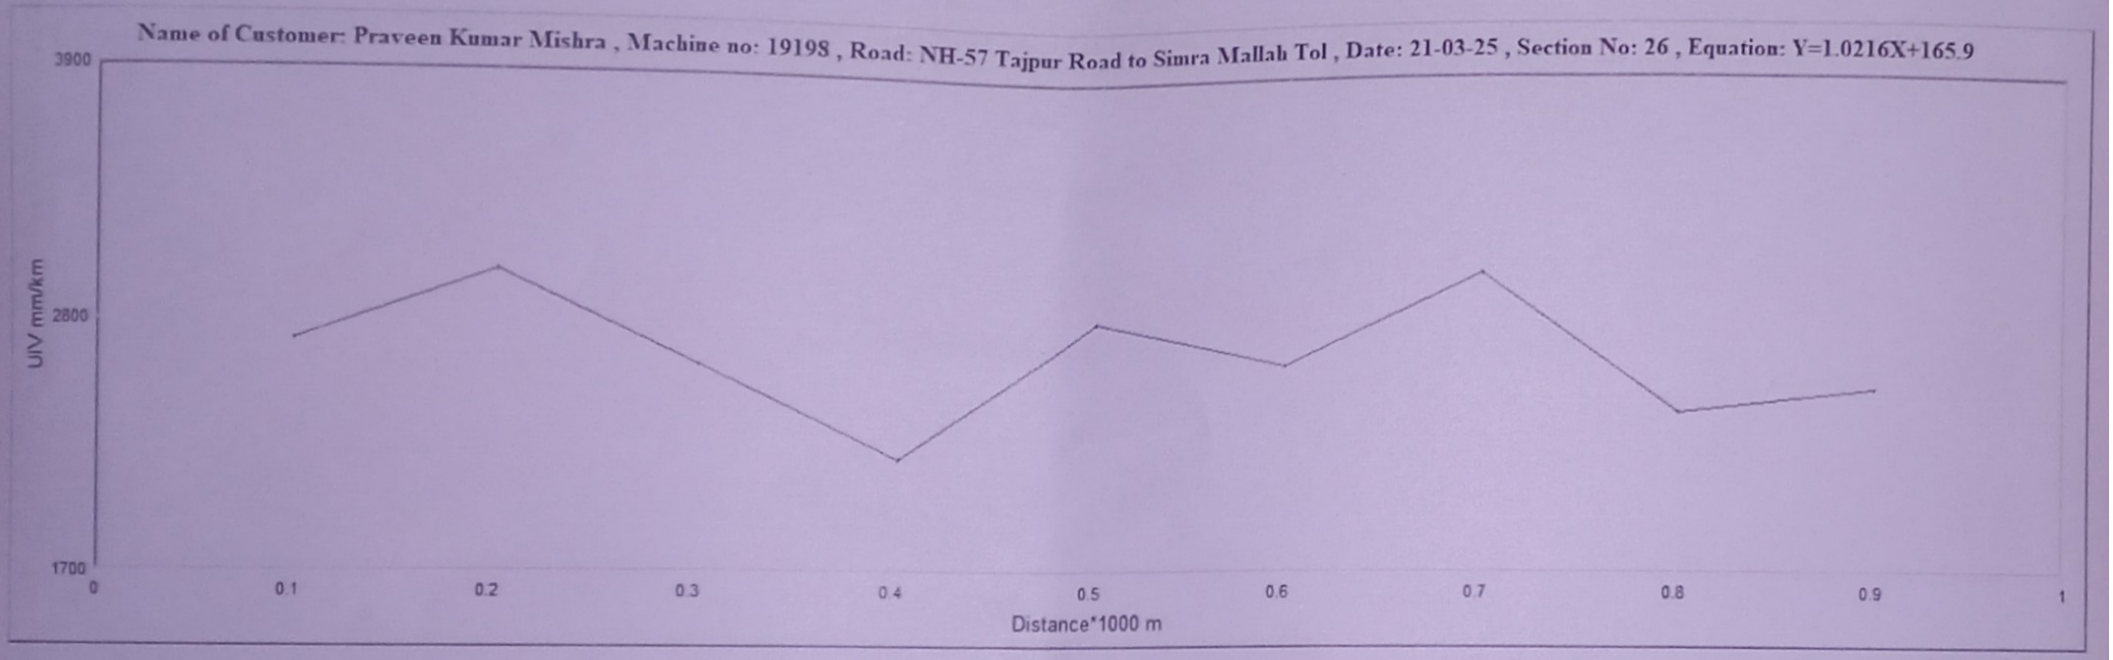
Name of Customer: Praveen Kumar Mishra , Machine no: 19198 , Road: NH-57 Tajpur Road to Simra Mallah Tol , Date: 21-03-25 , Section No: 26 , Equation: Y=1.0216X+165.9
3900
2800
1700
UIV mm/km
0
0.1
0.2
0.3
0.4
0.5
0.6
0.7
0.8
0.9
1
Distance*1000 m

21-3-25

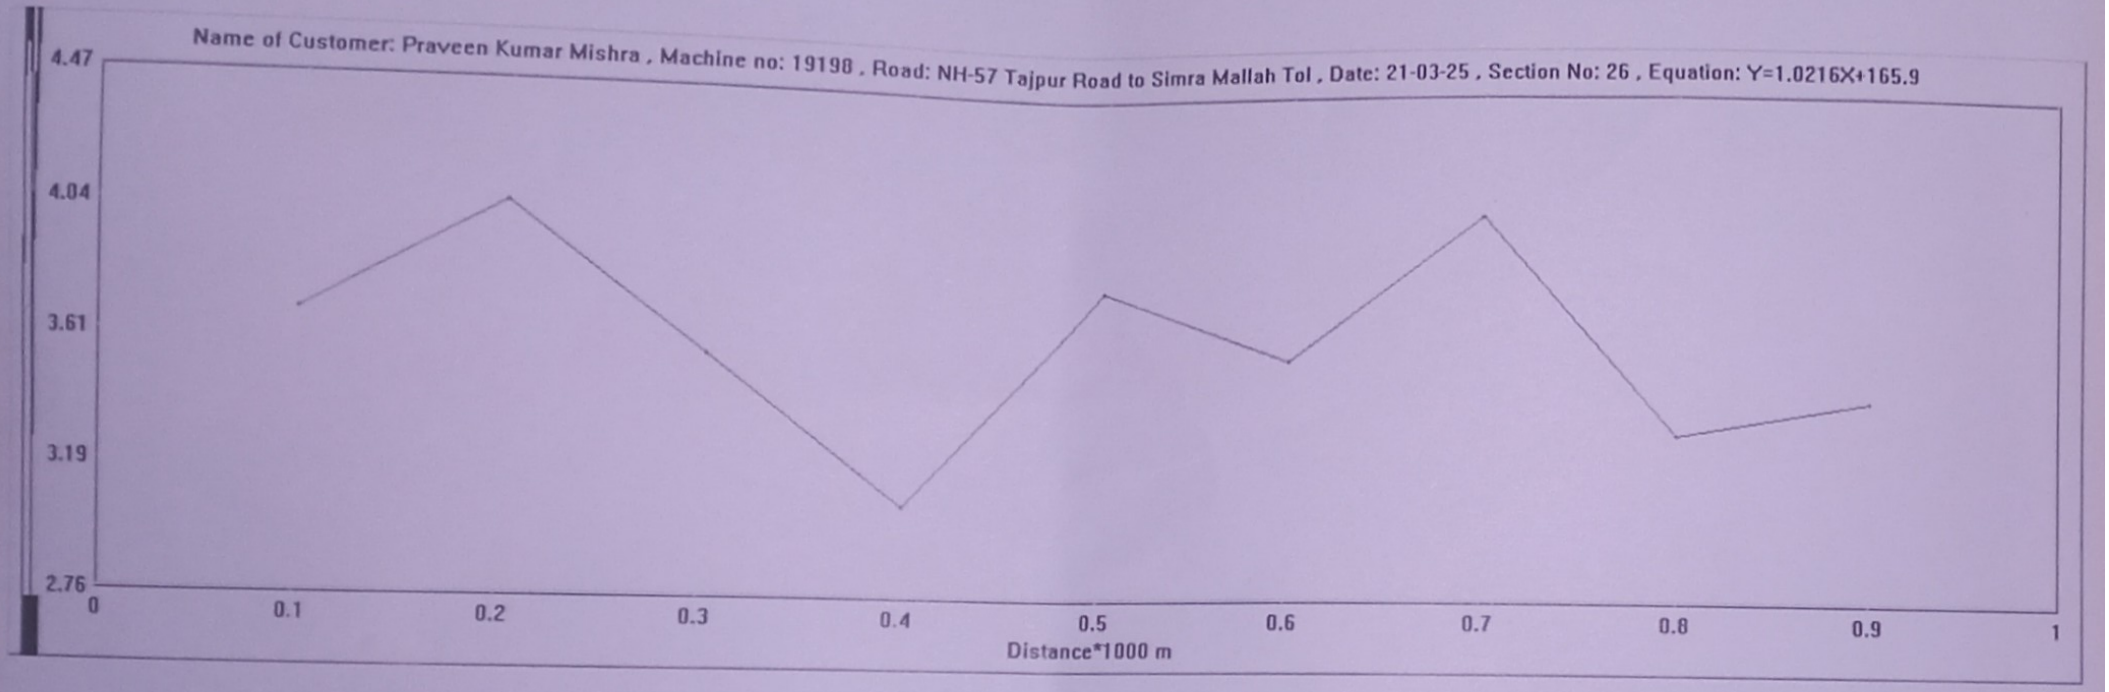

21-3-25
J.F.

ACE Scanner
PDF Scanner
