कार्यपालक अभियंता का कार्यालय, ग्रामीण कार्य विभाग, कार्य प्रमंडल, मनिहारी (कटिहार)।

पत्रांक 271 अनु0 मनिहारी, दिनांक 28/02/23

प्रेषक,

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल मनिहारी (कटिहार)।

सेवा में,

अपर –मुख्य–कार्यपालक –पदाधिकारी,
ग्रामीण कार्य विभाग,
बिहार, पटना।

विषय :– **MR (New-Maintenance Policy-2018) योजनान्तर्गत चल रहें कार्यें का निधि की अधियाचना के संबंध में।**

महाशय्

उपर्युक्त विषय के संबंध में कहना है कि ग्रामीण कार्य विभाग कार्य, कार्य प्रमंडल, मनिहारी के अधीन **MR (New-Maintenance Policy-2018** योजनान्तर्गत चल रहे कार्यें का निधि उपलब्ध कराने हेतु अधियाचना विहित प्रपत्र में तैयार कर आपके अग्रेतर कार्रवाई हेतु समर्पित की जाती है।

अनु:–यथोक्त।

विश्वासभाजन

28/2/23

कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,कार्य प्रमंडल,
मनिहारी(कटिहार)।

28/02/23

28/2/23

RWD, Works Division,Manihari

Requisition Format for Scheme Head - MR (3054) Under Bihar Rural Road maintenance Policy 2018 (Initial Rectification and Surface Renewal)

Name of Division : Manihari

SLNo	Package no.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount (in Lac)		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (in mm/km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content in percentage	Previous Total Alloted Amount (In Lac)	up to date expenditure as per MIS (In Lac)	Requisition Against work done (In lac)	Remarks
					Length (In Km)	Amount (in Lac)	Initial Rectification with Surface Renewal (in lac)	5 years Routine Maintenance (In lac)										
1	MR N/20-21 MANIHARI/04	Mahiyarpur To Jagbatti Road	NEA220001014	1841/ 24.06.2019	3.770	116.360	78.533	28.74565	01/MBD/ 2020-21, 11.05.2020	10.05.2021	27.10.2022	2274.04	25	5.1%	45.82282	45.82282	16.42756	
2	MR N/20-21 MANIHARI/04	Dilarpur To Mahiyarpur	NEA220001011	1841/ 24.06.2019	4.330	174.492	78.533	28.74565	01/MBD/ 2020-21, 11.05.2020	10.05.2021	24.10.2022	2232.55	25	5.1%	98.19518	98.19518	17.53377	
		Total													**144.01800**	**144.01800**	**33.96133**	

28/02/23
Divisional Accounts Officer
RWD, Works Division, Manihari

28/2/23
Executive Engineer
RWD, Works Division, Manihari
28/2/23

EXECUTIVE ENGINEER, WORK DEPARTMENT , WORKS DIVISION, MANIHARI

FORM GER – 19 – A
(See Government of India's Decision (i) below Rule – 150)
Form of Utilization Certificate up to month of Febuary-2023

Sl. No.	Name of Scheme	Sanction No. & Date with Amount (In Lacs)		Total Amount Received (In Lacs)	Particulars	Balance Amount (In Lakh) Bank+ CFMS
1	Construction of Rural Road under MR (New-Maintenance Policy-2018)	Letter No.22 we. Dt-08.08.2022	317.2483	1767.22026	Certified that out of Rs. **1767.22026** lakh through CFMS of grants in aid sanctioned during the years in favour of Engineer incharge , R.W.D, Works Division, Manihari, Sum of Rs.**1706.59702** Lacs has been utilized for the purpose **New-Maintenance Policy-2018** New Rural Roads & Bridge Schemes as given in the margin for which it was sanctioned and that the balance of Rs. **60.623** Lacs remaining unutilized at the end of the period under.	**60.62300**
		Total	**317.248**	**1767.22026**		**60.62300**

Certified that I have satisfied myself that the condition on which the grants in aid sanctioned have been duly fulfilled / are being fulfilled and that I have Exercised the following Checks to see that the money was actually utilized for the purpose for which it was sanctioned .

2	i	**Works have been supervised by Executive Engineer / Superintending Engineer.**
	ii	**Periodical inspection has been conducted by A.E. / Executive Engineer / Superintending Engineer.**
	iii	**Construction materials have been tested.**
	iv	**Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer.**
	v	**All other Codal formalities have been observed.**

28/02/23
D.A.O.
Rural works Department
Works Division Manihari

28/2/23
Executive Engineer
Rural works Department
Works Division Manihari
28/2/23

Lab Job number :11

Date :24-03-2022

Name of Customer :Ashok Kumar

Name of Work/ Road :Mahiyarpur To Jagbatti

Sr.no	Location of test (in km)	Corrected U.I value (mm/km)	Road catagory
1	0.100	2497	G
2	0.200	2109	G
3	0.300	2787	G
4	0.400	2206	G
5	0.500	2206	G
6	0.600	2497	G
7	0.700	2109	G
8	0.800	2303	G
9	0.900	2206	G
10	1.000	1915	G
11	1.100	2400	G
12	1.200	2109	G
13	1.300	2109	G
14	1.400	2012	G
15	1.500	1721	G
16	1.600	2690	G
17	1.700	2593	G
18	1.800	2981	G
19	1.900	2981	G
20	2.000	1818	G
21	2.100	2012	G
22	2.200	1721	G
23	2.300	2206	G
24	2.400	2400	G
25	2.500	2497	G
26	2.600	1721	G
27	2.700	2593	G
Average IRI value		**2274.04**	

20/03/22
AE

E. E.
R. W. D. W. D.
Manihari

Lab Job number :11
Date :24-03-2022

Name of Customer :Ashok Kumar
Name of Work/ Road :Mahiyarpur To Jagbatti

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	CATEGORY ROAD	Latitude	Longitude	Event
24/ 3/ 22	13: 25: 0	11	0.1	250	0	2500	2497	G	25.417973	87.613315	Normal
24/ 3/ 22	13: 25: 35	11	0.1	210	10.1	2100	2109	G	25.418718	87.612727	Normal
24/ 3/ 22	13: 26: 10	11	0.1	280	10.1	2800	2787	G	25.419503	87.612340	Normal
24/ 3/ 22	13: 26: 10	11	0.1	220	10.1	2200	2206	G	25.420340	87.612070	Normal
24/ 3/ 22	13: 27: 0	11	0.1	220	10.1	2200	2206	G	25.421197	87.611868	Normal
24/ 3/ 22	13: 27: 20	11	0.1	250	10.1	2500	2497	G	25.422070	87.611700	Normal
24/ 3/ 22	13: 27: 20	11	0.1	210	10.1	2100	2109	G	25.422972	87.611565	Normal
24/ 3/ 22	13: 28: 0	11	0.1	230	10.1	2300	2303	G	25.423805	87.611328	Normal
24/ 3/ 22	13: 28: 31	11	0.1	220	10.1	2200	2206	G	25.424655	87.611110	Normal
24/ 3/ 22	13: 29: 0	11	0.1	190	10.1	1900	1915	G	25.425227	87.611397	Curve
24/ 3/ 22	13: 29: 6	11	0.1	240	10.1	2400	2400	G	25.425240	87.612357	Normal
24/ 3/ 22	13: 32: 3	11	0.1	210	10.1	2100	2109	G	25.426002	87.610622	Normal
24/ 3/ 22	13: 32: 3	11	0.1	210	20.2	2100	2109	G	25.426843	87.610387	Normal
24/ 3/ 22	13: 32: 38	11	0.1	200	20.2	2000	2012	G	25.427655	87.610773	Normal
24/ 3/ 22	13: 33: 0	11	0.1	170	20.2	1700	1721	G	25.428400	87.611312	Normal
24/ 3/ 22	13: 33: 13	11	0.1	270	10.1	2700	2690	G	25.429197	87.611835	Normal
24/ 3/ 22	13: 38: 30	11	0.1	260	10.1	2600	2593	G	25.433147	87.612895	Normal
24/ 3/ 22	13: 38: 30	11	0.1	300	20.2	3000	2981	G	25.433160	87.613855	Normal
24/ 3/ 22	13: 38: 30	11	0.1	300	20.2	3000	2981	G	25.433308	87.614830	Normal
24/ 3/ 22	13: 39: 5	11	0.1	180	10.1	1800	1818	G	25.433657	87.615638	Curve
24/ 3/ 22	13: 39: 5	11	0.1	200	20.2	2000	2012	G	25.433490	87.616582	Normal
24/ 3/ 22	13: 39: 40	11	0.1	170	20.2	1700	1721	G	25.433405	87.617525	Normal
24/ 3/ 22	13: 40: 0	11	0.1	220	20.2	2200	2206	G	25.433378	87.618518	Normal
24/ 3/ 22	13: 40: 16	11	0.1	240	20.2	2400	2400	G	25.433342	87.619477	Normal
24/ 3/ 22	13: 40: 16	11	0.1	250	20.2	2500	2497	G	25.433145	87.620453	Normal
24/ 3/ 22	13: 40: 16	11	0.1	170	20.2	1700	1721	G	25.432993	87.621430	Normal
24/ 3/ 22	13: 41: 0	11	0.1	260	20.2	2600	2593	G	25.433052	87.622473	Normal

Y = 0 * X ^ 2 + 0.969 * X + 74.60
X = 2600
Y = 2593

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

20/03/22

20/3/22

E. E.
R. W. D. W. D.
Manihari

File :C:\RAM KUMAR\MISC Files\Bump integrator\Manihari\Mahiyarpur to Jagbatti\24031353.Xls, Section No. :11,

Name of Customer :Ashok Kumar, Name of Work/ Road :Mahiyarpur To Jagbatti, Lab Job number :11

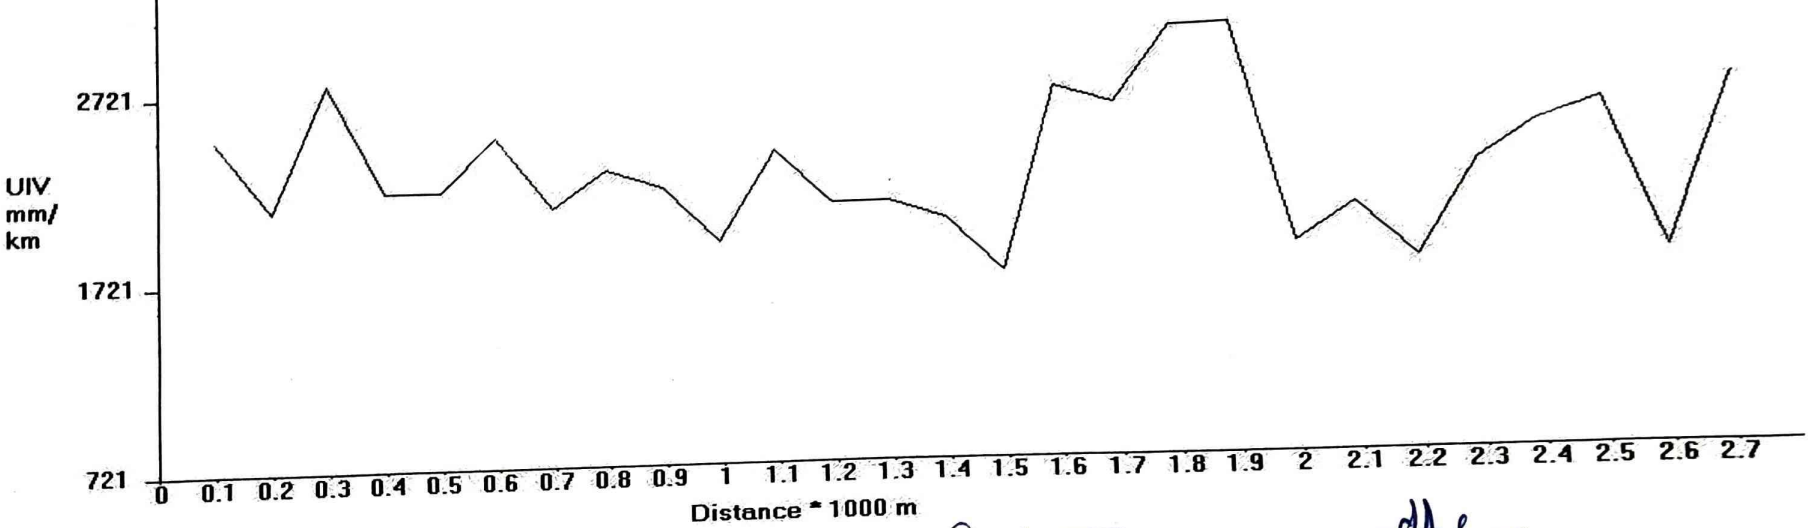

20/03/22
AE

20/3/22
E. E.
R. W. D. W. D.
Manihari
