कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल, दानापुर

पत्रांक :- 782(3)

दानापुर/ दिनांक :- 15/4/24

प्रेषक : ई० चन्दन कुमार
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमंडल, दानापुर ।

सेवा में,
विशेष सचिव ,
ग्रामीण कार्य विभाग ,
बिहार, पटना ।

विषय:- शीर्ष-MR (3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत आवंटन के अधियाचना के सम्बन्ध में ।

महाशय ,

उपर्युक्त विषय के सम्बन्ध में कहना है कि शीर्ष- MR(3054) Under Bihar Rural Road Maintenance Policy-2018 योजना अंतर्गत पथो के आवंटन की अधियाचना विहित प्रपत्र में तैयार कर Signed Hard Copy of Recorded IRI के साथ भेजी जा रही है।

अत: आपसे अनुरोध है कि उक्त योजना का आवंटन उपलब्ध करने की कृपा की जाये ताकि संवेदक का भुगतान किया जा सके।

अनु :-- यथोक्त।

विश्वासभाजन

15.04.24

ई० चन्दन कुमार
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दानापुर ।

Scanned with CamScanner

Requisition Format for Scheme Head - MR (3054) under Bihar Rural Road Maintenance Policy -2018 (Initial Rectification and Surface Renewal)

Name of Work Division:- Danapur

Sl. No.	Package No.	Name of Road	Project ID as per MIS	Administrative Approval (AA) Letter No. & Date	Administrative Approval (AA)		Agreement Amount		Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Value of IRI (In mm/km)	Thickness of Bitumen Layer (In mm)	Value of Bitumen Content in Percentage	Previous Total Alloted Amount (In Lakh)	Up-to-date Expenditure as per MIS (In Lakh)	Requistion against work done (In Lakh)	Remarks
					Length (In Km)	Amount of (In Lakh)	Initial Rectification with Surface Renewal (In Lakh)	5 Year Routine Maintanance (In Lakh)										
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	RM/PA/DAN/22/0004	Lai Sikariya Path to Taranagar	10100102154	2094 06.05.2022	1.470	90.22900	74.90603	13.88658	02-MBD/2022-23 14.11.2022	13.08.2023	–	3285.73333	100mm/ 25mm	5%	0.00	0.00	74.90603	Surface Work Completed
2	RM/PA/DAN/22/0007	NH-30 Baramchari to Jangali Mahadev	10100102184	317 23.06.2022	2.00	130.68600	107.81584	8.82109	03-MBD/2023-24 13.06.2023	12.03.2024	–	3310.65	100mm/ 25mm	5%	0.00	0.00	107.81584	Surface Work Completed
3	RM/PA/DAN/23/0004	T09 To Makhdumpur	10100202013	2328 04.05.2023	0.900	71.9680	56.86933	3.31807	06-MBD/2023-24 07.10.2023	06.07.2024	–	3096.333333	100mm/ 25mm	5%	0.00	0.00	56.86933	Surface Work Completed

Signed Hard Copy and Soft Copy (in excel) of recorded IRI is enclosed.

Up-to-Date Physical Progress has been uploaded in MIS.

D.A.O

R.W.D, Works Division, Danapur

15.04.24

Executive Engineer

RWD, Works Division, Danapur

Scanned with CamScanner

FORM GFR 19-A

(See Government of India's Decision (1) below Rule-150)
Form of utilisation Certificate up to the Month of April-2024

PIU: RWD Works Division , Danapur

Sl No.	Name of Scheme	Sanction No. & Date with Amount	Amount Received (In Rs.)	Particulars
1	Construction of Rural roads under **New Maintenance Policy-2018**	1. Current Allotment Vide Letter No:-57 WE Dt:- 31.03.2024	**88,50,24,461.00**	Certified that out of Rs **88,50,24,461.00** received during the years 2024-25 in favour of Ex. Engineer, RWD, Works Div. Danapur Bihar a sum of Rs 87,05,81,358.00 has been utilized for the purpose of **New Maintenance Policy-2018** Schemes as given in the margin for which it was sanctioned and that the balance of Rs. 1,44,43,103.00 remaining unutilized at the end to the period under
Total			**88,50,24,461.00**	

2. Certified that I have satisfied myself that the conditions of which the grants-in-and was Sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following Checks to see that the money was actually utilized for the purpose for which it was sanctioned
Kind of Checks exercised
(lxi) Works have been supervised by Executive Engineer/Superintending Engineer
(lxii) Periodical inspection has been conducted by Executive Engineer/Superintending Engineer
(lxiii) Construction material have been tested
(lxiv) Measurements have been recorded in the MBs and test check conducted by the Assistant
(lxv) All other codal formalities have been observed

3. Physical Progress achieved:
(I) Construction of Road works.
(ii) Construction of CD work.

15/4/24
D.A.O
Rural works Deptt.
Works Division, Danapur

15.04.24
Executive Engineer
Rural works Deptt.
Works Division, Danapur

Scanned with CamScanner

Name of The Road:- NH-30 Baramchari To Jangali Mahadev

Total Length:- 2.0 Km

Package No:- RM/PA/DAN/22/0007

Block:- Maner

Date	Time	Section	Length	Bumps	Speed	OR	IRI	CATEGORY		Latitude	Longitude	Event			
		No.	in km	in mm	Rate	mm/km	mm/km	ROAD					Y = 0 * X ^ 2 + 0.936 * X + 278.4		
13/ 4/ 24	12: 52: 42	67	0.1	290	0	2900	2992	G		25.65599	84.96972	Normal	X = 13636		
13/ 4/ 24	12: 52: 42	67	0.1	300	30.3	3000	3086	G		25.65520	84.96958	Normal	Y = 13041		
13/ 4/ 24	12: 53: 0	67	0.1	360	20.2	3600	3648	G		25.65444	84.96948	Speed Breaker			
13/ 4/ 24	12: 53: 0	67	0.1	310	30.3	3100	3180	G		25.65364	84.96920	Normal			
13/ 4/ 24	12: 53: 18	67	0.1	360	10.1	3600	3648	G		25.65270	84.96894	Curve	(R) RURAL ROAD		
13/ 4/ 24	12: 53: 18	67	0.1	320	20.2	3200	3273	G		25.65230	84.96838	Normal	Good	Average	Poor
13/ 4/ 24	12: 53: 18	67	0.1	340	10.1	3400	3460	G		25.65179	84.96829	Curve	<4000	4001-5000	>5001
13/ 4/ 24	12: 54: 23	67	0.1	300	20.2	3000	3086	G		25.65141	84.96808	Speed Breaker			
13/ 4/ 24	12: 54: 0	67	0.1	330	10.14	3300	3367	G		25.65065	84.96780	Curve			
13/ 4/ 24	12: 44: 0	67	0.1	320	30.3	3200	3273	G		25.65046	84.96921	Normal			
13/ 4/ 24	12: 54: 28	67	0.1	360	20.2	3600	3648	G		25.65052	84.97016	Speed Breaker			
13/ 4/ 24	12: 54: 28	67	0.1	310	10.1	3100	3180	G		25.65126	84.97085	Curve			
13/ 4/ 24	12: 54: 38	67	0.1	290	30.3	2900	2992	G		25.65180	84.97108	Normal			
13/ 4/ 24	12: 54: 52	67	0.1	320	30.3	3200	3273	G		25.65243	84.97098	Normal			
13/ 4/ 24	12: 55: 4	67	0.1	350	20.2	3500	3554	G		25.65324	84.97083	Speed Breaker			
13/ 4/ 24	12: 55: 4	67	0.1	340	30.3	3400	3460	G		25.65385	84.97076	Normal			
13/ 4/ 24	12: 55: 39	67	0.1	300	30.3	3000	3086	G		25.65431	84.96989	Normal			
13/ 4/ 24	12: 55: 39	67	0.1	340	10.1	3400	3460	G		25.65501	84.97122	Curve			
13/ 4/ 24	12: 56: 14	67	0.1	330	20.2	3300	3367	G		25.65548	84.97099	Speed Breaker			
13/ 4/ 24	12: 56: 14	67	0.1	310	30.3	3100	3180	G		25.65431	84.97030	Normal			
TOTAL			**2.00**	**6480**	**414.1**	**64800**	**66213**								
AVERAGE						**3240.00**	**3310.65**								

15.04.24

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दानापुर

Scanned with CamScanner

Steco Analyzer

Name of Customer :	Sanjay Kumar
Name of Work/ Road :	NH-30 Baramchari To Jangali M
Lab Job number	67
Date :	13-04-2024
Section No.	67

Test Date :	13-04-2024	Road Name :	NH-30 Baramchari To Jangali I
Machine No :	474	Road Type :	(R) RURAL ROAD
Start S No :		Side :	
Start E No :			Interval
Weather :		UIV Range :	1992 To 5000 1000 mm/km
Start Location :	NH-30 Baram	Dist Range :	0 To 2.1 0.1 * 1000 m
End Location :	Jangali Mahar	Equation :	Y = 0 * X ^ 2 + 0.936 * X + 278.4

Print | Generate Report and Graph | Redraw Graph | Map View

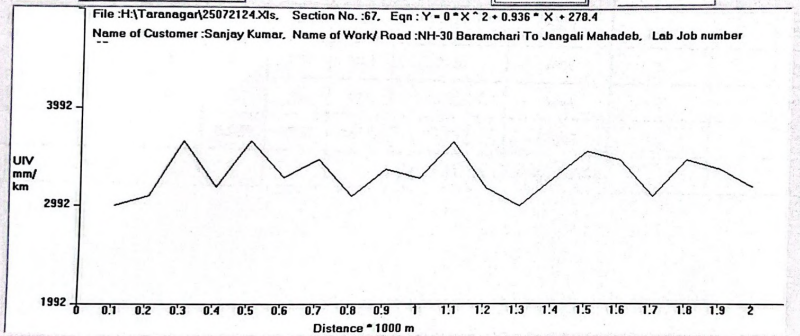

15.04.24
कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दानापुर

Scanned with CamScanner
