# कार्यपालक अभियंता का कार्यालय
# ग्रामीण कार्य विभाग कार्य प्रमंडल,नवगछिया

Email Id-eenavgachhiya@gmail.com

पत्रांक 4038 नवगछिया/ दिनांक 28.12.2024

प्रेशक,

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नवगछिया।

सेवा में,

नोडल पदाधिकारी,
नई अनुरक्षण नीति 2018
ग्रामीण कार्य विभाग,
विश्वेश्वरैया भवन,बेली रोड़,पटना।

विषयः– नई अनुरक्षण नीति 2018 अन्तर्गत पथ में आवंटन उपलब्ध कराने के संबंध में।

महाशय

उपर्युक्त विषय के संबंध में कहना है कि संलग्न विवरणी अनुसार नई अनुरक्षण नीति 2018 के निर्माण कार्य मद में राशि 40.00000/- लाख रूपये का आंबंटन उपलब्ध कराने की कृपा की जाय ताकि संवेदक द्वारा कराये गये निर्माण कार्य का भुगतान किया जा सके।

अनु0– Requisition Format,Form GFR 19-A and IRI Report

विश्वसभाजन

28/12/24

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल नवगछिया।

28/12/2024
JE

28/12/2024

**FORM GFR 19-A**

(See Government of India's Decision (I) below Rule- 150

Form of Utilization Certificate up to the Month November- 2024

Rural Road New Maintenance Policy 2018

PIU – R.W.D. Works Division Navgachhiya

| SL. No. | Name of Scheme | Sanction No. & Date with Amount (in lacs Rs.) | Amount Received (in Lacs Rs.) | Particulars |
|---|---|---|---|---|
| 1. | Construction of Rural Roads under Rural Road New Maintenance Policy 2018 | Letter No C.E-4(HQ) 3054-01-05/2022-Part-V -125 /Patna,Date: 29.11.2024 | 48.99696 | Certified that out of **Rs.9889.36163**Lakhs received upto the Financial years 2024-25 in favour of Ex. Engineer, RWD,Navgachhiya a sum of **Rs.9756.51491** lakhs has been utilized for the purpose of Rural Road New Maintenance Policy 2018 Schemes as given in the margin for which it was sanctioned and that the balance of **Rs.132.84.672** lakhs the end of the period under. |
| | **Total** | | **48.99696** | |

2. Certified that I have satisfied may self that the conditions on which the grants in aid was sanctioned have been duly fulfilled/ are being fulfilled and that I have exercised the following checks to see that the money was actually utilized for the purpose for which it was sanctioned.
   - i. Works have been supervised by Executive Engineer/Superintending Engineer
   - ii Periodical inspection has been conducted by Executive engineer/Superintending Engineer
   - iii Construction materials have been tested.
   - iv Measurements have been recorded in the MBs and test check conducted by the Assistant Engineer / Executive Engineer
   - v. All other codal formalities have been observed.
3. Physical Progress achieved-
   - i. Construction of Road Works
   - ii. Construction of C.D. Works

Shwetha 28/12/24

Executive Engineer
Rural Work Department
Works Division, Navgachhiya

28/12/2024

**Requisition Format for Scheme Head-MR(3054) under Bihar Rural Road Maintenance Policy -2018(Initial Rectification and Surface Renewal)**

**Name of Division:- RWD Works Division Navgachhiya**

| SL No | Package No | Name of Road | Project ID as per MIS | Administrative Approval(AA) Letter No. & Date | Administrative | | Agreement Amount | | Agreement No & Date | Date of Completion as per Agreement | Actual Date of Completion | Value of IRI (in MM/KM) | Thickness of Bitumen Layer (in mm) | Value of Bitumen Content in Percentage | Previous Total Alloted Amount (in Lacs) | up-to date expenditure as per MIS (in Lacs) | Requisition against work done (in Lacs) | Remarks |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | | | | | Length (In Km) | Amount (In Lacs) | Initial Rectification with Surface Renewal(in Lakh) | 5 Year Routine Maintenance in Lakh | | | | | | | | | | |
| 1 | 2 | 3 | 4 | 5 | 6 | 7 | 8 | 9 | 10 | 11 | 12 | 13 | 14 | 15 | 16 | 17 | 18 | 19 |
| 1 | MR-N/2023-24/NAVGACHHIYA/12 | **KHARIK BAZAR GOL CHOWK PCC TO SAHNI TOLA** | | **1086/01.03.2024** | **0.780** | **51.956** | **41.63732** | **5.39505** | 07MBD/2024-25 | **18.04.2025** | **PROGRESS** | **2759.429** | **ONLY PCC** | **NIL** | **0.00000** | **0.00000** | **40.00000** | |
| **Total** | | | | | | | | | | | | | | | | | **40.00000** | |

1. Signed Hard Copy and soft copy(in excel) of recored IRI is enclosed
2. Up-to-date Physical Progress has been uploaded in MIS

Shweta 30/12/24

Executive Engineer
RWD Works Division
Navgachhiya

30/12/24

# कार्यपालक अभियंता का कार्यालय
# ग्रामीण कार्य विभाग कार्य प्रमंडल,नवगछिया

**Email Id-eenavgachhiya@gmail.com**

प्रमाणित किया जाता है कि शीर्ष 3054(MR) नई अनुरक्षण नीति 2018 योजनान्तर्गत **KHARIK BAZAR GOL CHOWK PCC TO SAHNI TOLA**पथ का निर्माण कार्य पूर्ण कर दिया गया है जिसमें कनीय अभियंता द्वारा कार्य के सभी मदों की जॉच शत प्रतिशत की गई एवं सहायक अभियंता के द्वारा 50 प्रतिशत की गई तथा कार्यपालक अभियंता के द्वारा 10 प्रतिशत जॉच की गई जो गुणवत्ता पूर्ण एवं विशिष्टयों के अनुरूप है।

| | | |
|---|---|---|
| 28/12/24 | 28/12/24 | 28/12/24 |
| कनीय अभियंता | सहायक अभियंता | कार्यपालक अभियंता<br>ग्रामीण कार्य विभाग<br>कार्य प्रमंडल नवगछिया |

| Name of Customer: Ravi Shankar Pandey | | | | | | | | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|
| Name of Road : Kharik Bazar Gol Chowk PCC to Sahni Tola | | | | | | | | | | | |
| Date | Time | Section No. | Length in km | Bumps in mm | Speed Rate | OR mm/km | IRI mm/km | CATEGORY ROAD | Latitude | Longitude | Event |
| 9/ 10/ 24 | 10: 42: 0 | 65 | 0.1 | 280 | 0 | 2800 | 2787 | G | 25.36912 | 86.99964 | Normal |
| 9/ 10/ 24 | 10: 42: 10 | 65 | 0.1 | 210 | 30.3 | 2100 | 2109 | G | 25.3665 | 86.99887 | Normal |
| 9/ 10/ 24 | 10: 42: 34 | 65 | 0.1 | 260 | 30.3 | 2600 | 2593 | G | 25.36737 | 86.99897 | Normal |
| 9/ 10/ 24 | 10: 43: 9 | 65 | 0.1 | 380 | 20.2 | 3800 | 3756 | G | 25.36862 | 86.99952 | Normal |
| 9/ 10/ 24 | 10: 43: 19 | 65 | 0.1 | 220 | 30.3 | 2200 | 2206 | G | 25.37011 | 86.99956 | Normal |
| 9/ 10/ 24 | 10: 44: 18 | 65 | 0.1 | 220 | 30.3 | 2200 | 2206 | G | 25.37167 | 86.99992 | Normal |
| 9/ 10/ 24 | 10: 45: 29 | 65 | 0.1 | 370 | 20.2 | 3700 | 3659 | G | 25.37174 | 87.00006 | Normal |
| | | | Total IRI | | | | 19316 | | | | |
| | | | Average IRI | | | | 2759.429 | | | | |

Y = 0 * X ^ 2 + 0.969 * X + 74.60
X = 3700
Y = 3659

(R) RURAL ROAD

| Good | Average | Poor |
|---|---|---|
| <4000 | 4001-5000 | >5001 |

28/12/24
JE

28/12/24

Steco Analyzer

| | |
|---|---|
| Name of Customer : | Ravi Shankar Pandey |
| Name of Work/ Road : | r Gol Chowk PCC to Sahni Tola |
| Lab Job number | 65 |
| Date : | 09-10-2024 |
| Section No. | 65 |

| | | | |
|---|---|---|---|
| Test Date : | 09-10-2024 | Road Name : | r Gol Chowk PCC to Sahni Tola |
| Machine No : | 485 | Road Type : | (R) RURAL ROAD |
| Start S No : | | Side : | |
| Start E No : | | | |
| Weather : | | UIV Range : | 1109 To 5000 Interval 1000 mm/km |
| Start Location : | 9115 86.99964 | Dist Range : | 0 To 0.8 0.1 * 1000 m |
| End Location : | 174 87.000058 | Equation : | Y = 0 * X ^ 2 + 0.969 * X + 74.60 |

Print | Generate Report and Graph | Redraw Graph | Map View

File :E:\bump naugachiya construction\ravishakar pandey\new group\kharik bazar to sahni tola\02031153.Xls,

Name of Customer :Ravi Shankar Pandey. Name of Work/ Road :Kharik Bazar Gol Chowk PCC to Sahni Tola. Lab

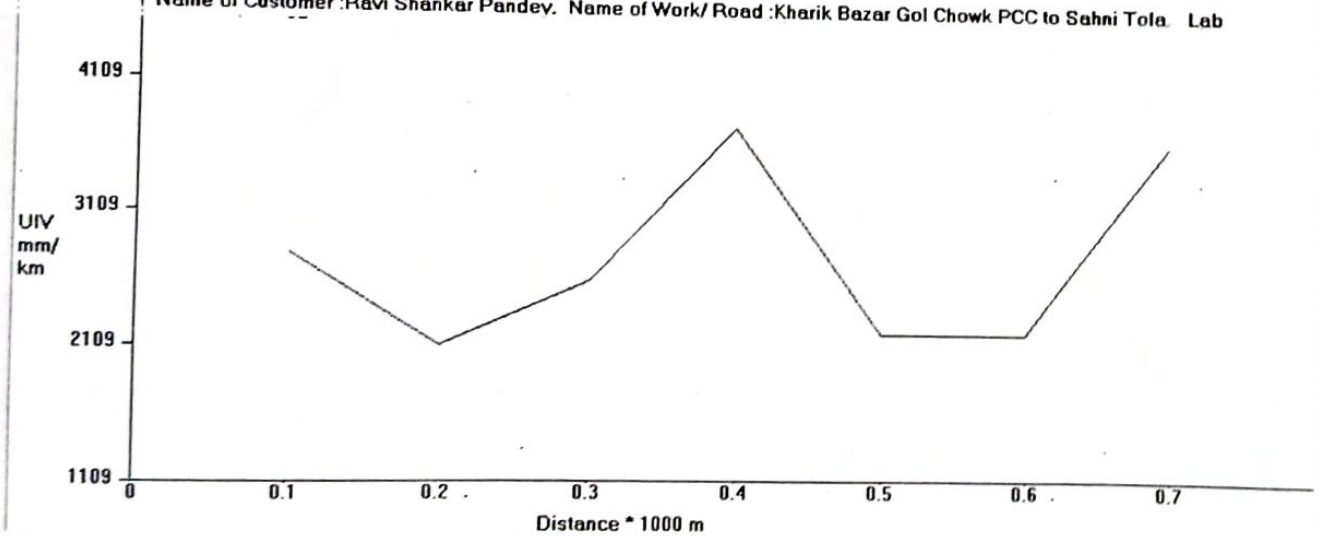


28/12/24
JE

28/12/24
