कार्यपालक अभियंता का कार्यालय
ग्रामीण कार्य विभाग, कार्य प्रमण्डल दरभंगा–2
Mail ID-rwdeedbg2@gmail.com

पत्रांक 506 अन्र दिनांक 10/03/2025

प्रेषक,

ई0 अवधेश कुमार,
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्र0, दरभंगा–2

सेवा में,

सचिव–सह–सशक्त पदाधिकारी,
ब्राडा–सह–अतिरिक्त मुख्य कार्यपालक पदा0,
बिहार, पटना।

विषयः– मुख्यमंत्री ग्रामीण पथ उन्नयन कार्यक्रम (MMGSUY-SC) अन्तर्गत योजना अन्तर्गत राशि की अधियाचना के संबंध में।

महाशय,

उपर्युक्त विषयक के संबंध में कहना है कि शीर्ष मुख्यमंत्री ग्रामीण पथ उन्नयन कार्यक्रम (MMGSUY-SC) योजना अन्तर्गत राशि की मॉग हेतु अधियाचना अंकित मापीपुस्त के अनुसार विहित प्रपत्र में तैयार कर समर्पित की जा रही है।

अतः श्रीमान् से अनुरोध है कि तत्काल मो0 – 506.00 लाख (कुल पॉच करोड़ छः लाख रूपये) मात्र रूपये का आवंटन उपलब्ध कराने की कृपा की जाय, ताकि संवेदकों को भुगतान किया जा सके।

अनु0:–विहित प्रपत्र संलग्न।

विश्वासभाजन
10/3/25
(ई0 अवधेश कुमार)
कार्यपालक अभियंता,
ग्रामीण कार्य विभाग,
कार्य प्रमण्डल, दरभंगा–2
10.3.25

Requisition Format for Scheme MMGSUY (SC)

Name of the Works Division :- RWD Works Division Darbhanga-2

Sl. No.	Package No.	Project ID as per MIS	Name of Road	AA Length (in km.)	Administrative Approval (construction work) Amount (in Lakh)	Agreement (construction work) Amount (in Lakh)	Agreement No. & Date	Date of Completion as per Agreement	Actual Date of Completion	Work Status (WBM/WMM/BM/ SDBC etc.)	Value of IRI (in mm/ km)	Thickness of Bitumen Layer (in mm)	Value of Bitumen Content (in %)	Total Previous Allotted Amount (in Lakh)	Upto date Expenditure as per MIS (in Lakh)	Value of Work Done (in Lakh)	Current Demand (in Lakh)	Remarks
1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19
1	MMGSUY/23-24 Darbhanga-2/04	6190930300002	Rewdha Patel Chowk to Sitamadhi Sima	2.100	327.734	228.22149	16/MBD/24-25 Dt-13.11.2024	12.08.2025	-	Surface Completed	2793.76	25mm	5%	41.00	41.00	194.00	153.00	
2		6190930300003	BASANTI SUMAN CHWOK TO DOGHRA VIA BAJINATHPUR, LATRAHA ATARCWEL	3.170	310.10	209.14045			-	Surface Completed	2972.09	25mm	5%	42.00	42.00	197.00	155.00	
3	MMGSUY/23-24 Darbhanga-2/05	6190930300004	Garry PWD Railway Gumati to Modi Pokhar	1.700	162.839	109.56901	13/MBD/2024-25 Dt-13.11.2024	12.08.2025	-	Surface Completed	2585.5	25mm	5%	22.00	22.00	110.00	88.00	
4		6190930300005	Sitamadhi Sima to Kheshar Tak	2.245	210.18	143.76081			-	Surface Completed	2721.90	25mm	5%	29.00	29.00	139.00	110.00	
															कुल अधियाचित राशि मो0–	506.00		लाख

It is certified that Physical & Financial Progress has been updated in MIS.

10/3/25

D.A.O./D.A.O.
RWD, Works Division Darbhanga-2

10/3/25

Executive Engineer
RWD, Works Division Darbhanga-2

10.3.25

Note :-

1 Above Signed Copy along with Forwading Letter & Utilisation Certificate must be uploaded in MIS.
2 Signed Hard Copy and Soft Copy (in excell) of recorded IRI is enclosed (As Applicable).

GFR 12-B

[See Rule 256 (2)]

FORM OF UTILIZATION CERTIFICATE (MMGSUY-SC)

(1) Certified that out of the Loan of Rs 661.70490 Lakh Sanctioned under MMGSUY (SC) dated....., in favour of Executive Engineer, RWD, Works Division Darbhanga-2 during the year 2024-25 an amount of Rs 594.70490 Lakh has been utilized for the purpose for which it was sanctioned, and that the balance of Rs 67.00 Lakh remaining unutilized at the end of the year 2024-25 has been surrendered to the Government (vide No....., dated.....)/ will be adjusted towards the loan payable during the next financial year.

(2) Certified that I have satisfied myself that the conditions on which the loan was sanctioned have been duly fulfilled/are being fulfilled and that I have exercised the following checks to see that the money was actually spent for the purpose for which the loan was made.

Kinds of checks exercised

1. Works haves been supervised by Executive Engineer/ Superintending Engineer
2. Periodical inspection has been conducted by Executive Engineer/ Superintending Engineer.
3. Constructions materials have tested.
4. Measurements have been recorded in the MBs and test check conduction by the Assistant Engineer/ Executive Engineer
5. All other codal formalities have been observed.

10/03/25

Divisional Account Officer
RWD Works Div. Darbhanga-2

10/3/25

Executive Engineer
RWD Works Div. Darbhanga-2

10.3.25

Name OF Road- Const. of Work From basant Suman Chowk To Doghra Via Bajinathpur latraha Atarwel in Jale Block

Date	Time	Section No.	Length in km	Bumps in mm	Speed Rate	OR mm/km	IRI mm/km	TEGORY ROAD		Latitude	Longitude	Event
7/ 3/ 25	10: 37: 35	27	0.1	380	0	3800	3716	G		26.359433	85.72243	Normal
7/ 3/ 25	10: 38: 0	27	0.1	320	20.2	3200	3220	G		26.359573	85.7223	Normal
7/ 3/ 25	10: 38: 11	27	0.1	290	20.2	2900	2972	G		26.362687	85.71983	Normal
7/ 3/ 25	10: 38: 11	27	0.1	260	20.2	2600	2724	G		26.31998	85.72003	Normal
7/ 3/ 25	10: 38: 46	27	0.1	300	10.1	3000	3055	G		26.361481	85.72032	Normal
7/ 3/ 25	10: 39: 0	27	0.1	340	20.2	3400	3386	G		26.36042	85.72124	Normal
7/ 3/ 25	10: 39: 0	27	0.1	300	10.1	3000	3055	G		26.363605	85.71957	Normal
7/ 3/ 25	10: 39: 21	27	0.1	170	10.1	1700	1980	G		26.364569	85.71968	Normal
7/ 3/ 25	10: 40: 0	27	0.1	320	10.1	3200	3220	G		26.365589	85.72006	Normal
7/ 3/ 25	10: 40: 0	27	0.1	250	20.2	2500	2641	G		26.366508	85.72003	Normal
7/ 3/ 25	10: 40: 0	27	0.1	240	30.3	2400	2559	G		26.36996	85.71622	Normal
7/ 3/ 25	10: 40: 32	27	0.1	250	20.2	2500	2641	G		26.369491	85.71695	Normal
7/ 3/ 25	10: 40: 32	27	0.1	260	20.2	2600	2724	G		26.368988	85.71771	Normal
7/ 3/ 25	10: 41: 7	27	0.1	280	20.2	2800	2889	G		26.36763	85.71962	Normal
7/ 3/ 25	10: 41: 7	27	0.1	300	10.1	3000	3055	G		26.370618	85.71512	Normal
7/ 3/ 25	10: 41: 42	27	0.1	240	20.2	2400	2559	G		26.37168	85.71419	Normal
7/ 3/ 25	10: 42: 0	27	0.1	260	20.2	2600	2724	G		26.373005	85.71267	Normal
7/ 3/ 25	10: 42: 18	27	0.1	240	10.1	2400	2559	G		26.373627	85.71183	Normal
7/ 3/ 25	10: 42: 18	27	0.1	270	30.3	2700	2807	G		26.376687	85.70824	Normal
7/ 3/ 25	10: 43: 0	27	0.1	260	20.2	2600	2724	G		26.3756	85.70867	Normal
7/ 3/ 25	10: 43: 0	27	0.1	280	20.2	2800	2889	G		26.374815	85.70888	Normal
7/ 3/ 25	10: 43: 28	27	0.1	290	20.2	2900	2972	G		26.374301	85.71032	Normal
7/ 3/ 25	10: 43: 28	27	0.1	340	20.2	3400	3386	G		26.377263	85.70759	Normal
7/ 3/ 25	10: 44: 1	27	0.1	280	20.2	2800	2889	G		26.377944	85.70557	Normal
7/ 3/ 25	10: 44: 1	27	0.1	360	10.1	3600	3551	G		26.377833	85.70597	Normal
7/ 3/ 25	10: 44: 37	27	0.1	290	20.2	2900	2972	G		26.377608	85.70666	Normal
7/ 3/ 25	10: 44: 37	27	0.1	360	20.2	3600	3551	G		26.378063	85.70498	Normal
7/ 3/ 25	10: 45: 12	27	0.1	350	10.1	3500	3468	G		26.378282	85.70441	Normal
7/ 3/ 25	10: 45: 12	27	0.1	290	20.2	2900	2972	G		26.378282	85.70441	Normal
7/ 3/ 25	10: 46: 1	27	0.1	340	20.2	3400	3386	G		26.378237	85.70453	Normal
7/ 3/ 25	10: 46: 1	27	0.1	280	20.2	2800	2889	G		26.378073	85.70501	Normal
7/ 3/ 25	10: 46: 47	27	0.075	290	10.1	2900	2972	G		26.195546	85.7447	Normal
					Average IRI		2972.09					

Y = 0 * X ^ 2 + 0.827 * X + 574.3
X = 2900
Y = 2972

(R) RURAL ROAD

Good	Average	Poor
<4000	4001-5000	>5001

Atarwel 7/3/25 JE

Nitish 7/3/25 A.E.

10/3/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दरभंगा- 2

Steco Analyzer

Name of Customer : Satish Kumar Thakur

Name of Work/ Road : Const of Work From Basant Sur

Lab Job number : 27

Date : 07-03-2025

Section No. : 27

Test Date : 07-03-2025 | Road Name : Jaymathpur Ishreha asarwel jala

Machine No : 477 | Road Type : (R) RURAL ROAD

Start S No : | Side :

Start E No : | Interval

Weather : | UIV Range : 960 To 5000 1000 mm/km

Start Location : | Dist Range : 0 To 33 01 * 1000 m

End Location : | Equation : Y = 0 * X ^ 2 + 0.027 * X + 574.3

Print | Generate Report and Graph | Redraw Graph | Map View

File :D:\STECO-USB-GPS V1_1_3\07031420 BasantXls. Section No. :27. Eqn : Y = 0 * X ^ 2 + 0.027 * X + 574.3

Name of Customer :Satish Kumar Thakur. Name of Work/ Road :Const of Work From Basant Suman Chowk To Doghr

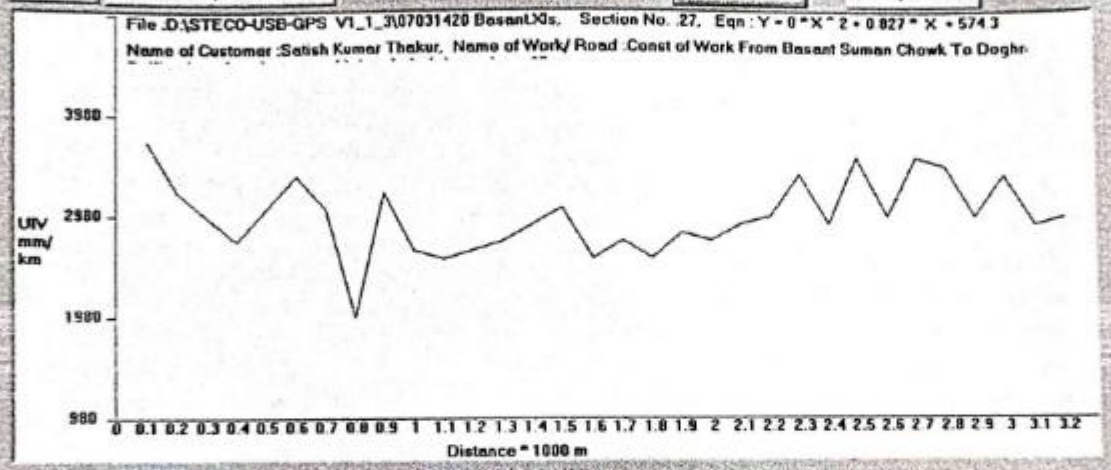

7/3/25

07/3/25

7/3/25

10/3/25

कार्यपालक अभियंता
ग्रामीण कार्य विभाग
कार्य प्रमंडल, दरभंगा-
